PREPARED FOR	COMPANY	DATE

LEASE	WELL No.	FIELD	CO./PARISH	STATE	☐ NEW COMPLETION ☐ WORKOVER

INSTALLATION

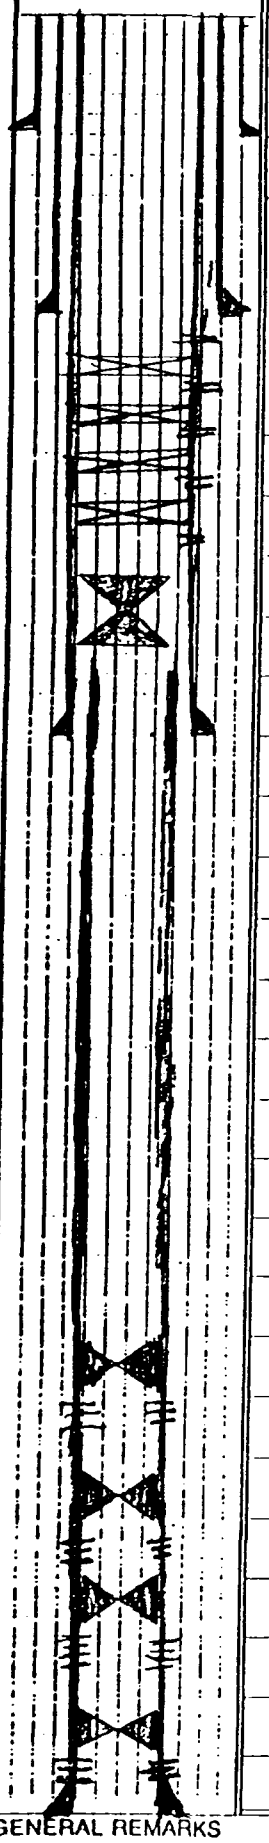

ITEM	LENGTH	FROM	TO	DESCRIPTION	OD	ID
				13 3/8", 54.50#, J-55 @ 343'		
	343'	0	343'	Cement w/ 325 sx. Circ - 25 sx.		
				10 3/4" 45.5 + 51.50# K55 @ 2873'		
	2873'	0	2873'	Cement w/ 2000 sx. Circ - 198 sx		
		5080'	5090'	Delaware Perfs CIBP @ 6400		
		6437'	6474'	Perfs - CIBP @ 6510'		
		6523'	6564'	Perfs - CIBP @ 6580'		
		6590'	6604'	Perfs - CIBP @ 6690'		
		6701'	6936'	BS Perfs - Frac 4		
				CIBP @ 10,100'		
	10,848	0	10,848'	7 5/8", 29.7#, HSC. @ 10,848		
				Cem w/ 1450 sx, DV @ 6784 TOC @ 2500'		
	3352'	10,343'	13,695'	5" 18# Liner w/ 375 sx		
				CIBP @ 11,800'		
		11,980'	12,722'	Atoka Perfs		
				CIBP @ 12,850		
		12,888	12,968	Morrow Perfs		
				CIBP @ 13000'		
		13,107	13,258'	Morrow Perfs AOF - 4105 mcf/d		
			13,400'	Cement Retainer		
		13,529'	13,586'	Morrow Perfs - Squeeze w/ 60 sx		

GENERAL REMARKS	PACKER TYPE	RETRIEVING METHOD Include shear release or collet snap value
	top	
COMP. FLUID TYPE AND WEIGHT / ESTIMATED BHT / ESTIMATED BHP	middle	
MAX. ANGLE AND KICKOFF DEPTH (ft) / SAND CONTROL	lower	
DATE / OPERATOR'S NAME / AREA		DELIVERY TICKET No.

Order Code: 5310

PRAIRIE SUN. INC.
BEFORE EXAMINER ASHLEY
NMOCD CASE NO. 12236
DATE: 09/02/99
EXHIBIT NO. 6
