DATE	TIME	CUM. HRS.	/MIN	P.S.I.G. @ 10,500 FEET
8-31-73	11:10 A.M.	00 HRS.	00 MIN.	2871 GUAGE REACHED 10,500 '
9-1-73	9:35 A.M.	22	25	2875 CHOKE OPENED
	9:50 A.M.	22	40	2737 CHOKE CLOSED TO REPAIR REG.
	12:00 P.M.	24	50	2862 CHOKE OPEN RATE 1 @ 6/64 CHOKE
		25	05	2648
		25	20	2483
		25	35	2278
		25	50	2196
		26	05	2114
		26	20	2070
		26	35	2021
	2:00 P.M.	26	50	1980 END RATE 1
		27	05	1758 RATE 2 @ 9/64 CHOKE
		27	20	1615
		27	35	1515
	3:00 P.M.	27	50	1463 END RATE 2
		28	05	1344 RATE 3 @ 11/64 CHOKE
		28	20	1283
		28	35	1254
	4:00 P.M.	28	50	1237 END RATE 3
		29	05	1130 RATE 4 @ 14/64 CHOKE
		29	20	1006
		29	35	965
	5:00 P.M.	29	50	952 END RATE 4 GUAGE OUT END TEST

HORIZON OIL & GAS CO
STATE 28 NO. 2

TEST DATE: 8-31/9-1,1973
TEST DEPTH: 10,500FEET

ELEMENT NO.: 4391 (0-3700#)
CLOCK NO.: 5124 (0-72HRS.)

GUAGE NO.: 16163
OPERATOR: D. TYSON

RECEIVED
SEP 10 1973
HORIZON OIL & GAS CO.
SPEARMAN, TEXAS

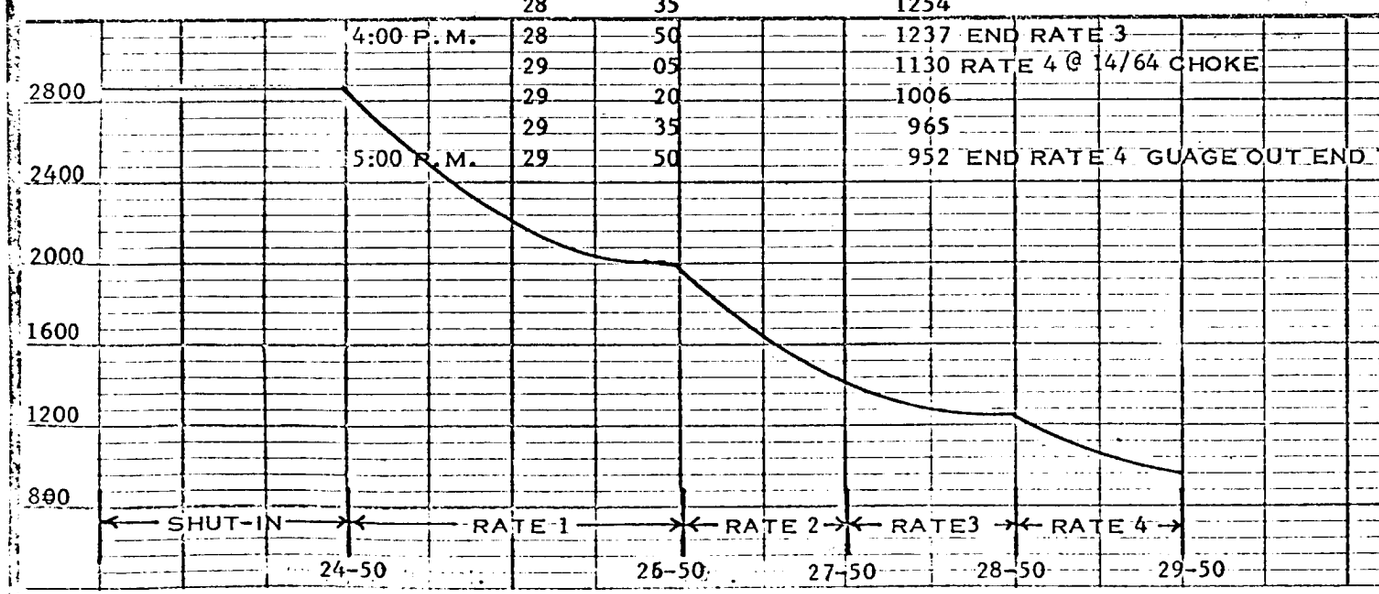

HORIZON OIL AND GAS COMPANY

STATE 28 WELL NO. 2

FOUR POINT BACK PRESSURE TEST

JOHN W. WEST ENGINEERING CO. HOBBS, NEW MEXICO

Date: 9-5-73 Drawn by: DAT Scale: AS SHOWN
