DEVON ENERGY CORPORATION
WELLBORE SCHEMATIC

WELL NAME: TURNER "B" #90	FIELD: GRAYBURG-JACKSON	
LOCATION: 75'FNL & 2610'FWL, SEC 29-T17S-R31E	COUNTY: EDDY	STATE: NM
ELEVATION: GL=3689'; KB=3700'	SPUD DATE: 01/11/91	COMP DATE: 03/19/91
API#: 30-015-26606 PREPARED BY: C.H. CARLETON		DATE: 09/16/97

	DEPTH	SIZE	WEIGHT	GRADE	THREAD	HOLE SIZE
CASING:	0' - 606'	8 5/8"	24#	J-55	ST&C	12 1/4"
CASING:	0' - 3603'	5 1/2"	17#	J-55	LT&C	7 7/8"
CASING:						
TUBING:						
TUBING:						
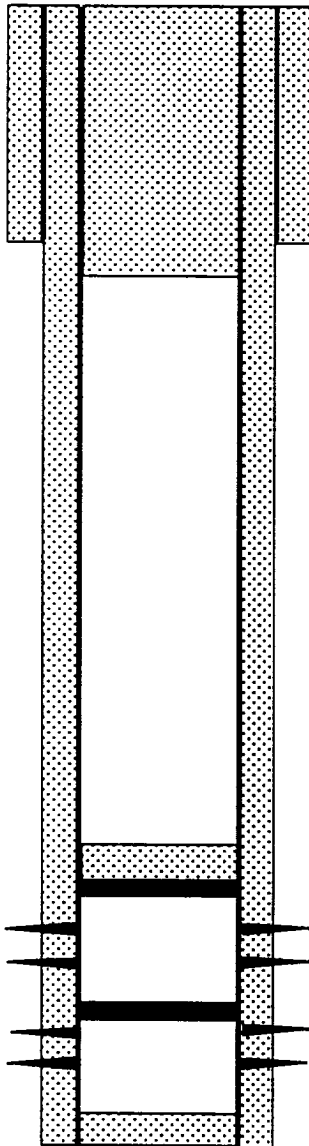
■ CURRENT ☐ PROPOSED

OPERATOR: DEVON ENERGY CORPORATION(NEVADA)
PLUGGED & ABANDONED: 10/15/97

CEMENT PLUG: 0'- 654' WITH 180 SXS CEMENT
8 5/8" CASING @ 606' W/465 SXS. TOC @ SURFACE

NOTE: 9.5ppg MUD SPOTTED BETWEEN CEMENT PLUGS

DETAIL OF PERFORATIONS
M.GRAYBURG: 3002', 04', 06', 08', 11', 14'
LOCO HILLS: 3031', 32', 35', 36', 65', 68'
METEX: 3075', 79', 80', 81', 82', 85', 86'
L.GRAYBURG: 3181', 82', 83'
PREMIER: 3194', 96', 98', 3200', 02', 04', 05', 19', 21', 84', 85', 89', 90', 91'

CIBP @ 2835', CAPPED WITH 5 SXS CEMENT(+50')

PERFORATIONS: 3002'- 3086'(OA) - 19 HOLES

CIBP @ 3155'
PERFORATIONS: 3181'- 3291'(OA) - 17 HOLES

PBTD @ 3558'
5 1/2" CASING @ 3603' W/1620 SXS. TOC @ SURFACE
TD @ 3606'

NOTE: FOR CALCULATED CEMENT TOPS A YIELD OF 1.32 CU FT/SX AND 50% FILLUP WERE ASSUMED.
