BURLINGTON RESOURCES

CORRAL DRAW 9 FEDERAL NO. 1
CORRAL DRAW (WOLFCAMP) FIELD
T25S, R29E, Section 9
660' FNL and 1650' FEL
Eddy County, New Mexico
Current Completion

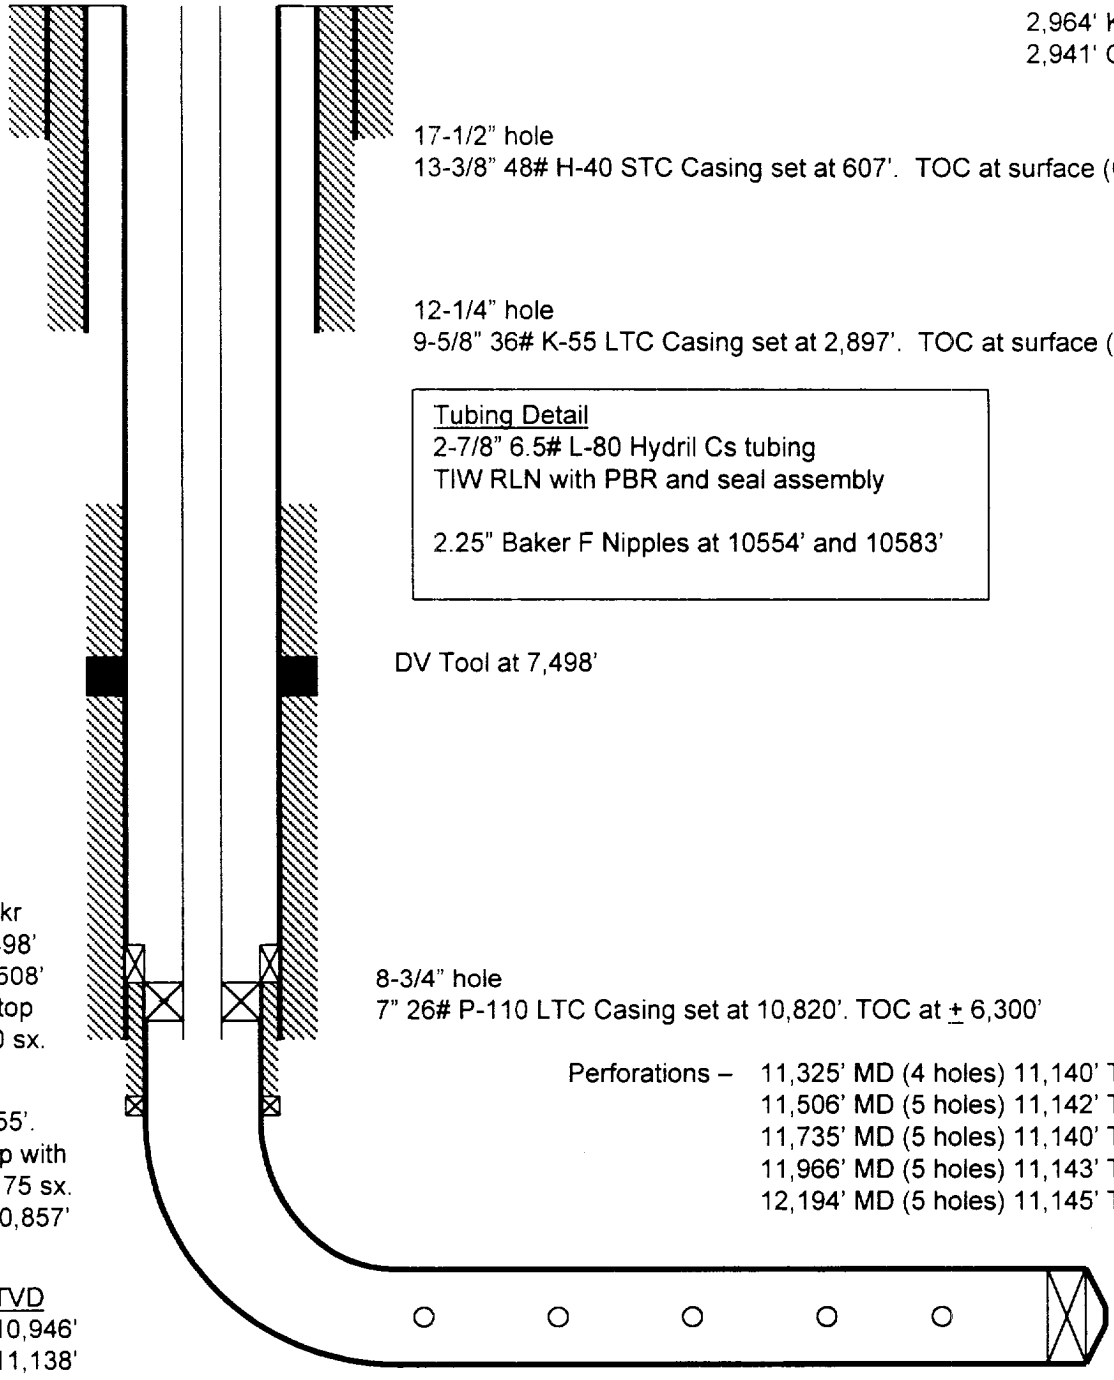

ERC 10,000 psig Wellhead

2,964' KB
2,941' GL

17-1/2" hole
13-3/8" 48# H-40 STC Casing set at 607'. TOC at surface (Circ).

12-1/4" hole
9-5/8" 36# K-55 LTC Casing set at 2,897'. TOC at surface (Circ).

Tubing Detail
2-7/8" 6.5# L-80 Hydril Cs tubing
TIW RLN with PBR and seal assembly

2.25" Baker F Nipples at 10554' and 10583'

DV Tool at 7,498'

TIW Liner top pkr at 10,498'
Liner top at 10,508'
Squeeze Liner top with 150 sx.

8-3/4" hole
7" 26# P-110 LTC Casing set at 10,820'. TOC at ± 6,300'

Perforations – 11,325' MD (4 holes) 11,140' TVD
11,506' MD (5 holes) 11,142' TVD
11,735' MD (5 holes) 11,140' TVD
11,966' MD (5 holes) 11,143' TVD
12,194' MD (5 holes) 11,145' TVD

DV tool at 10,855'.
Cement liner top with 75 sx.
Davis ECP at 10,857'

LATERAL

	MD	TVD
KOP	10,946'	10,946'
EOB	11,273'	11,138'
TD	12,236'	11,145'
AZ	124 degrees	

6-1/8" hole.
4-1/2" 15.1# P-110 HDL Liner set at 10,508' to 12,236'.
Baker CIBP at 12,235'.
