San Juan - San Juan South BP FLORANCE H3

Country:	UNITED STATES	County:	SAN JUAN	Event:	WORKOVER	Wellbore:	01
Region:	NORTH AMERICA	State:	NEW MEXICO	Event Start:	11/14/2007	Top TMD:	2,905.0 ft
Bus. Unit:	NAG SPU	District:	FARMINGTON	Event End:	12/14/2007	Bottom TMD:	3,013.0 ft
Perf Unit:	SAN JUAN			Objective:	DEEPEN WELLBORE	Spud:	6/22/1989
Asset:	SAN JUAN SOUTH			Contractor:	AZTEC WELL SERVICING		
Field:	BASIN-FRUITLAND COAL GAS POOL						

Orig KB Elev:	0.00 ft
Ground Elev:	0.00 ft
KB to GL:	0.0 ft
Mud Line Elev:	0.00 ft

API: 30-045-27330

Tubing/CT/SS Components	Min ID	Top
1 - ROD, POLISHED: 1.25 X 16 FT		5.0 ft
1 - TUBING HANGER, 2.375	1.995 in	12.0 ft
94 - TUBING, 2.375, 4.7#, J-55, EUE	1.995 in	12.9 ft
1 - RODS: 0.75 X 25 GRD. D		21.0 ft
3 - RODS, PONY: 0.75 GRD. D		46.0 ft
113 - RODS: 0.75 X 25 GRD. D		68.0 ft
3 - RODS, SINKER: 1.25 GRD.D		2,893.0 ft
1 - PUMP, RHAC, 2.0 X 1.25 X 11		2,968.0 ft
1 - NIPPLE, PROFILE, "F", 2.375 OD, 1.780 ID	1.780 in	2,971.1 ft
1 - MULE SHOE, 2.375	2.041 in	2,972.1 ft

Wellsketch

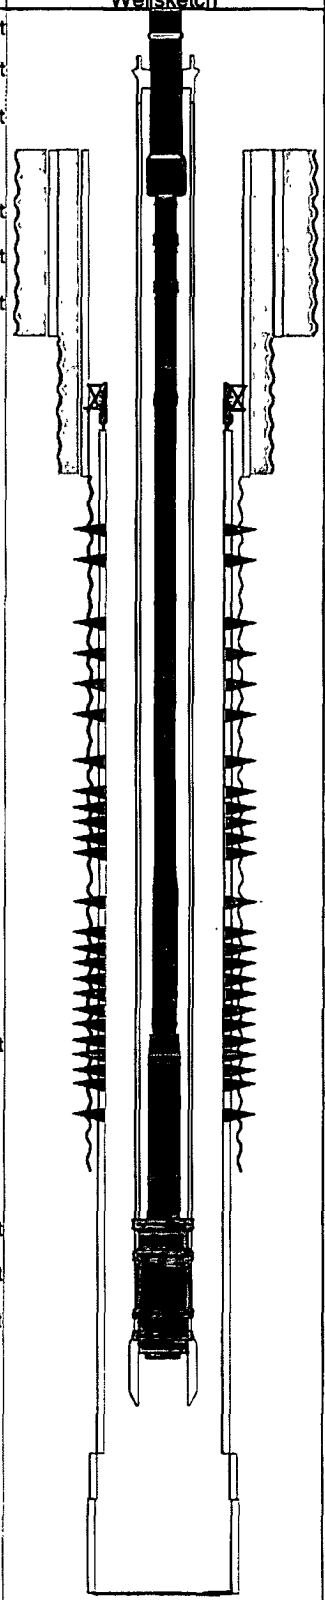

Perf Interval / SPF / Phasing

Baker 7"x5½" SLPR liner hanger @ 2666'

2,732.0 ft - 2,744.0 ft - 4 /ft - 90.0 °

2,752.0 ft - 2,766.0 ft - 4 /ft - 90.0 °

2,802.0 ft - 2,820.0 ft - 4 /ft - 90.0 °

2,805.0 ft - 2,820.0 ft - 4 /ft - 90.0 °

2,868.0 ft - 2,885.0 ft - 4 /ft - 90.0 °

2,882.0 ft - 2,897.0 ft - 4 /ft - 90.0 °

2,885.0 ft - 2,902.0 ft - 4 /ft - 90.0 °

5½" 15.5# K-55, 511 Hyd Bit sub & 6⅛" bit on bottom @ 3012'
