BURLINGTON RESOURCES API # 30-045-34741

ConocoPhillips

Schematic - Current

HUERFANO UNIT #314

Most Recent Job

Job Category	Primary Job Type	Secondary Job Type	Actual Start Date	End Date
COMPLETIONS	INITIAL COMPLETION	INITIAL COMPLETION	1/5/2009	2/2/2009

Well Config: VERTICAL - Original Hole, 2/9/2009 6:38:40 AM

ftKB (MD)

Schematic - Actual

Schematic - Proposed

30-045-34741

0
16
17
18
48
52
58
67
98
264
298
324
337
338
340
342
343
2,403
2,414
3,250
6,042
6,196
6,199
6,287
6,290
6,305
6,315
6,426
6,460
6,462
6,492
6,493
6,494
6,665
6,666
6,670
6,674
6,678
6,679
6,682
6,703
6,704
6,713
6,714

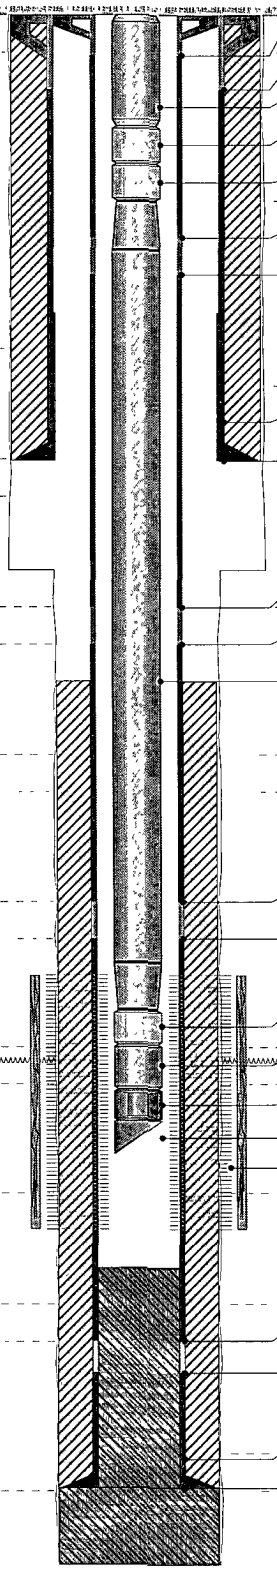

2-1, Casing Hanger, 4 1/2, 4.000, 16, 0.8
1-1, Casing Hanger, 8 5/8, 8.097, 16, 1.9
1-1, Tubing, 2 3/8, 1.995, 16, 31.4
1-2, Tubing Pup Joint, 2 3/8, 1.995, 47, 4.1
1-3, Tubing Pup Joint, 2 3/8, 1.995, 52, 6.1
2-2, Casing Joints, 4 1/2, 4.000, 17, 50.2
2-3, Casing Pup Joint, 4 1/2, 4.000, 67, 30.7
1-2, Casing Joints, 8 5/8, 8.097, 18, 319.3
1-3, Sawtooth Collar, 8 5/8, 8.097, 337, 0.8
2-4, Casing Joints, 4 1/2, 4.000, 98, 2,305.6
2-5, Marker Joint, 4 1/2, 4.000, 2,403, 10.5
1-4, Tubing, 2 3/8, 1.995, 58, 6,402.2
2-6, Casing Joints, 4 1/2, 4.000, 2,414, 3,891.4
2-7, Marker Joint, 4 1/2, 4.000, 6,305, 10.3
1-5, Tubing Pup Joint, 2 3/8, 1.995, 6,460, 2.0
1-6, Tubing, 2 3/8, 1.995, 6,462, 30.8
1-7, F-NIPPLE, 2 3/8, 1.780, 6,493, 0.9
1-8, Mule Shoe, 2 3/8, 6,493, 0.9
Perforated, 6,426-6,666, 1/15/2009
2-8, Casing Joints, 4 1/2, 4.000, 6,315, 362.6
2-9, Float Collar, 4 1/2, 4.000, 6,678, 0.7
2-10, Casing Joints, 4 1/2, 4.000, 6,679, 24.5
2-11, Float Shoe, 4 1/2, 4.000, 6,703, 0.8

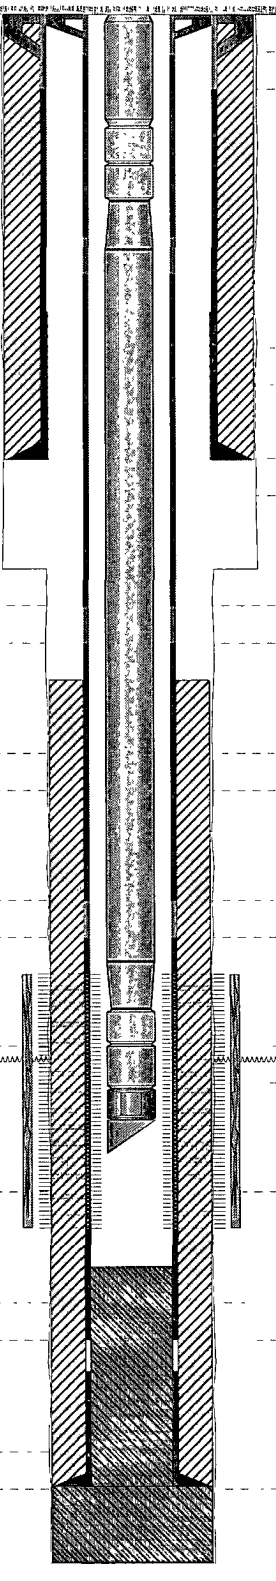

RCVD FEB 12 '09
OIL CONS. DIV.
DIST. 3

Report Printed: 2/9/2009
