MOUNTAIN FUEL SUPPLY COMPANY

3000 psi BLOWOUT PREVENTION EQUIPMENT

CHECKLIST 3000psi EQUIPMENT

Well _____ _____ Casing

Contractor and operator to furnish items checked (x)

No.	STANDARD STACK REQUIREMENTS Item	Nominal	ID	Type	Furn. by Oper.	Contr.
1	Drilling Nipple					
2	Flowline					
3	Fill up Line	2"				
4	Annular Preventor			Spherical Shaffer Hydrilor Rockfiler		
5	Two single or one dual Hyd. oper. ram			G. ram F. Ram		
6	Drilling Spool with 2" and 3" outlets			Forged		
7	(x Alternate to (6) Run and Kill lines from outlets in this ram.					
8	Valve Gate		3 1/8			
9	Valve-Hydraulically Operated Gate		3 1/8			
10	Choke Line		2.9			
11	Gate Valves		1 1/16			
12	Check Valve		1 1/16			
13	Kill line	2"				
14	Valves-Gate		2 1/16			
14	Kill line to Pumps	2"				
16	Casing Head					
17	Valves Gate___ Plug___		1 3/8			
18	Compound Pressure Gauge					
	Wear Bushing					

SPECIAL CHOKE AND KILL REQUIREMENTS					

SPECIAL STACK REQUIREMENTS					

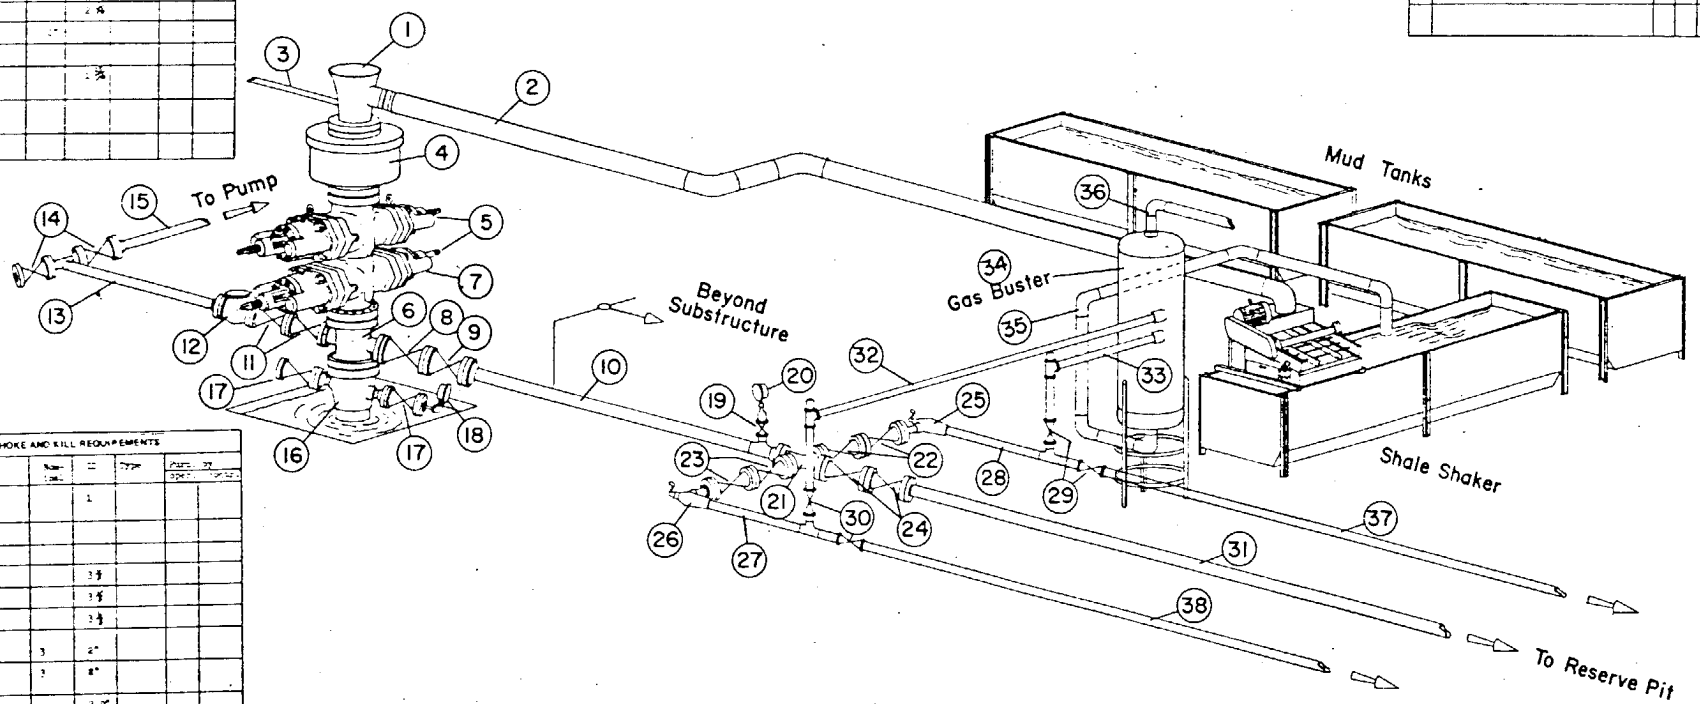

No.	STANDARD CHOKE AND KILL REQUIREMENTS Item	Nominal	ID	Type	Furn. by Oper.	Contr.
19	Valve Gate___ Plug___		1			
20	Compound Pressure					
21	Cross 3"X3					
22	Valve Gate		3 1/8			
23	Valve Gate		3 1/8			
24	Valve Gate		3 1/8			
25	Choke Dam N-2 or equivelent	3	2"			
26	Choke Dam N-2 or Equillivent	3	2"			
27	Line to Seperator		2.9"			
28	Line to Seperator		2.9"			
29	Valve Gate		3 1/8			
30	Valves Gate		3 1/8			
31	Line to Res. Pit		2.9"			
32	Line to Seperator		2.9"			
33	Line to Seperator		2.9"			
34	Seperator					
35	Discharge Line					
36	Vent Line					
37	Line to Res.		2.9"			
38	Line to Res. Pit		2.9"			
