30-025-43841

Wellbore Diagram : NHSAU 657-24

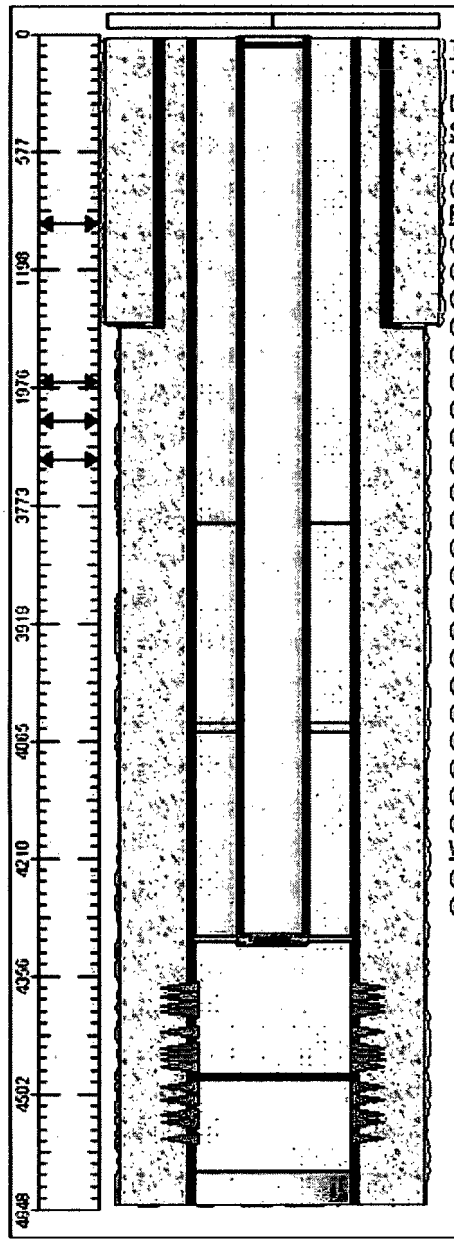

Tubing String Quantity (Top-Bottom Depth) Desc
1 @(4305-4313) Packer Mandrel 7.000"-7" X 2 7/8" X 17-26# ARROWSET 1-X DOUBLE GRIP PKR - Rebuilt-
Surface Casing (Top-Bottom Depth) Desc
@(1481-1523) J-55 9.625 OD/ 36.00# Round Long 8.921 ID 8.764 Drift-
@(18-1525) Cement (behind Casing)-
Production Casing (Top-Bottom Depth) Desc
@(18-3793) L-80 7.000 OD/ 26.00# Round Long 6.276 ID 6.151 Drift-
@(3793-3795) Cement Stage Tool-
@(4364-4370) Perforations-Open
@(4374-4380) Perforations-Open
@(4386-4392) Perforations-Open
@(4394-4402) Perforations-Open
@(4418-4423) Perforations-Open
@(4439-4442) Perforations-Open
@(4446-4448) Perforations-Open
@(4452-4456) Perforations-Open
@(4462-4469) Perforations-Open
@(4477-4482) Plug - Cement on Top of Bridge Plug-
@(4482-4486) Bridge Plug Cast Iron 7.000" - New-
@(4487-4492) Perforations-Isolated
@(4502-4510) Perforations-Isolated
@(4520-4524) Perforations-Isolated
@(4530-4534) Perforations-Isolated
@(4364-4556) Producing Interval (Completion)-
@(4550-4556) Perforations-Isolated
@(4599-4600) Float Collar Nominal - 7.000" OD- 7.650" Drillout ID- 6.351"-
@(4600-4642) L-80 7.000 OD/ 26.00# Round Long 6.276 ID 6.151 Drift-
@(18-4644) Cement (behind Casing)-
Wellbore Notes (Top-Bottom Depth) Desc
@(4644-4644) Total Depth-
@(4477-4644) Plug Back Total Depth-

HOBBS OCD
JUL 02 2018
RECEIVED
