Form C-103

OIL CONSERVATION COMMISSION

SANTA FE, NEW MEXICO

Miscellaneous Reports on Wells

Submit this report in triplicate to the Oil Conservation Commission or its proper agent within ten days after the work specified is completed. It should be signed and sworn to before a notary public for reports on beginning drilling operations, results of shooting well, results of test of casing shut off, result of plugging of well, and other important operations, even though the work was witnessed by an agent of the Commission. Reports on minor operations need not be signed and sworn to before a notary public. See additional instructions in the Rules and Regulations of the Commission.

Indicate nature of report by checking below.

REPORT ON BEGINNING DRILLING OPERATIONS		REPORT ON REPAIRING WELL	
REPORT ON RESULT OF SHOOTING OR CHEMICAL TREATMENT OF WELL		REPORT ON PULLING OR OTHERWISE ALTERING CASING	
REPORT ON RESULT OF TEST OF CASING SHUT-OFF		REPORT ON DEEPENING WELL	
REPORT ON RESULT OF PLUGGING OF WELL		REPORT ON SETTING CASING	X

January 8, 1951 (Date) Monument, New Mexico (Place)

OIL CONSERVATION COMMISSION,
SANTA FE, NEW MEXICO.
Gentlemen:

Following is a report on the work done and the results obtained under the heading noted above at the Amerada Petroleum Corporation (Company or Operator) State S "B" (Lease) Well No. 2 in the C/NE/4 NW/4 of Sec. 3, T. 15-S, R. 33-E, N. M. P. M., Saunders Field Lea County.

The dates of this work were as follows: January 6, 1951

Notice of intention to do the work was ~~XXXXXXX~~ submitted on Form C-102 on January 6, 1951 and approval of the proposed plan was ~~XXXXXXX~~ obtained. (Cross out incorrect words.)

DETAILED ACCOUNT OF WORK DONE AND RESULTS OBTAINED

3100' - Total Depth - Anhydrite. Ran 37 Joints of 7-5/8" O.D., 26.40#, 8-Rd. Thd., Grade J-55, Range 3, S.S. New Casing; 6 Joints same described casing - SH; and 35 Joints of 7-5/8" O.D. 26.40#, 8-Rd. Thd., Grade H-40, S.S. New Casing; set at 3100' and cemented with 1000 sacks of Regular cement of which 500 sacks were mixed with 3% Jell. Plug to 3014' at 1:40 A.M., 1-7-51. Maximum pump pressure 1300#. Ran 2 - 7-5/8" O.D. Weatherford Centralizers at 3075' & 3055' and 4 - 7-5/8" O.D. Weatherford Wall Scratchers 10' apart in above section.

Witnessed by C. E. Telge (Name) Amerada Petroleum Corporation (Company) Farm Boss (Title)

Subscribed and sworn before me this 8th day of January, 1951

W. P. Mohr
Notary Public

My commission expires 10-11-54

I hereby swear or affirm that the information given above is true and correct.

Name [signature]

Position Assistant District Superintendent

Representing Amerada Petroleum Corporation (Company or Operator)

Address Drawer D, Monument, New Mexico

Remarks: APPROVED JAN 10 1951 Date

[signature] Name
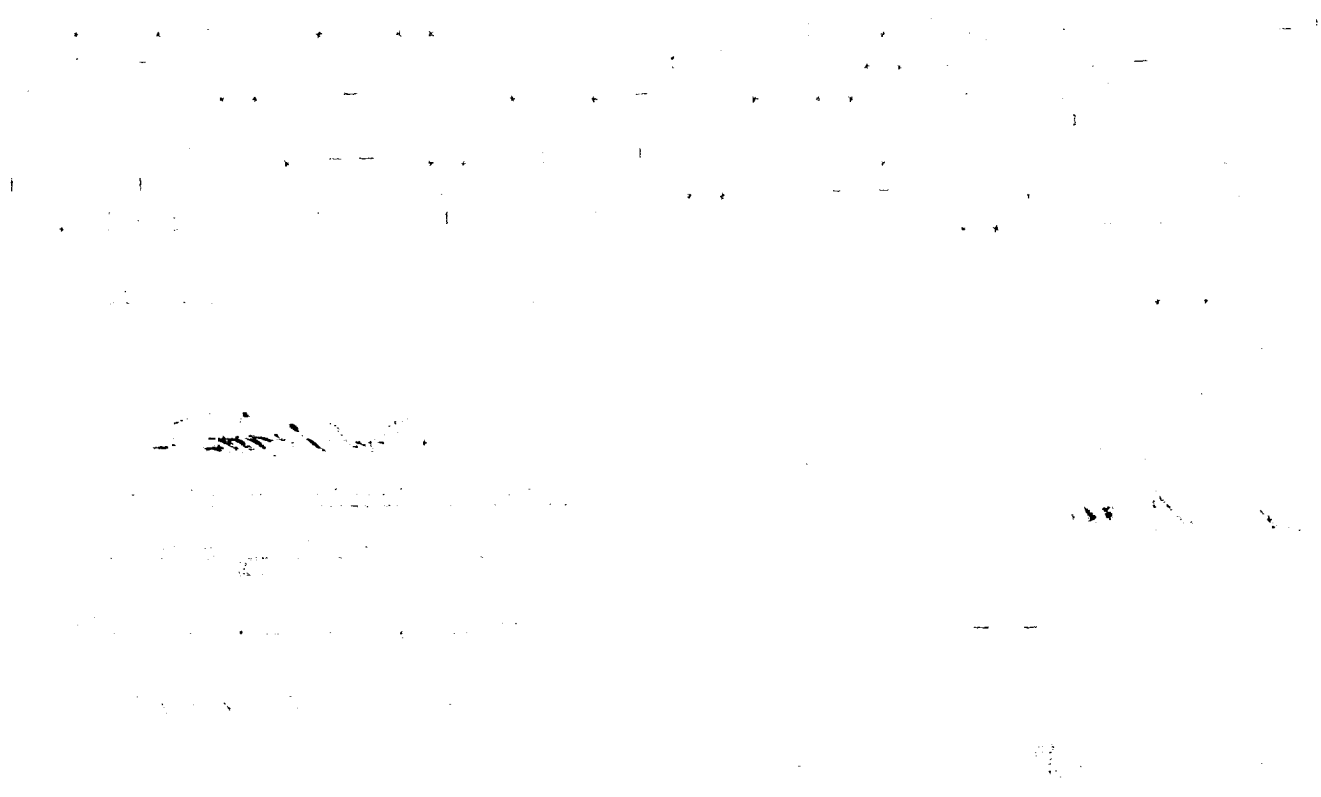
Title
