FIELD VACUUM GLORIETA	OPERATOR MARATHON OIL COMPANY		DATE 6/29/76
LEASE McCALLISTER STATE	WELL NO. 6	LOCATION Sec.25-T17S-R34E	

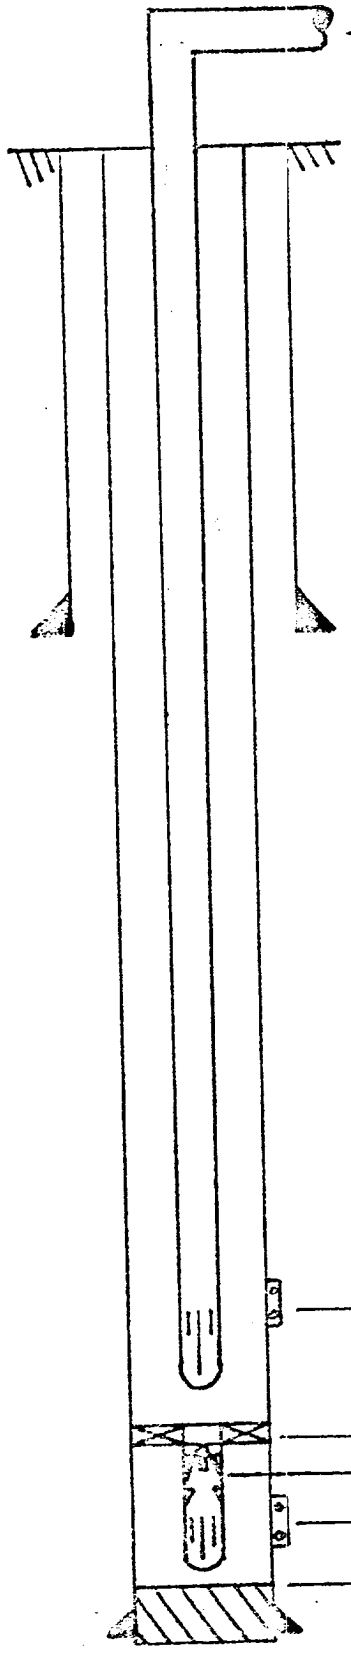

2-3/8" Tbg. Set @ 6476'

9-5/8" casing set at 364' with 300 sx of Trinity Reg. cement
Hole size 12-1/4" Cement Top Circ'd (Observed)

Perfs. 5968-6017'

Otis Type "WA" Prod. Packer @ 6550'

Blanking Plug Set @ 6564'

Perfs. 6587-6719'

PBTD @ 6757'

5-1/2" casing set at 6799' with 3000 sx of Lite Wate cement
Total Depth 6800' Followed w/300 sx of Regular cement
Hole Size 7-5/8" Cement Top 240' (Temp. Survey)
