WELL	DATE	ACE NO	DISTRICT
Alves "A" 2	9-21-76	33-6046	Midland
FIELD	OBJECTIVE ZONE		TOTAL DEPTH
Penrose Skelly (Grayburg)	Grayburg		

LOCATION: SW/4, SW/4, Sec. 8, T-21-S, R-37-E, Lea County, New Mexico

PROPOSED JOB: P. & A.

CONDITIONS — DEPTH — PRESENT — PROPOSED — PROCEDURE — REMARKS

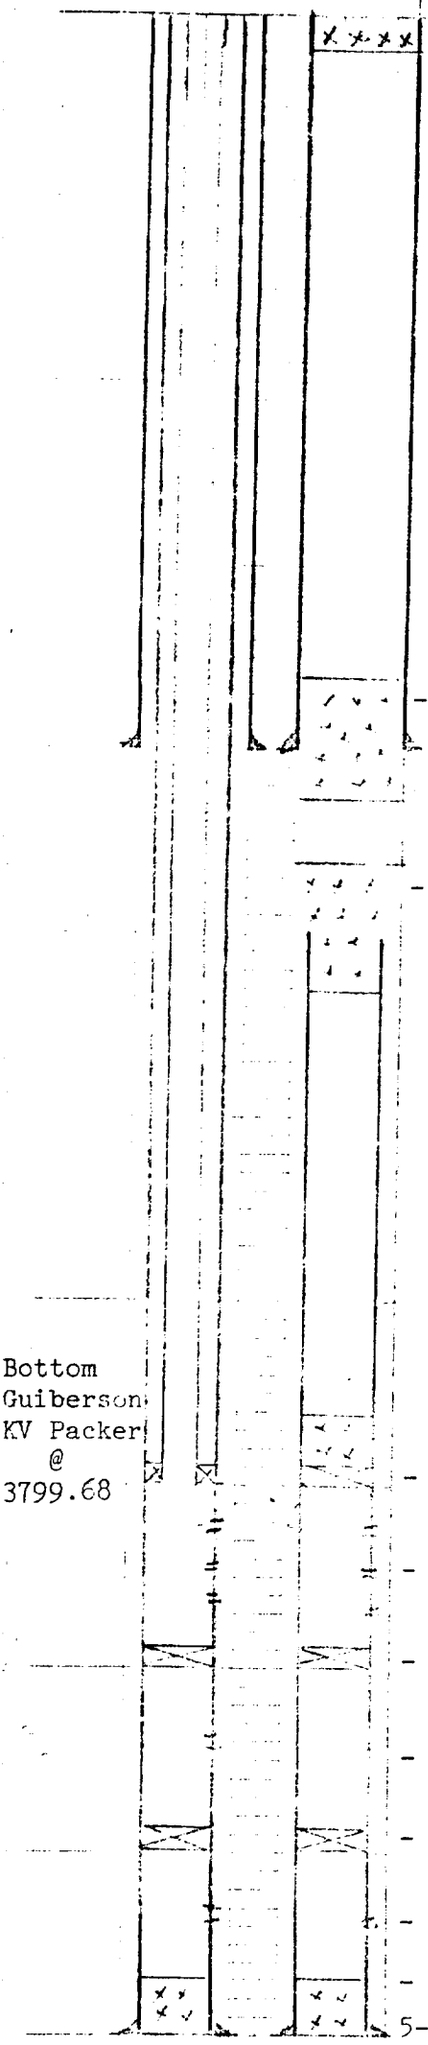

10 sacks cement at surface.

Tubing setting:

10.82	RKB
3777.29	123 jts. 2-3/8" EUE
1.10	SN
1.67	Hyd holddown
8.80	Guiberson KV packer
3799.68'	

Packer releases with 1/2 turn to right.
Eleven points weight on packer.
Packer fluid - 8.4#/gal. water.

- - - 100' cement plug, 1186' to 1286'.

- - 13-3/8", 23#/ft. @ 1236' RKB. Cmt circ to surface.

- - - 100' cement plug, 50' in and 50' out of 5-1/2".

- - Calculated top of cement based on 100% fill = 1401'

- - - CIBP at 3800'± with 35' cement cap.

- - - Perfs 3836 - 3881'.

- - - CIBP at 4030'.

- - - Perfs 4043 - 4060'.

- - - CIBP at 4090'.

- - - Perfs 4096 - 4116'.

- - - PBTD 4379'.

5-1/2" at 4461', 15-1/2# to 2200', 17# to T. D.
