DIAGRAMMATIC SKETCH OF MULTIPLE COMPLETION INSTALLATION

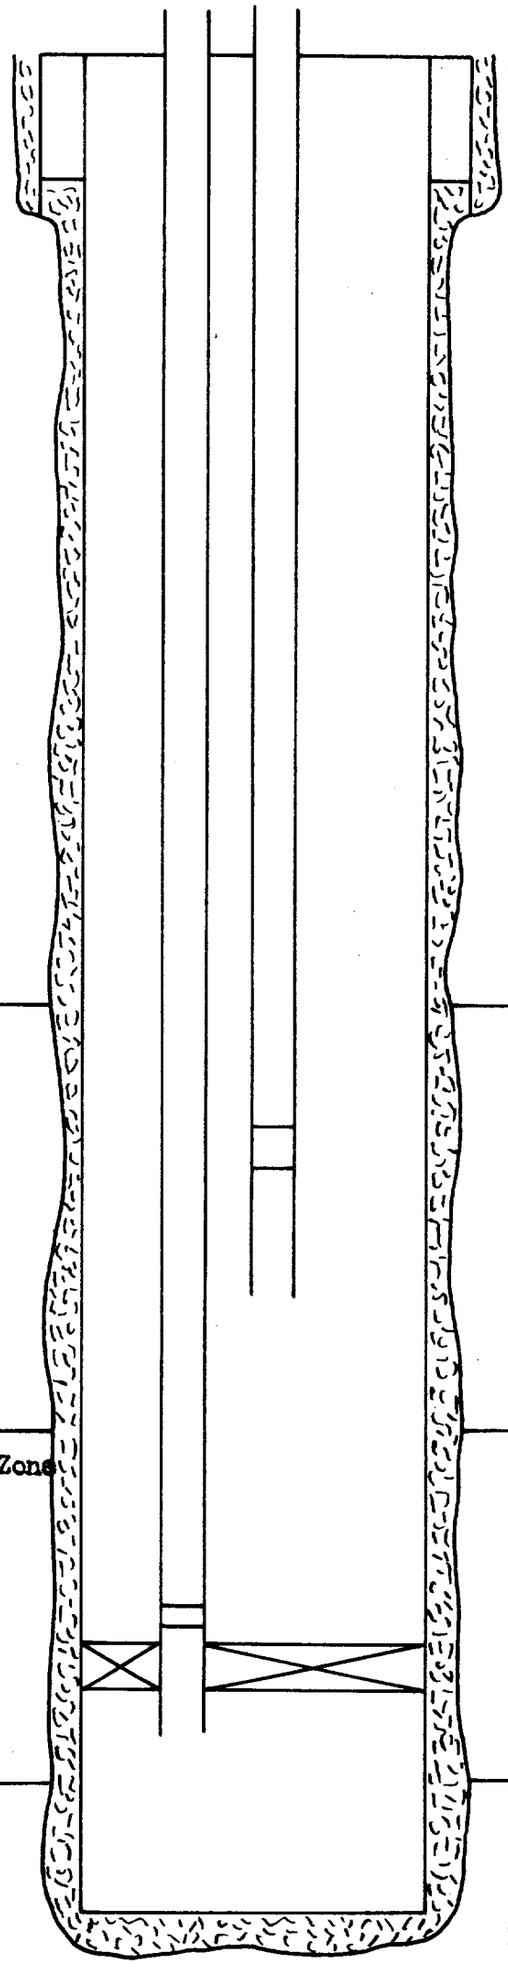

Drilled 13-3/4" hole to 915'.

9-5/8" casing set at 911.13'. Used 2 centralizers at 898' and 845'. Cemented with 580 sacks Incor. Cement circulated. Tested with 1000# for 30 minutes. Drilled 8-3/4" hole to 6052'.

Top of cement - 1475'.

Blinebry Zone

Perforation: 5300-5570' with 4 shots/foot (Probable)
Tubing string - 2-3/8" O.D. EUE 8 rd. Seating nipple at 5270'. Tubing bottomed at 5300' (Probable)

Tubb/Drinkard Zone

Perforation: 5800-6020' with 4 shots/foot (Probable)
Tubing string - 2-3/8" O.D. EUE 8 rd. Seating nipple at 5770'. Tubing bottomed at 5800' (Probable)

Permanent Packer set at 5780' (Probable)

7" casing set at 6045.00' (0-129.33' 7-5/8" casing) Used 15 centralizers at 4897, 4941, 5028, 5071, 5245, 5332, 5376, 5420, 5506, 5758, 5843, 5887, 5930, 5974, 6030. Cement with 450 sacks Incor plus 40% Diacel D. plus 200 Incor. TD 6050'.

THE ATLANTIC REFINING COMPANY
LANGLIE FEDERAL "B" NO. 1 WELL
JUSTIS BLINEBRY & JUSTIS TUBB/DRINKARD POOLS
