XTO ENERGY

A F F I D A V I T

THIS IS TO CERTIFY that to the best of my knowledge the attached survey report details the deviation tests taken on XTO ENERGY INC'S

Breech D #240G
in UL D, Section 15, T26N, R6W,
API #30-039-31013
Rio Arriba County, New Mexico.

Signed

Printed Name Justin Niederhofer

Title Drilling Engineer

THE STATE OF NEW MEXICO)
) SS.
COUNTY OF SAN JUAN)

OFFICIAL SEAL
LORRI D. BINGHAM
NOTARY PUBLIC - STATE OF NEW MEXICO
My commission expires: 7/30/13

BEFORE ME, the undersigned authority, on this day personally appeared, Justin Niederhofer, known to me to be Drilling Engineer for XTO Energy Inc and to be the person whose name is subscribed to the above statement, who, being by me duly sworn on oath, states that he has knowledge of the facts stated herein and that said statement is true and correct.

SUBSCRIBED AND SWORN to before me, a Notary Public in and for said County and State this 14th day of October, 2011.

Notary Public

My Commission Expires: July 30th, 2013

A

Wellbores and Deviation

Well Name: Breech D 240G

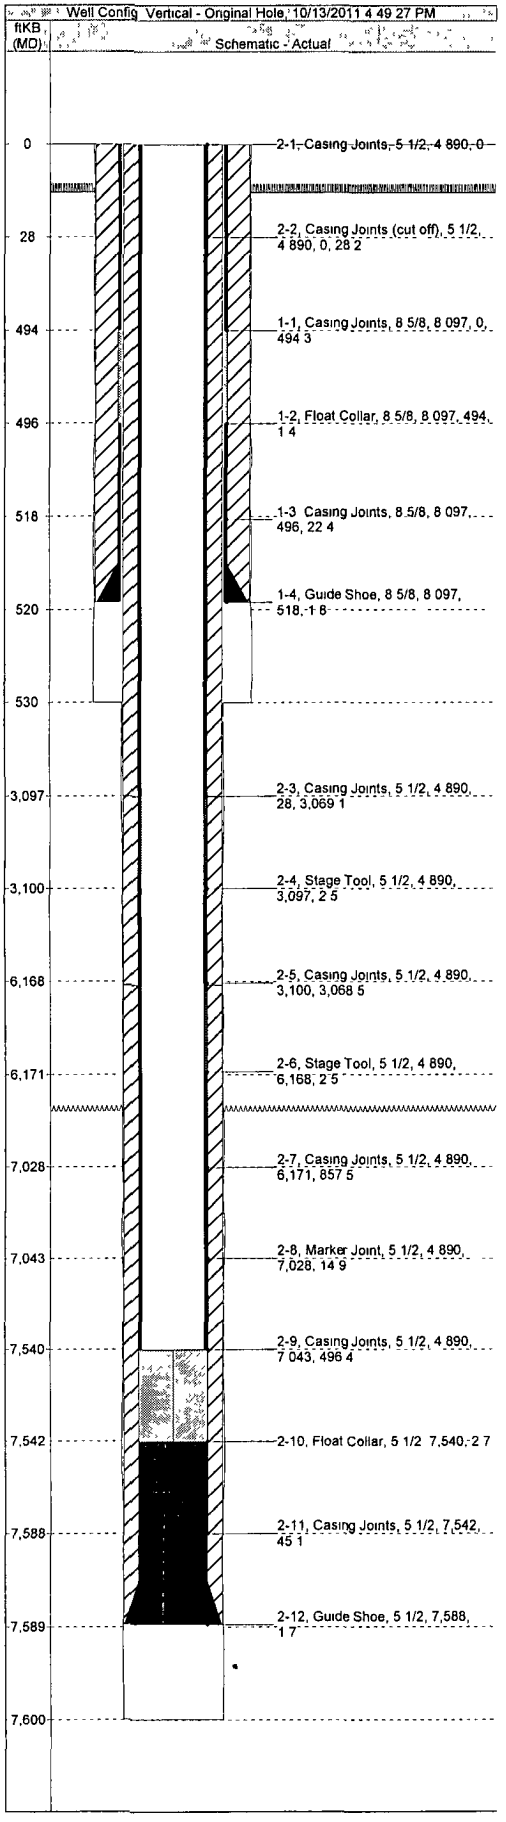

Wellbores

Wellbore Name	Parent Wellbore	Start Depth (ftKB)
Original Hole	Original Hole	0 0

Kick Off Depth (ftKB)	Kick Off Method	Deviation Survey

Wellbore Sections

Section	Size (in)	Act Top (ftKB)	Act Btm (ftKB)	Start Date	End Date
SURFACE1	12 1/4	0 0	530 0	9/9/2011	9/10/2011
PROD1	7 7/8	530 0	7,600 0	9/10/2011	9/30/2011

Deviation Surveys

Date	Description
9/9/2011	WL single shot

Survey Data

Date	MD (ftKB)	Incl (°)	Azm (°)
9/9/2011	154 00	2.00	
9/9/2011	314 00	3 25	
9/9/2011	475 00	3 50	
9/10/2011	530 00	3 50	
9/10/2011	600 00	2 50	
9/10/2011	703 00	2 75	
9/10/2011	827 00	2 50	
9/10/2011	1,139 00	3 25	
9/10/2011	1,265 00	3 25	
9/10/2011	1,420 00	4 00	
9/10/2011	1,520 00	3 75	
9/10/2011	1,610 00	2 25	
9/10/2011	1,850 00	2 25	
9/10/2011	2,048 00	1 75	
9/10/2011	2,143 00	2 00	
9/10/2011	2,238 00	1 25	
9/10/2011	2,325 00	2 00	
9/10/2011	2,584 00	1 75	
9/10/2011	3,058 00	2 00	
9/10/2011	3,530 00	1 50	
9/10/2011	4,120 00	4 00	
9/10/2011	4,230 00	4 00	
9/10/2011	4,348 00	3 75	
9/10/2011	4,444 00	3 00	
9/10/2011	4,539 00	3 00	
9/10/2011	4,633 00	3 00	
9/10/2011	4,735 00	2 75	
9/10/2011	4,835 00	2 50	
9/10/2011	4,935 00	2 00	
9/10/2011	5,135 00	2 25	
9/27/2011	5,325 00	2 00	
9/27/2011	5,840 00	1 75	
9/27/2011	6,340 00	2 75	
9/27/2011	6,552 00	1 75	
9/28/2011	7,054.00	1 00	
9/29/2011	7,215 00	1 50	
9/30/2011	7,600 00	1 25	
