Santa Fe Main Office
Phone: (505) 476-3441
General Information
Phone: (505) 629-6116

Online Phone Directory Visit:
https://www.emnrd.nm.gov/ocd/contact-us/

State of New Mexico
Energy, Minerals and Natural Resources

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-103
Revised July 18, 2013

WELL API NO. 30-021-20667

5. Indicate Type of Lease STATE ☑ FEE ☐

6. State Oil & Gas Lease No.

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)

7. Lease Name or Unit Agreement Name: LEWIS 2028 - 35

1. Type of Well: Oil Well ☐ Gas Well ☐ Other CO2

8. Well Number #001

2. Name of Operator: Breitburn Operating LP

9. OGRID Number: 370080

3. Address of Operator: 500 Dallas st, STE 2300 , Houston ,Tx 77002

10. Pool name or Wildcat

4. Well Location
Unit Letter P : 1112 feet from the South line and 1284 feet from the East line
Section 35 Township 20N Range 28E NMPM County

11. Elevation *(Show whether DR, RKB, RT, GR, etc.)*

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:				SUBSEQUENT REPORT OF:			
PERFORM REMEDIAL WORK	☐	PLUG AND ABANDON	☑	REMEDIAL WORK	☐	ALTERING CASING	☐
TEMPORARILY ABANDON	☐	CHANGE PLANS	☐	COMMENCE DRILLING OPNS.	☐	P AND A	☐
PULL OR ALTER CASING	☐	MULTIPLE COMPL	☐	CASING/CEMENT JOB	☐		
DOWNHOLE COMMINGLE	☐						
CLOSED-LOOP SYSTEM	☐						
OTHER:	☐			OTHER:			☐

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

Breitburn Operating LP is submitting for your review the P&A plan for this well.

Spud Date: Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Arbaz Hussain TITLE Regulatory Analyst DATE 07/06/2026

Type or print name Arbaz Hussain E-mail address: ahussain@dgoc.com PHONE: 832-589-5181

For State Use Only

APPROVED BY: TITLE DATE


Conditions of Approval (if any):

Phone: 918-747-1691
Fax: 918-746-1379
Email: info@orrenergy.com

ORR ENERGY SERVICES

First Place Tower
15 E 5th St., Suite 500
Tulsa, OK 74103

For:	Catherine Isaly	Page:	1
Company:	DGOC	API#:	30-021-20667
Subject:	Lewis 2028 35-1 P&A	Date:	7/6/2026
Location:	Harding Co., NM	By:	Ben Gifford

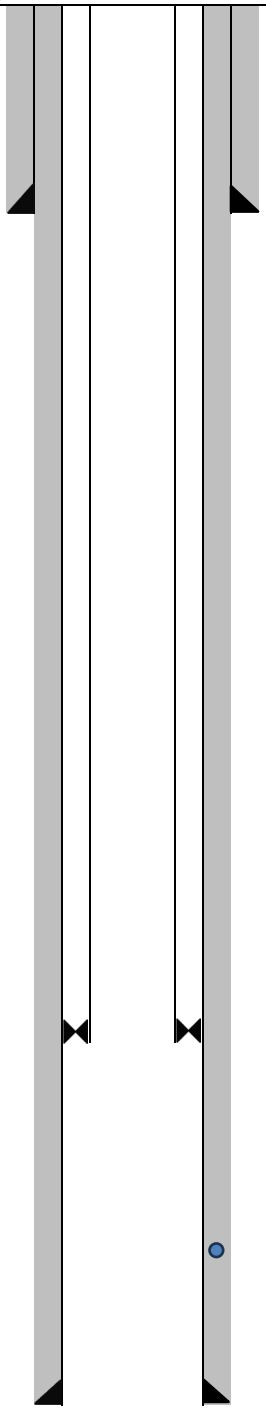

WELLBORE NOTES:

Csg/Tbg Data

Size	Weight	Interval	Top of Cement	Formation	Perforations		
9 5/8"	36#	771'	Surface	Tubb	2688'	to	2713'
5 1/2"	15.5#	2920'	Surface			to	
						to	
						to	
						to	

Procedure:

1. MIRU. BD CSG AND TBG. NU BOP. RELEASE PKR. POH WITH TBG.

2.PU 5 1/2" TBG SET CIBP. SET AT 2638'. RELEASE TBG. CIRC WITH MUD. CAP WITH 30 SKS CEMENT. PUH.


3. LOCATE EOT AT 2231'. MIX AND SPOT 75 SKS CEMENT. PUH WOC AND TAG TOC. PUH.

4. LOCATE EOT AT 1425'. MIX AND SPOT 30 SKS CEMENT. PUH WOC AND TAG TOC. PUH.

5. RU WIRELINE. PERFORATE AT 871'. SQUEEZE WITH 30 SKS CEMENT. WOC AND TAG TOC.

6. PERFORATE AT 500'. LOCATE EOT AT 500'. ATTEMPT SQUEEZE/CIRC TO SURFACE WITH 75 SKS CEMENT. POH. LEAVE FULL.

7. RDSU. CUT AND CAP WELL. DIG UP RIG ANCHORS.

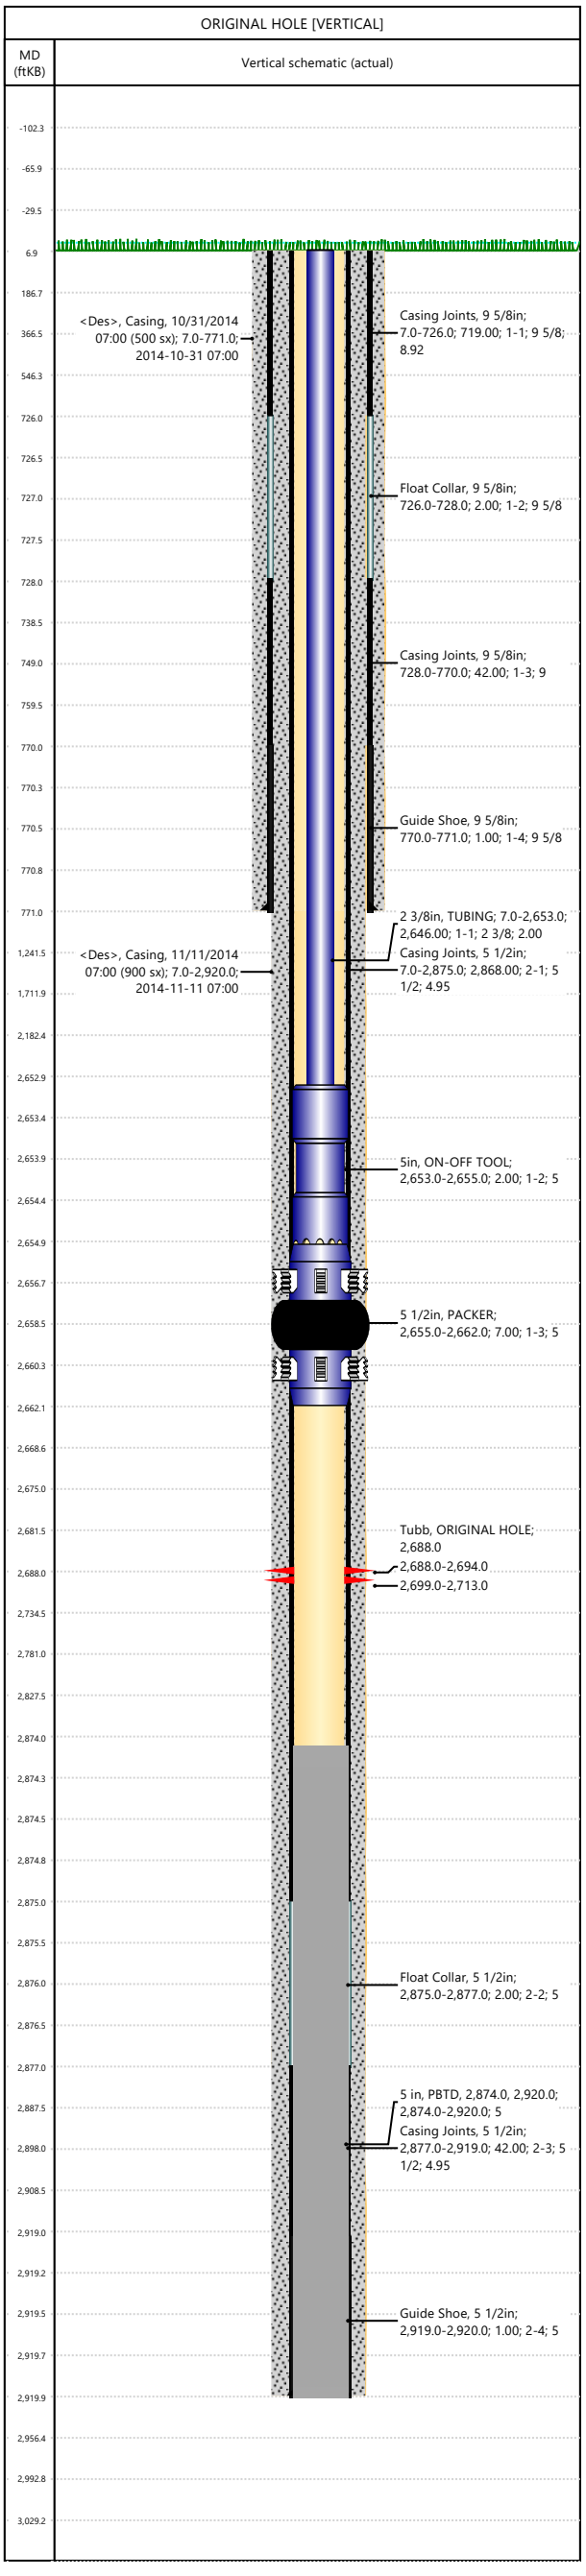

DIVERSIFIED energy

Well Information

Well Name	API/UWI	DGOC Well Code
LEWIS 2028 35-1	3002120667	1238683

County	State/Province
HARDING	NM

Original KB Elevation (ft)	Ground Elevation (ft)	KB-Ground Distance (ft)
5,425.00	5,418.00	7.00

Surface Legal Location	Lat/Long Datum	Latitude (°)	Longitude (°)
	NAD 27	35° 54' 57.352" N	103° 55' 52.849" W

Directions To Well

Casing

Run Date	Casing Description	Set Depth (ftKB)	OD (in)	ID (in)	Wt (lb/ft)	Grade
10/31/2014 06:00	SURFACE	771.0	9 5/8	8.92	36.00	J-55
10/31/2014 06:00	SURFACE	771.0	9 5/8	0.00	0.00	
11/11/2014 06:00	PRODUCTION	2,920.0	5 1/2	4.95	15.50	J-55
11/11/2014 06:00	PRODUCTION	2,920.0	5 1/2	0.00	0.00	

Cement

Description	Top Depth (ftKB)	Bottom Depth (ftKB)
500 sx	7.0	771.0
900 sx	7.0	2,920.0

Zones

Zone Name	Top Depth (ftKB)	Bottom Depth (ftKB)
Tubb	2,688.0	

Tubing

Item Description	OD (in)	ID (in)	Wt (lb/ft)	Grade	Length (ft)	Joints	Top (ftKB)
TUBING	2 3/8	2.00	4.70	J-55	2,646.00	82	7.0
ON-OFF TOOL	5	0.00	0.00		2.00		2,653.0
PACKER	5 1/2	0.00	0.00		7.00		2,655.0

Other In Hole

Description	OD (in)	ID (in)	Top (ftKB)	Btm (ftKB)	Run Date
PBTD	5		2,874.0	2,920.0	11/21/2014 06:00

Plunger Lift Systems

Frequenc	Plunger T	Make	Model	OD (in)	Run Date	Comment	Top (ftK	Btm (ft

State: New Mexico
County: Harding
Spud Date: 10/30/2014


DIVERSIFIED ENERGY
Lewis 2028 35-1
API# 30-021-20667

PROPOSED P&A WBD
6/15/2026

Surface Casing:
9-5/8" 36# J-55
Cmt w/ 500 sx to Surface
771

Production Casing:
5-1/2" 15.5# J-55
Cmt w/ 900 sx to Surface
CBL confirmed TOC @ Surface
2,920

	Southeastern
T. Anhy	
T. Salt	
B. Salt	
T. Yates	
T. Santa Rosa	1325'
T. Queen	
T. Grayburg	
T. San Andres	1824'
T. Glorieta	2131'
T. Paddock	
T. Blinebry	
T.Tubb	2661'
T. Drinkard	
T. Abo	2739'

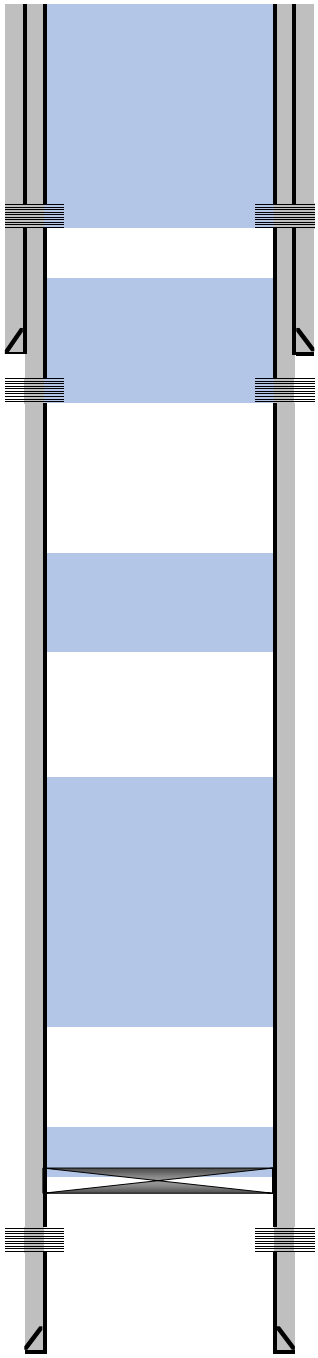

MD

500'

671'
871'

SURFACE & FW ZONE PLUG
Perforate 5-1/2" casing @ 500'
Attempt sq. DO NOT exceed 500 psi.
Squeeze 75 sx Class C cement.
Circ cmt to surface and top fill.

SURFACE SHOE PLUG
Perforate 5-1/2" casing @ 871'
Attempt sq. DO NOT exceed 500 psi.
Squeeze 30 sx Class C cement.
WOC 4 hrs. Tag and record plug depth.

1,225'
1,425'

SANTA ROSA PLUG
Spot 30 sx of Class C cement @ 1,425'
WOC 4 hrs. Tag and record plug depth.

1,734'

2,231'

GLORIETA & SAN ANDRES PLUG
Spot 75 sx of Class C cement @ 2,231'
WOC 4 hrs. Tag and record plug depth.

2,461'
2,638'

TUBB PLUG
Set CIBP @ 2638'
Spot 30 sx of Class C cement @ 2,638'

2,688' **Tubb Perforations**
2688'-2713'

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
Standard Plugging Conditions

This document provides OCD's general plugging conditions of approval. It should be noted that the list below may not cover special plugging programs in unique and unusual cases, and OCD expressly reserves the right to impose additional requirements to the extent dictated by project conditions. The OCD also reserves the right to approve deviations from the below conditions if field conditions warrant a change. A C-103F NOI to P&A must be approved prior to plugging operations. Failure to comply with the conditions attached to a plugging approval may result in a violation of 19.15.5.11 NMAC, which may result in enforcement actions, including but not limited to penalties and a requirement that the well be re-plugged as necessary.

1. Notify OCD office at least 24 hours before beginning work and seek prior approval to implementing any changes to the C-103 NOI to PA.
    - North Contact, Monica Kuehling, 505-320-0243, monica.kuehling@emnrd.nm.gov
    - South Contact, Gilbert Cordero, 575-626-0830, gilbert.cordero@emnrd.nm.gov

2. A Cement Bond Log is required to ensure strata isolation of producing formations, protection of water and correlative rights. A CBL must be run or be on file that can be used to properly evaluate the cement behind the casing.

    Note: Logs must be submitted to OCD via OCD permitting. A copy of the log may be emailed to OCD inspector for faster review times, but emailing does not relieve the operators obligation to submit through OCD permitting.

3. Once Plugging operations have commenced, the rig must not rig down until the well is fully plugged without OCD approval. If gap in plugging operations exceeds 30 days, the Operator must file a subsequent sundry of work performed and revised NOI for approval on work remaining. At no time shall the rig be removed from location if it will result in waste or contamination of fresh water.

4. Insure all bradenheads have been exposed, identified and valves are operational prior to rig up.

5. Fluids must be placed between all cement plugs mixed at 25 sacks per 100 bbls of water.
    - North, water or mud laden fluids
    - South, mud laden fluids

6. Closed loop system is to be used for entire plugging operation. Upon completion, contents of steel pits are to be hauled to an OCD permitted disposal facility.

7. Class of cement shall be used in accordance with the below table for depth allowed.

Class	TVD Lower Limit (feet)
Class A/B	6,000
Class I/II	6,000
Class C or III	6,000
Class G and H	8,000
Class D	10,000
Class E	14,000
Class F	16,000

8. After cutting the well head any "top off cement jobs" must remain static for 30 minutes. Any gas bubbles or flow during this 30 minutes shall be reported to the OCD for approval of next steps.

9. Trucking companies being used to haul oilfield waste fluids (Commercial or Private) to a disposal facility shall have an approved OCD C-133 permit.
    - A copy of this permit shall be available in each truck used to haul waste products.
    - It is the responsibility of the Operator and Contractor to verify that this permit is in place prior to performing work.
    - Drivers shall be able to produce a copy upon request of an OCD Compliance Officer.

10. Filing a [C-103] Sub. Plugging (C-103P) will serve as notification that the well has been plugged.

11. A [C-103] Sub. Release After P&A (C-103Q) shall be filed no later than a year after plugging and a site inspection by OCD Compliance officer to determine if the location is satisfactorily cleaned, all equipment, electric poles and trash has been removed to meet OCD standards before bonding can be released.

12. Produced water or brine-based fluids may not be used during any part of plugging operations without prior OCD approval.

13. Cementing;
    - All cement plugs will be neat cement and a minimum of 100' in length. 50' of calculated cement excess required for inside casing plugs and 100% calculated cement excess required on outside casing plugs.
    - If cement does not exist between or behind the casing strings at recommended formation depths, the casing perforations will be shot at 50' below the formation top and the cement retainer shall be set no more than 50' from the perforations.
    - WOC (Wait on Cement) time will be:
        - 4 hours for accelerated (calcium chloride) cement.
        - 6 hours on regular cement.
    - Operator must tag all cement plugs unless it meets the below condition.
        - The operator has a passing pressure test for the casing annulus and the plug is only an inside plug.
    - If perforations are made operator must tag all plugs using the work string to tag unless given approval to tag with wireline by the correct contact from COA #1 of this document.
        - This includes plugs pumped underneath a cement retainer to ensure retainer seats properly after cement is pumped.
    - Cement can only be bull-headed with specific prior approval.
    - Squeeze pressures are not to exceed the exposed formations frac gradient or the burst pressure of the casing.

14. A cement plug is required to be set from 50’ below to 50’ above (straddling) formation tops, casing shoes, casing stubs, any attempted casing cut offs, anywhere the casing is perforated, DV tools.
    - Perforation/Formation top plug. (When there is less than 100ft between the top perforation to the formation top.) These plugs are required to be started no greater than 50ft from the top perforation. However, the plug should be set below the formation top or as close to the formation top as possible for the maximum isolation between the formations. The plug is required to be a 100ft cement plug plus excess.
    - Perforation Plug when a formation top is not included. These plugs are required to be started within 50ft of the top perforation. The plug is required to be a 100ft cement plug plus excess.
    - Cement caps on top of bridge plugs or cement retainers for perforation plugs, that are not straddling a formation top, may be set using a bailer with a minimum of 35’ of cement in lieu of the 100’ plug. The bridge plug or retainer must be set within 50ft of the perforations.
    - Perforations are required below the surface casing shoe if cement does not exist behind the casing, a 30-minute minimum wait time will be required immediately after perforating to determine if gas and/or water flows are present. If flow is present, the well will be shut-in for a minimum of one hour and the pressure recorded. If gas is detected contact the OCD office for directions.

15. No more than 3000 feet is allowed between cement plugs in cased hole and no more than 2000 feet is allowed in open hole.

16. Formation Tops to be isolated with cement plugs, but not limited to are:
    - Northwest See Figure A
    - South (Artesia) See Figure B
    - Potash See Figure C
        - In the R-111-P (Or as subsequently revised) Area a solid cement plug must be set across the salt section. Fluid used to mix the cement shall be saturated with the salts that are common to the section penetrated and in suitable proportions, not more than 3% calcium chloride (by weight of cement) will be considered the desired mixture whenever possible, woe 4 hours and tag, this plug will be 50' below the bottom and 50' above the top of the Formation.
    - South (Hobbs) See Figure D1 and D2
    - Areas not provided above will need to be reviewed with the OCD on a case by case basis.

17. Markers
    - Dry hole marker requirements 19.15.25.10.
      The operator shall mark the exact location of plugged and abandoned wells with a steel marker not less than four inches in diameter set in cement and extending at least four feet above mean ground level. The marker must include the below information:
        1. Operator name
        2. Lease name and well number
        3. API number
        4. Unit letter
        5. Section, Township and Range

- AGRICULTURE (Below grade markers)
  In Agricultural areas a request can be made for a below ground marker. For a below ground marker the operator must file their request on a C-103 notice of intent, and it must include the following;
  A) Aerial photo showing the agricultural area
  B) Request from the landowner for the below ground marker.
  C) Subsequent plugging report for a well using a below ground marker must have an updated C-102 signed by a certified surveyor for SHL.

  Note: A below ground marker is required with all pertinent information mentioned above on a plate, set 3' below ground level, a picture of the plate will be supplied to OCD for record, the exact location of the marker (longitude and latitude by GPS) will be provided to OCD. OCD requires a current survey to verify the location of the below ground marker, however OCD will accept a GPS coordinate that were taken with a GPS that has an accuracy of within 15 feet.

18. If work has not commenced within 1 year of the approval of this procedure, the approval is automatically expired. After 1 year a new [C-103] NOI Plugging (C-103F) must be submitted and approved prior to work.

Figure A

North Formations to be isolated with cement plugs are:

- San Jose
- Nacimiento
- Ojo Alamo
- Kirtland
- Fruitland
- Picture Cliffs
- Chacra (if below the Chacra Line)
- Mesa Verde Group
- Mancos
- Gallup
- Basin Dakota (plugged at the top of the Graneros)
- Deeper formations will be reviewed on a case-by-case basis

Figure B

South (Artesia) Formations to be isolated with cement plugs are:

- Fusselman
- Montoya
- Devonian
- Morrow
- Strawn
- Atoka
- Permo-Penn
- Wolfcamp
- Bone Springs
- Delaware , in certain areas where the Delaware is subdivided into;
  - 1. Bell Canyon
  - 2. Cherry Canyon
  - 3. Brushy Canyon
- Any salt sections
- Abo
- Yeso
- Glorieta
- San Andres
- Greyburg
- Queen
- Yates

Figure C

Potash Area R-111-P

T 18S – R 30E
Sec 10 Unit P. Sec 11 Unit M,N. Sec 13 Unit L,M,N. Sec 14 Unit C -P. Sec 15 Unit A G,H,I,J,K,N,O,P. Sec 22 Unit All
except for M. Sec 23, Sec 24 Unit C,D,E,L, Sec 26 Unit A-G, Sec 27 Unit A,B,C

T 19S – R 29E
Sec 11 Unit P. Sec 12 Unit H-P. Sec 13. Sec 14 Unit A,B,F-P. Sec 15 Unit P. Sec 22 Unit A,B,C,F,G,H,I,J
K,N,O,P. Sec 23.
Sec 24. Sec 25 Unit D. Sec 26 Unit A- F. Sec 27 Unit A,B,C,F,G,H.

T 19S – R 30E
Sec 2 Unit K,L,M,N. Sec 3 Unit I,L,M,N,O,P. Sec 4 Unit C,D,E,F,G,I-P. Sec 5 Unit A,B,C,E-P. Sec 6 Unit I,O,P. Sec 7 – Sec
10. Sec 11 Unit D, G—P. Sec 12 Unit A,B,E-P. Sec 13 Unit A-O. Sec 14-Sec 18. Sec 19 Unit A-L, P. Sec 20 – Sec 23. Sec
24 Unit C,D,E,F,L,M,N. Sec 25 Unit D. Sec 26 Unit A-G, I-P. Sec 27, Sec 28, Sec 29 Unit A,B,C,D,F,G,H,I,J,O,P. Sec 32
Unit A,B,G,H,I,J,N,O,P. Sec 33. Sec 34. Sec 35. Sec 36 Unit D,E,F,I-P.

T 19S – R 31E
Sec 7 Unit C,D,E,F,L. Sec 18 Unit C,D,E,F,G,K,L. Sec 31 Unit M. Sec 34 Unit P. Sec 35 Unit M,N,O. Sec 36 Unit O,P.

T 20S – R 29E
Sec 1 Unit H,I,P. Sec 13 Unit E,L,M,N. Sec 14 Unit B-P. Sec 15 Unit A,H,I,J,N,O,P. Sec 22 Unit A,B,C,F,G,H,I,J,O,P. Sec
23. Sec 24 Unit C,D,E,F,G,J-P. Sec 25 Unit A-O. Sec 26. Sec 27 Unit A,B,G,H,I,J,O,P. Sec 34 Unit A,B,G,H. Sec 35 Unit
A-H. Sec 36 Unit B-G.

T 20S – R 30E
Sec 1 – Sec 4. Sec 5 Unit A,B,C,E-P. Sec 6 Unit E,G-P. Sec 7 Unit A-H,I,J,O,P. Sec 8 – 17. Sec 18 Unit A,B,G,H,I,J,O,P.
Sec 19 Unit A,B,G,H,I,J,O,P. Sec 20 – 29. Sec 30 Unit A-L,N,O,P. Sec 31 Unit A,B,G,H,I,P. Sec 32 – Sec 36.

T 20S – R 31E
Sec 1 Unit A,B,C,E-P. Sec 2. Sec 3 Unit A,B,G,H,I,J,O,P. Sec 6 Unit D,E,F,J-P. Sec 7. Sec 8 Unit E-P. Sec 9 Unit E,F,J-P.
Sec 10 Unit A,B,G-P. Sec 11 – Sec 36.

T 21S – R 29E
Sec 1 – Sec 3. Sec 4 Unit L1 – L16,I,J,K,O,P. Sec 5 Unit L1. Sec 10 Unit A,B,H,P. Sec 11 – Sec 14. Sec 15 Unit A,H,I. Sec
23 Unit A,B. Sec 24 Unit A,B,C,D,F,G,H,I,J,O,P. Sec 25 Unit A,O,P. Sec 35 Unit G,H,I,J,K,N,O,P. Sec 36 A,B,C,F – P.

T 21S – R 30E
Sec 1 – Sec 36

T 21S – R 31E

Sec 1 – Sec 36

T 22S – R 28E
Sec 36 Unit A,H,I,P.

T 22S – R 29E
Sec 1. Sec2. Sec 3 Unit I,J,N,O,P. Sec 9 Unit G – P. Sec 10 – Sec 16. Sec 19 Unit H,I,J. Sec 20 – Sec 28. Sec 29 Unit
A,B,C,D,G,H,I,J,O,P. Sec 30 Unit A. Section 31 Unit C – P. Sec 32 – Sec 36

T 22S – R 30E
Sec 1 – Sec 36

T 22S – R 31E
Sec 1 – Sec 11. Sec 12 Unit B,C,D,E,F,L. Sec 13 Unit E,F,K,L,M,N. Sec 14 – Sec 23. Sec 24 Unit
C,D,E,F,K,L,M,N. Sec 25
Unit A,B,C,D. Sec 26 Unit A,BC,D,G,H. Sec 27 – Sec 34.

T 23S – R 28E
Sec 1 Unit A

T 23S – R 29E
Sec 1 – Sec 5. Sec 6 Unit A – I, N,O,P. Sec 7 Unit A,B,C,G,H,I,P. Sec 8 Unit A – L, N,O,P. Sec 9 – Sec 16. Sec 17 Unit
A,B,G,H,I,P. Sec 21 – Sec 23. Sec 24 Unit A – N. Sec 25 Unit D,E,L. Sec 26. Sec 27. Sec 28 Unit A – J, N,O,P. Sec 33
Unit A,B,C. Sec 34 Unit A,B,C,D,F,G,H. Sec 35. Sec 36 Unit B,C,D,E,F,G,K,L.

T 23S – R 30E
Sec 1 – Sec 18. Sec 19 Unit A – I,N,O,P. Sec 20, Sec 21. Sec 22 Unit A – N, P. Sec 23, Sec 24, Sec 25. Sec 26 Unit
A,B,F-P. Sec 27 Unit C,D,E,I,N,O,P. Sec 28 Unit A – H, K,L,M,N. Sec 29 Unit A – J, O,P. Sec 30 Unit A,B. Sec 32 A,B. Sec
33 Unit C,D,H,I,O,P. Sec 34, Sec 35, Sec 36.

T 23S – R 31E
Sec 2 Unit D,E,J,O. Sec 3 – Sec 7. Sec 8 Unit A – G, K – N. Sec 9 Unit A,B,C,D. Sec 10 Unit D,P. Sec 11 Unit G,H,I,J,M,N,O,P. Sec 12 Unit E,L,K,M,N. Sec 13 Unit C,D,E,F,G,J,K,L,M,N,O. Sec 14. Sec 15 Unit A,B,E – P. Sec 16 Unit
I, K – P. Sec 17 Unit B,C,D,E, I – P. Sec 18 – Sec 23. Sec 24 Unit B – G, K,L,M,N. Sec 25 Unit B – G, J,K,L. Sec 26 – Sec
34. Sec 35 Unit C,D,E.

T 24S – R 29E
Sec 2 Unit A, B, C, D. Sec 3 Unit A

T 24S – R 30E
Sec 1 Unit A – H, J – N. Sec 2, Sec 3. Sec 4 Unit A,B,F – K, M,N,O,P. Sec 9 Unit A – L. Sec 10 Unit A – L, O,P. Sec 11.
Sec 12 Unit D,E,L. Sec 14 Unit B – G. Sec 15 Unit A,B,G,H.

T 24S – R 31E
Sec 3 Unit B – G, J – O. Sec 4. Sec 5 Unit A – L, P. Sec 6 Unit A – L. Sec 9 Unit A – J, O,P. Sec 10 Unit B – G, K – N. Sec
35 Unit E – P. Sec 36 Unit E,K,L,M,N.

T 25S – R 31E
Sec 1 Unit C,D,E,F. Sec 2 Unit A – H.

Figure D1 and D2

South (Hobbs) Formations to be isolated with cement plugs are:

The plugging requirements in the Hobbs Area are based on the well location within specific areas of the Area (See Figure D1). The Formations in the Hobbs Area to be isolated with cement plugs are (see Figure D2)

Figure D1 Map

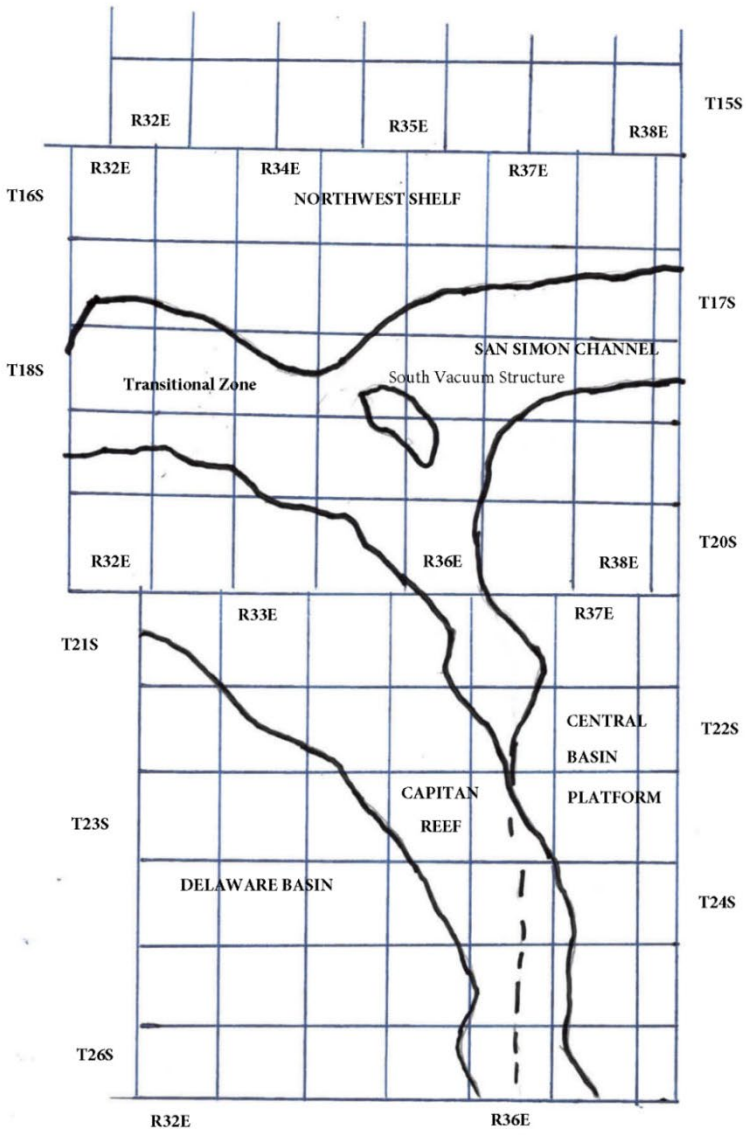


Figure D2 Formation Table

100' P'lug to isolate upper and lower fresh water zones (typiailly 2.50' to 350')						
ND!rthwest Shelf	**C;iptan Reef Are<a**	**Trani5ition Zone**	**San Simon Oh.annel**	**South \lacJUUm Structure**	**Delaware Basin**	**Ce<n,tiral Basin Platform**
Granit \./ash (Detrital basement material and fractured pre-Cambrian basement rock)	Siluro-Devonian	Morrow	Siluro-Devonian	Ellenburger	Siluro-Devonian	Granit \./ash (Detrital basement material, fractured pre-Cambrian basement rock and fracture Mafic Volcanic intrusives).
Montoya	Mississippian	Atoka	Morrow	Mckee	Morrow	Ellenburger
Fusselman	Morrow	Strawn	\./olfcamp	Siluro-Devonian	Atoka	Connell
Woodford	Atoka	Cisco	Abo Reef	Woodford	Strawn	Waddell
Siluro-Devonian	Strawn	Pennsylvanian	Bone Spring	Mississippian	Pennsylvanian	Mckee
Chester	Pennsylvanian	\./olfcamp	Delaware	Barnett Shale	Low er \./olfcamp	Simpson Group
Austin	\./olfcamp	Bone Spring	San Andres	Morrow	Upper \./olfcamp	Montoya
Mississippian	Abo Reef, if present	Delaware	Queen	Atoka	\./olfcamp	Fusselman
Morrow	Abo, if present	San Andres	Yates	Strawn	Third Bone Spring Sand (Top of \./olfbone)	Silurian
Atoka	Queen, if present	Grayburg-San Andres	Base of Salt	Canyon	First Bone Spring Sand (Top of Lower Bone Spring)	Devonian
Lower Pennsylvanian	Bone Spring	Queen	Rustler	Pennsylvanian	Bone Spring	Strawn
Cisco-Canyon	Delaware	Seven Rivers		Blinebry	Brushy Canyon	Pennsylvanian
Pennsylvanian	Base Capitan Reef	Yates		Bone Spring	Delaw are (Base of Salt)	\./olfcamp
Bough	Seven Rivers	Base of Salt		San Andres	Rustler	Abo
\./olfcamp	Yates	Rustler		Queen		Abo Reef
Abo	Top Capitan Reef			Base of Salt		Drinkard
Abo Reef, if present	Base of Salt			Rustler		Tubb
Yeso (Township 15 South to Township 17 South)	Rustler					Blinebry
Drinkard or Low er Y eso (Township 15 South to Township 17 South)						Paddock
Tubb (Township 15 South to Township 17 South)						Glorieta
Blinebry (Township 15 South to Township 17 South)						San Andres
Pad dock (Township 15 South to Township 17 South)						Grayburg
Glorieta						Gr ayburg-San Andres
San Andres						Queen
Queen (Township 15 South to Township 17 South)						Seven Rivers
Seven Rivers (Township 15 South to Township 17 South)						Yates
Yates (Township 15 South to Township 17 South)						Base of Salt
Base of Salt						Rustler
Rustler						

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 602250

CONDITIONS

Operator: BREITBURN OPERATING LP 500 Dallas street, Suite 2300 Houston, TX 77002	OGRID: 370080
	Action Number: 602250
	Action Type: [C-103F] NOI Plug & Abandon (C-103F)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	Notify the OCD inspection supervisor via email 24 hours prior to beginning Plug & Abandon (P&A) operations.	7/20/2026
loren.diede	Monitor all string pressures including Bradenhead daily and report those findings on Subsequent Report.	7/20/2026
loren.diede	A CBL log must be run and submitted to NMOCD for evaluation after the CIBP has been set at 2638' and prior to commencing with the plugging.	7/20/2026
loren.diede	See attached COAs regarding the P&A marker requirements.	7/20/2026
