Well Name: ARIZONA JICARILLA

Well Location: T25N / R4W / SEC 36 / SESE / 36.3511812 / -107.1983111

County or Parish/State: RIO ARRIBA / NM

Well Number: 6

Type of Well: CONVENTIONAL GAS WELL

Allottee or Tribe Name: JICARILLA APACHE

Lease Number: JIC125

Unit or CA Name:

Unit or CA Number:

US Well Number: 3003905699

Operator: HILCORP ENERGY COMPANY

Subsequent Report

Sundry ID: 2925628

Type of Submission: Subsequent Report

Type of Action: Plug and Abandonment

Date Sundry Submitted: 08/04/2026

Time Sundry Submitted: 08:20

Date Operation Actually Began: 07/29/2026

Actual Procedure: Hilcorp Energy Company has plugged and abandoned the subject well on 8/3/2026 per the attached daily report.

SR Attachments

Actual Procedure

ARIZONA_JICARILLA_6_SR_P_A_BLM_Submitted_20260804081951.pdf

CONFIDENTIAL

Well Name: ARIZONA JICARILLA

Well Location: T25N / R4W / SEC 36 / SESE / 36.3511812 / -107.1983111

County or Parish/State: RIO ARRIBA / NM

Well Number: 6

Type of Well: CONVENTIONAL GAS WELL

Allottee or Tribe Name: JICARILLA APACHE

Lease Number: JIC125

Unit or CA Name:

Unit or CA Number:

US Well Number: 3003905699

Operator: HILCORP ENERGY COMPANY

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: PRISCILLA SHORTY

Signed on: AUG 04, 2026 08:20 AM

Name: HILCORP ENERGY COMPANY

Title: Regulatory Technician

Street Address: 382 ROAD 3100

City: AZTEC **State:** NM

Phone: (505) 324-5188

Email address: PSHORTY@HILCORP.COM

Field

Representative Name:

Street Address:

City: **State:** **Zip:**

Phone:

Email address:

BLM Point of Contact

BLM POC Name: KENNETH G RENNICK

BLM POC Title: Petroleum Engineer

BLM POC Phone: 5055647742

BLM POC Email Address: krennick@blm.gov

Disposition: Accepted

Disposition Date: 08/04/2026

Signature: Kenneth Rennick

CONFIDENTIAL

ARIZONA JICARILLA 6 30.039.05699 PLUG AND ABANDONMENT

7/29/2026 - HELD PJSM. MOVE P&A PKG TO LOC. LOTO. SPOT EQUIP. RU P&A PKG. CK PSI; TBG-280#, CSG-20#, BH-0#. BDW 5 MINS. FT BOP. ND WH. NU BOP, RU RF & TBG EQUIP. PULL HANGER. SIW. SDFN.

7/30/2026 - HELD PJSM. SERVICE & START EQUIP. CK PSI; TBG-10#, CSG-10#, BH-0#, BDW 1 MIN. LD 117 JTS OF 2 3/8'' J55 EUE. SWAP TBG TRAILERS. TALLY, RABBIT & PUP. RH W/ 4.5'' SM TO 3550'. TOOH LD SM. TIH W/ 4.5'' CR. SET CR @ 3500' +/-. PUMP 45 BBLS TO EST CIRC PUMP 65 TOTAL. PSI TEST CSG TO 600# PSI. NO TEST. TOOH LD STINGER. RU TWG. RIH W/ CBL TOOL. LOG WELL FROM CR @ 3500' TO SURF. RD WL. EST TOC @ 2850'. TIH W/ TS TO CR. **PLUG #1 FROM 3500' - 3038'. (4.5'') (462') M&P 36 SKS CLASS G, 15.8PPG, 1.15YIELD, 7.3BLSRY, 4.2MIX, 11.5 DIS**, LD TOC. TOOH SIW. WOC. SDFN. **BILL DIERS, BLM REP, ON LOCATION.**

7/31/2026 - HELD PJSM. SERVICE & START EQUIP. CK PSI; TBG-0#, CSG-0#, BH-0#, BDW 0 MIN. **TIH TAG TOC @ 3065'. (BLM REP APPROVED TAG)** LD TBG TO PLUG #2. **PLUG #2 FROM 3044'- 2839' (4.5'')(205') M&P 16 SKS CLASS G, 15.8PPG, 1.15YIELD. 3.2BLSRY, 1.9MIX, 10.7DIS, 2%CAL.** LD TOC. TOOH. SIW. WOC. **TIH TAG TOC @ 2881'. (BLM REP APPROVED TAG)** PSI TEST CSG. NO TEST. (BAD LEAK OFF) LD TBG TO PLUG #3. TOOH LD TS. JSA. RU TWG. RIH W/ TG & PERF @ 821'. NO RATE EST DUE TO BAD CSG TEST. RD WL. TIH W/ 4.5'' CR & SET CR @ 771'. PSI TEST CSG ABOVE CR TO 600# PSI. NO TEST. NO RATE EST BELOW CR. PSI LOCK UP TO 1500# PSI. **BLM REP APPROVED 14 SKS INSIDE 4.5''. PLUG #3 FROM 771'- 591' (4.5'') M&P 14 SKS CLASS G, 15.8PPG, 1.15YIELD. 2.8BLSRY, 5,MIX, 2.2DIS.** LD TOC. REVERSE OUT. TOOH LD STINGER. SIW, SDFN. **BILL DIERS, BLM REP, ON LOCATION.**

8/3/2026 - HELD PJSM. SERVICE & START EQUIP. CK PSI; TBG-0#, CSG-0#, BH-0#, BDW 0 MIN. **TIH TAG TOC @ 615'. (BLM REP APPROVED TAG**) LD ALL TBG. JSA RU WL. RIH W/ TG & PERF @ 207'. WL BECAME STUCK UNABLE TO MOVE UP OR DOWN) PUMP 33 BBLS TO EST CIRC FROM BH VALVE. WORK WL, STILL STUCK. **WAIT ON ORDERS.** PUMP DYE TO DETERMINE CIRC POINT. PUMP 22 BBLS TOTAL. **ORDERS TO PULL OUT OF ROPE SOCKET & PROCEED. BLM APPROVED TO BULLHEAD SURF PLUG**. **PULL OUT OF WL ROPE SOCKET.** RD WL. RD RF & TBG EQUIP. ND BOP. NU WH. **PLUG #4 FROM 207'- 0' (4.5' x 8 5/8'') M&P 57 SKS CLASS G, 15.8PPG, 1.15YIELD. 11.6BLSRY, 6.7MIX, 2%CAL. CIRC CMT TO SURF.** SIW. WOC. DIG OUT WH. MONITOR WH PSI. BUBBLE TEST BH. TEST OK CUT & REMOVE WH. FIND TOC @ 60' INSIDE 4.5'' CSG. **WELD & INSTALL DHMP @ 36.3512 / -107.19892.** TOP OFF CELLAR W/ 26 SKS CLASS G 15.8PPG, 1.15YIELD. RD P&A PKG. DRAIN EQUIP. CLEAN & SECURE LOC. **BILL DIERS, BLM REP, ON LOCATION.**

WELL PLUGGED AND ABANDONED ON 8/3/2026.


Wilcorp Energy Co
Arizona Jicarilla #6
Lease # Jic 125
API 30-039-05699
T25N R4W Sec 36 SESE
Lat 36.3511812
Long -107.1983111
Rio Arriba NM
8-3-26
03.08.2026 14:40
36.3512, -107.19892 (±6m)
N
11°

Hilcorp Energy Company

Current Schematic - Version 3


Well Name: ARIZONA JICARILLA #6

API / UWI	Surface Legal Location	Field Name	Route	State/Province	Well Configuration Type
3003905699	036-025N-004W-P	BLANCO P.C. SOUTH (GAS)	1411	NEW MEXICO	Vertical
Ground Elevation (ft)	**Original KB/RT Elevation (ft)**	**Tubing Hanger Elevation (ft)**	**RKB to GL (ft)**	**KB-Casing Flange Distance (ft)**	**KB-Tubing Hanger Distance (ft)**
7,203.00	7,213.00		10.00		

Tubing Strings

Run Date	Set Depth (ftKB)	String Max Nominal OD (in)	String Min Nominal ID (in)	Weight/Length (lb/ft)	Original Spud Date
1/25/1971 00:00	3,520.00	2 3/8	2.00	4.70	9/12/1959 00:00

Original Hole, ARIZONA JICARILLA 6 [Vertical]

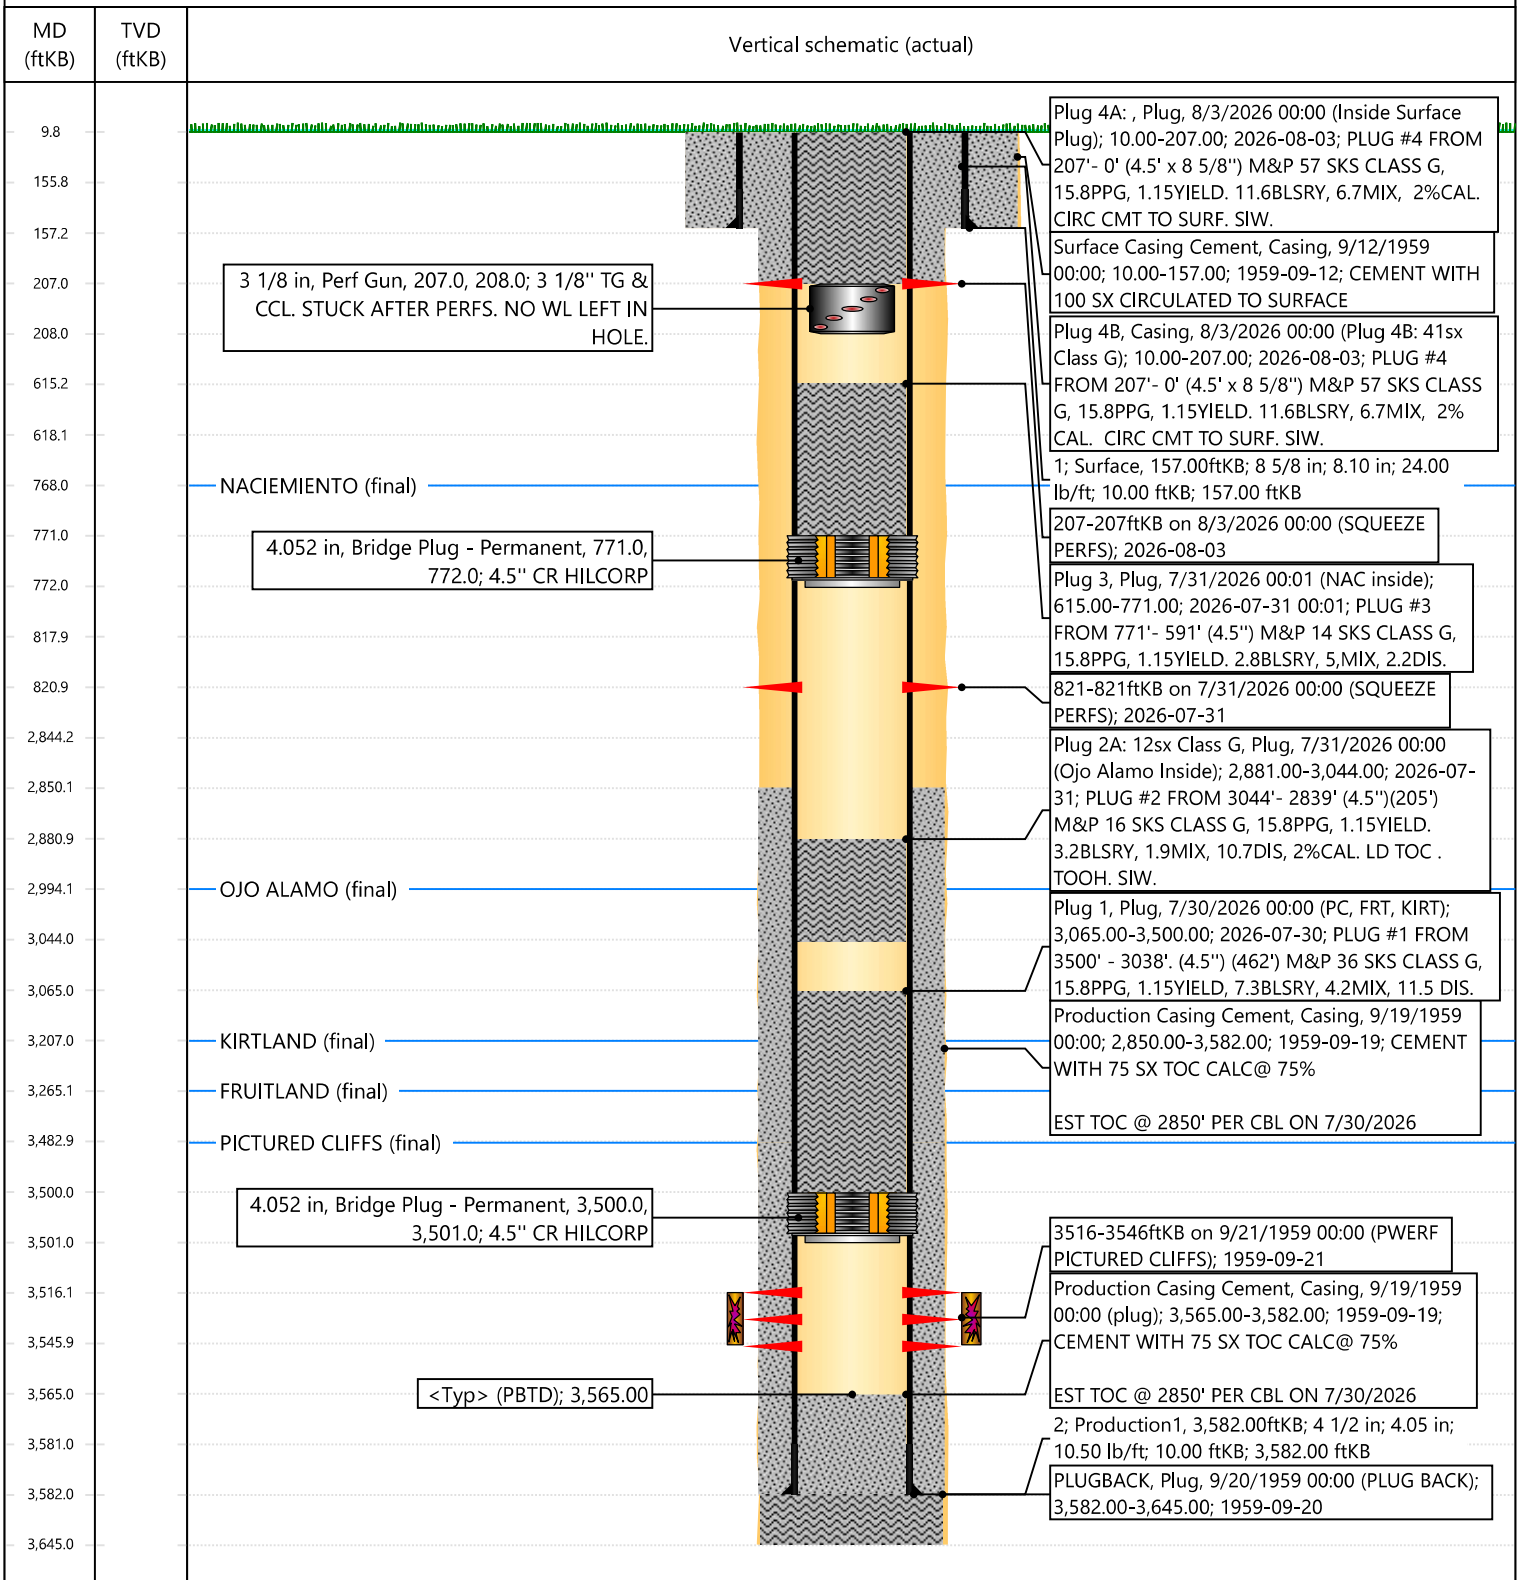

Priscilla Shorty

From: Garcia, John, EMNRD <JohnA.Garcia@emnrd.nm.gov>
Sent: Friday, July 31, 2026 3:03 PM
To: Whitney Majetich; Oscar Sanchez - (C); Farmington Regulatory Techs; Priscilla Shorty; Tammy Jones
Subject: RE: [EXTERNAL] Fw: HILCORP ARIZONA JICARILLA #6 - Procedure Update

CAUTION: External sender. DO NOT open links or attachments from UNKNOWN senders.

OCD agrees with BLM.

Thank you,
John Garcia
Petroleum Specialist Supervisor
Oil Conservation Division
1220 South St. Francis Drive
Santa Fe, New Mexico 87505

From: Whitney Majetich <whitney.majetich@hilcorp.com>
Sent: Friday, July 31, 2026 3:00 PM
To: Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Tammy Jones <tajones@hilcorp.com>; Garcia, John, EMNRD <JohnA.Garcia@emnrd.nm.gov>
Subject: Fw: [EXTERNAL] Fw: HILCORP ARIZONA JICARILLA #6 - Procedure Update

See the below response from Matthew Kade backfilling Kenny Rennick while he is out.

Thanks,
Whitney Majetich
Cell: (281) 467-2130

From: Kade, Matthew H <mkade@blm.gov>
Sent: Friday, July 31, 2026 3:58 PM
To: Whitney Majetich <whitney.majetich@hilcorp.com>
Cc: Diers, William B <WDiers@blm.gov>; Benally, Jared J <jbenally@blm.gov>; jaredbenally <jaredbenally@jicarillaoga.com>; Rennick, Kenneth G <krennick@blm.gov>
Subject: Re: [EXTERNAL] Fw: HILCORP ARIZONA JICARILLA #6 - Procedure Update

You don't often get email from mkade@blm.gov. Learn why this is important

CAUTION: External sender. DO NOT open links or attachments from UNKNOWN senders.

Thank you. The BLM approves of moving forward with the approved plan from the field. If the BLM or Tribal Inspector witnessing wishes to require waiting on cement and tag, then Hilcorp will be required to wait and tag.

Thanks,
Matthew Kade
Supervisory Petroleum Engineer/Division Chief
Office: 406-791-7716
Cell: 406-464-4422
North Central Montana District - Division of Oil and Gas
Great Falls, MT 59405

From: Whitney Majetich <whitney.majetich@hilcorp.com>
Sent: Friday, July 31, 2026 2:41 PM
To: Kade, Matthew H <mkade@blm.gov>
Subject: [EXTERNAL] Fw: HILCORP ARIZONA JICARILLA #6 - Procedure Update

This email has been received from outside of DOI - Use caution before clicking on links, opening attachments, or responding.

Hi Matthew,

Per Kenny's out of office email, I wanted to forward you this update on the Arizona Jicarilla #6 well.

Thanks,
Whitney Majetich
Cell: (281) 467-2130

From: Whitney Majetich <whitney.majetich@hilcorp.com>
Sent: Friday, July 31, 2026 3:39 PM
To: Garcia, John, EMNRD <JohnA.Garcia@emnrd.nm.gov>; Rennick, Kenneth G <krennick@blm.gov>; Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Paula Routt - (C) <Paula.Routt@hilcorp.com>; Diers, William B <WDiers@blm.gov>; Benally, Jared J <jbenally@blm.gov>; jaredbenally <jaredbenally@jicarillaoga.com>
Subject: HILCORP ARIZONA JICARILLA #6 - Procedure Update

Good Afternoon Everyone,

Preparing for Plug #3, Nacimiento Plug. We were unable to successfully pressure test casing.
We perforated at 821' and set a CICR @ 771'. We did not receive a successful pressure test above the CICR. We stung in to establish injection on the CICR and we locked up to 1500# below our retainer. We received approval on location to pump 14sx cmt on top of the CICR and proceed with plug #4.

Thanks,
Whitney Majetich
Cell: (281) 467-2130

From: Garcia, John, EMNRD <JohnA.Garcia@emnrd.nm.gov>
Sent: Thursday, July 30, 2026 3:48 PM
To: Rennick, Kenneth G <krennick@blm.gov>; Whitney Majetich <whitney.majetich@hilcorp.com>; Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Paula Routt - (C) <Paula.Routt@hilcorp.com>; Diers, William B <WDiers@blm.gov>; Benally, Jared J <jbenally@blm.gov>; jaredbenally <jaredbenally@jicarillaoga.com>
Subject: RE: [EXTERNAL] HILCORP ARIZONA JICARILLA #6 CBL

CAUTION: External sender. DO NOT open links or attachments from UNKNOWN senders.

OCD agrees

Thank you,
John Garcia
Petroleum Specialist Supervisor
Oil Conservation Division
1220 South St. Francis Drive
Santa Fe, New Mexico 87505

From: Rennick, Kenneth G <krennick@blm.gov>
Sent: Thursday, July 30, 2026 2:48 PM
To: Whitney Majetich <whitney.majetich@hilcorp.com>; Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Paula Routt - (C) <Paula.Routt@hilcorp.com>; Garcia, John, EMNRD <JohnA.Garcia@emnrd.nm.gov>; Diers, William B <WDiers@blm.gov>; Benally, Jared J <jbenally@blm.gov>; Jared Benally <jaredbenally@jicarillaoga.com>
Subject: Re: [EXTERNAL] HILCORP ARIZONA JICARILLA #6 CBL

Jicarilla Apache well

The BLM finds the updated procedure appropriate.

Kenneth (Kenny) Rennick

Petroleum Engineer

Bureau of Land Management
Farmington Field Office
6251 College Blvd
Farmington, NM 87402

Email: krennick@blm.gov
Mobile & Text: 505.497.0019

From: Whitney Majetich <whitney.majetich@hilcorp.com>
Sent: Thursday, July 30, 2026 2:31 PM
To: Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Paula Routt - (C) <Paula.Routt@hilcorp.com>; Rennick, Kenneth G <krennick@blm.gov>; Garcia, John, EMNRD <johna.garcia@emnrd.nm.gov>; Diers, William B <WDiers@blm.gov>
Subject: Re: [EXTERNAL] HILCORP ARIZONA JICARILLA #6 CBL

Good Afternoon,

Attached is the CBL for the Arizona Jicarilla #6 API 3003905699 with an estimated TOC @ ~2850'

We propose the following amendment to our procedure:

- Pump an inside only plug on the Ojo Alamo
  - 12 sx from 2894-3044'

We will then proceed with the procedure as referenced in the approved NOI.

Thanks,
Whitney Majetich
Cell: (281) 467-2130

From: Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>
Sent: Thursday, July 30, 2026 3:26 PM
To: Whitney Majetich <Whitney.Majetich@hilcorp.com>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Paula Routt - (C) <Paula.Routt@hilcorp.com>; Rennick, Kenneth G <krennick@blm.gov>; Garcia, John, EMNRD <johna.garcia@emnrd.nm.gov>; Diers, William B <wdiers@blm.gov>
Subject: FW: [EXTERNAL] HILCORP ARIZONA JICARILLA #6 CBL

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 611260

CONDITIONS

Operator: HILCORP ENERGY COMPANY 1111 Travis Street Houston, TX 77002	OGRID: 372171
	Action Number: 611260
	Action Type: [C-103P] Sub. Plugging (C-103P)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	None	8/5/2026
