Received by OCD: 8/28/2026 10:54:57 AM

U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Sundry Print Report

08/28/2026

Well Name: WOOD

Well Location: T30N / R11W / SEC 35 / SWNE / 36.771609 / -107.957454

County or Parish/State: SAN JUAN / NM

Well Number: 2R

Type of Well: CONVENTIONAL GAS WELL

Allottee or Tribe Name:

Lease Number: NMSF079962

Unit or CA Name:

Unit or CA Number: NMNM99495

US Well Number: 3004529753

Operator: HILCORP ENERGY COMPANY

Subsequent Report

Sundry ID: 2930389

Type of Submission: Subsequent Report

Type of Action: Plug and Abandonment

Date Sundry Submitted: 08/28/2026

Time Sundry Submitted: 10:14

Date Operation Actually Began: 08/24/2026

Actual Procedure: Hilcorp Energy Company plugged and abandoned the subject well on 8/26/2026 per the attached daily reports.

SR Attachments

Actual Procedure

WOOD_2R_P_A_SR_20260828101414.pdf

CONFIDENTIAL

Released to Imaging: 9/1/2026 8:12:36 AM

Well Name: WOOD

Well Location: T30N / R11W / SEC 35 / SWNE / 36.771609 / -107.957454

County or Parish/State: SAN JUAN / NM

Well Number: 2R

Type of Well: CONVENTIONAL GAS WELL

Allottee or Tribe Name:

Lease Number: NMSF079962

Unit or CA Name:

Unit or CA Number: NMNM99495

US Well Number: 3004529753

Operator: HILCORP ENERGY COMPANY

Operator

I certify that the foregoing is true and correct. Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction. Electronic submission of Sundry Notices through this system satisfies regulations requiring a

Operator Electronic Signature: TAMMY JONES

Signed on: AUG 28, 2026 10:14 AM

Name: HILCORP ENERGY COMPANY

Title: Regulatory Compliance Specialist

Street Address: 382 ROAD 3100

City: AZTEC **State:** NM

Phone: (505) 324-5185

Email address: TAJONES@HILCORP.COM

Field

Representative Name:

Street Address:

City: **State:** **Zip:**

Phone:

Email address:

BLM Point of Contact

BLM POC Name: KENNETH G RENNICK

BLM POC Title: Petroleum Engineer

BLM POC Phone: 5055647742

BLM POC Email Address: krennick@blm.gov

Disposition: Accepted

Disposition Date: 08/28/2026

Signature: Kenneth Rennick

CONFIDENTIAL

WOOD 2R 30.045.29753 PLUG AND ABANDONMENT

8/24/2026 - HELD PJSM. MOVE P&A PKG TO LOC. LOTO. SPOT EQUIP. RU P&A PKG. CK PSI; TBG-65#, CSG-65#, BH-35#. BDW 20 MINS. FT BOP. SWAP EQUIP FOR COIL TBG. KILL WELL W/ 20 BBLS FW. KEEP PUMPING A SMALL TRICKLE OF WATER DOWN BACK SIDE. RU OVER SHOT. LATCH 1.75''CT. REMOVE CT HEAD. STRIP ON BOP. RU RF & CT CUTTER. LD CT. CUT CT IN 31' SECTIONS. LD 72 PIECES OF 1.75'' CT. RD CT EQUIP. RU 1.25'' EQUIP. SIW, SDFN.

8/25/2026 – HELD PJSM. SERVICE & START EQUIP. CK PSI; TBG-0#, CSG-65#, BH-10#, BDW 10 MINS. JSA RU TWG. RIH W/ 3.5'' GR TO 2200'. LD GR. RIH W/ 3.5'' CR & SET @ 2178' LD SETTING TOOLS. RD WL. TALLY, RABBIT & PUP. RIH W/ STINGER. TAG CR @ 2178'. PUMP 40 BBLS. NO CIRC EST. PUMP BELOW CR & EST A RATE OF 2.4 BPM @ 400#. **PLUG #1 FROM 2288' - 2178' M&P 10 SKS CLASS G, 15.8PPG, 1.15YIELD, 2.0BLSRY, 1.1MIX, 4.DIS, DIS ALL CMT BELOW CR.** RU TWG. RIH W/ CIBP & SET @ 2175'. RD WL. TIH OED. PUMP 29 BBLS TO EST CIRC. PUMP 40 TOTAL. PSI TEST CSG TO 600# PSI. TEST. TOOH. JSA. RU TWG. RIH W/ CBL TOOL. LOG WELL FROM 2175' TO SURF. LD CBL TOOL. RD WL. TIH W/ TS TO TOP OF CIBP. **PLUG #1A FROM 2178' - 1703' M&P 20 SKS CLASS G, 15.8PPG, 1.15YIELD, 4.0BLSRY, 2.3MIX, 2.7DIS**, LD TOC. TOOH. SIW, SDFN. WOC. **(BLM REP JIMMY DOBSON)**

8/26/2026 – HELD PJSM. SERVICE & START EQUIP. CK PSI; TBG-0#, CSG-0#, BH-5#, BDW 1 MIN. **TIH TAG TOC @ 1725'. (BLM REP APPROVED TAG)** PSI TEST CSG TO 600# FOR 30 MINS. TEST OK. LD TBG TO PLUG #2. **PLUG #2 FROM 1051'- 721' (3.5') M&P 14 SKS CLASS G, 15.8PPG, 1.15YIELD. 2.8BLSRY, 1.6MIX,** 1.3DIS. LD TOC. LD ALL TBG. JSA RU WL. RIH W/ TG & PERF @ 155'. PUMP 19 BBLS TO EST CIRC. PUMP 30 TOTAL. RD WL. PUP TO 196'. **PLUG #3 FROM 196'- 0' (3.5' X 7'') M&P 173 SKS CLASS G, 15.8PPG, 1.15YIELD. 35.4BLSRY, 20MIX, CIRC CMT TO SURF.** SIW. WOC. RD RF & TBG EQUIP. ND BOP. NU WH. DIG OUT WH. MONITOR WH PSI. BUBBLE TEST BH. TEST OK CUT & REMOVE WH. FIND TOC @ SURF. WELD & INSTALL DHMP @ 36.7716 / -107.95743. TOP OFF CELLAR W/ 13 SKS CLASS G 15.8PPG, 1.15YIELD. RD P&A PKG. RIG RELEASED @ 15:00 ON 8/26/2026. **(BLM REP JIMMY DOBSON)**

WELL PLUGGED AND ABANDONED ON 08/26/2026

From: Diede, Loren, EMNRD <Loren.Diede@emnrd.nm.gov>
Sent: Wednesday, August 26, 2026 8:52 AM
To: Whitney Majetich; Rennick, Kenneth G; Oscar Sanchez - (C); Priscilla Shorty; Garcia, John, EMNRD; Farmington Regulatory Techs; Dobson, Jimmie P
Subject: RE: [EXTERNAL] Hilcorp - CBL WOOD 2R - Proposed Procedure Adjustment

CAUTION: External sender. DO NOT open links or attachments from UNKNOWN senders.

NMOCD agrees with this change
\Loren

From: Whitney Majetich <whitney.majetich@hilcorp.com>
Sent: Wednesday, August 26, 2026 8:30 AM
To: Rennick, Kenneth G <krennick@blm.gov>; Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Garcia, John, EMNRD <JohnA.Garcia@emnrd.nm.gov>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Dobson, Jimmie P <jdobson@blm.gov>; Diede, Loren, EMNRD <Loren.Diede@emnrd.nm.gov>
Subject: Re: [EXTERNAL] Hilcorp - CBL WOOD 2R - Proposed Procedure Adjustment

Thanks Kenny,

Does the EMNRD approve of the following as well?

Thanks,
Whitney Majetich
Cell: (281) 467-2130

From: Rennick, Kenneth G <krennick@blm.gov>
Sent: Wednesday, August 26, 2026 8:29 AM
To: Whitney Majetich <whitney.majetich@hilcorp.com>; Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Garcia, John, EMNRD <johna.garcia@emnrd.nm.gov>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Dobson, Jimmie P <jdobson@blm.gov>
Subject: Re: [EXTERNAL] Hilcorp - CBL WOOD 2R - Proposed Procedure Adjustment

CAUTION: External sender. DO NOT open links or attachments from UNKNOWN senders.

The BLM finds the procedure appropriate.

Kenny Rennick

Get Outlook for iOS

From: Whitney Majetich <whitney.majetich@hilcorp.com>
Sent: Wednesday, 26 August 2026 07:10:22
To: Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Rennick, Kenneth G <krennick@blm.gov>; Garcia, John, EMNRD <johna.garcia@emnrd.nm.gov>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Dobson, Jimmie P <jdobson@blm.gov>
Subject: [EXTERNAL] Hilcorp - CBL WOOD 2R - Proposed Procedure Adjustment

This email has been received from outside of DOI - Use caution before clicking on links, opening attachments, or responding.

Good morning,

The CBL attached for the WOOD 2R, API 300452975300 shows an estimated TOC of ~ 160'.

We propose the following amendment to the procedure:

- Continue with Plug 2 as designed per COA's
  - 13sx cmt from 757-1051'
- We propose to Perforate @ 155' given the est TOC on the CBL
- Pump Plug #3 from 155- surface covering the surface casing shoe @ 140'
  - 22sx Circulated behind csg to surface
  - 7sx inside production casing to surface

Attached I the approved NOI for refernce

Thanks,
Whitney Majetich
Cell: (281) 467-2130

From: Oscar Sanchez - (C) <oscar.sanchez@hilcorp.com>
Sent: Tuesday, August 25, 2026 5:07 PM
To: Whitney Majetich <Whitney.Majetich@hilcorp.com>; Priscilla Shorty <pshorty@hilcorp.com>; Rennick, Kenneth G <krennick@blm.gov>; Garcia, John, EMNRD <johna.garcia@emnrd.nm.gov>; Farmington Regulatory Techs <FarmingtonRegulatoryTechs@hilcorp.com>; Dobson, Jimmie P <jdobson@blm.gov>
Subject: CBL WOOD 2R

Oscar Sanchez
Wellsite Supervisor
505-608-9185
Oscar.Sanchez@Hilcorp.com

WOOD 2R 30.045.29753 PLUG AND ABANDONMENT



WOOD 2R **30.045.29753** **PLUG AND ABANDONMENT**



Hilcorp Energy Company

Current Schematic - Version 3


Well Name: WOOD #2R

API / UWI	Surface Legal Location	Field Name	Route	State/Province	Well Configuration Type
3004529753	035-030N-011W-G	Area 07	0701	NEW MEXICO	Vertical
Ground Elevation (ft)	**Original KB/RT Elevation (ft)**	**Tubing Hanger Elevation (ft)**	**RKB to GL (ft)**	**KB-Casing Flange Distance (ft)**	**KB-Tubing Hanger Distance (ft)**
5,846.00	5,846.00		0.00		

Tubing Strings

Run Date	Set Depth (ftKB)	String Max Nominal OD (in)	String Min Nominal ID (in)	Weight/Length (lb/ft)	Original Spud Date
8/11/1999 00:00	2,240.00	1.9			4/6/1999 14:45

Original Hole, 30045297530000 [Vertical]

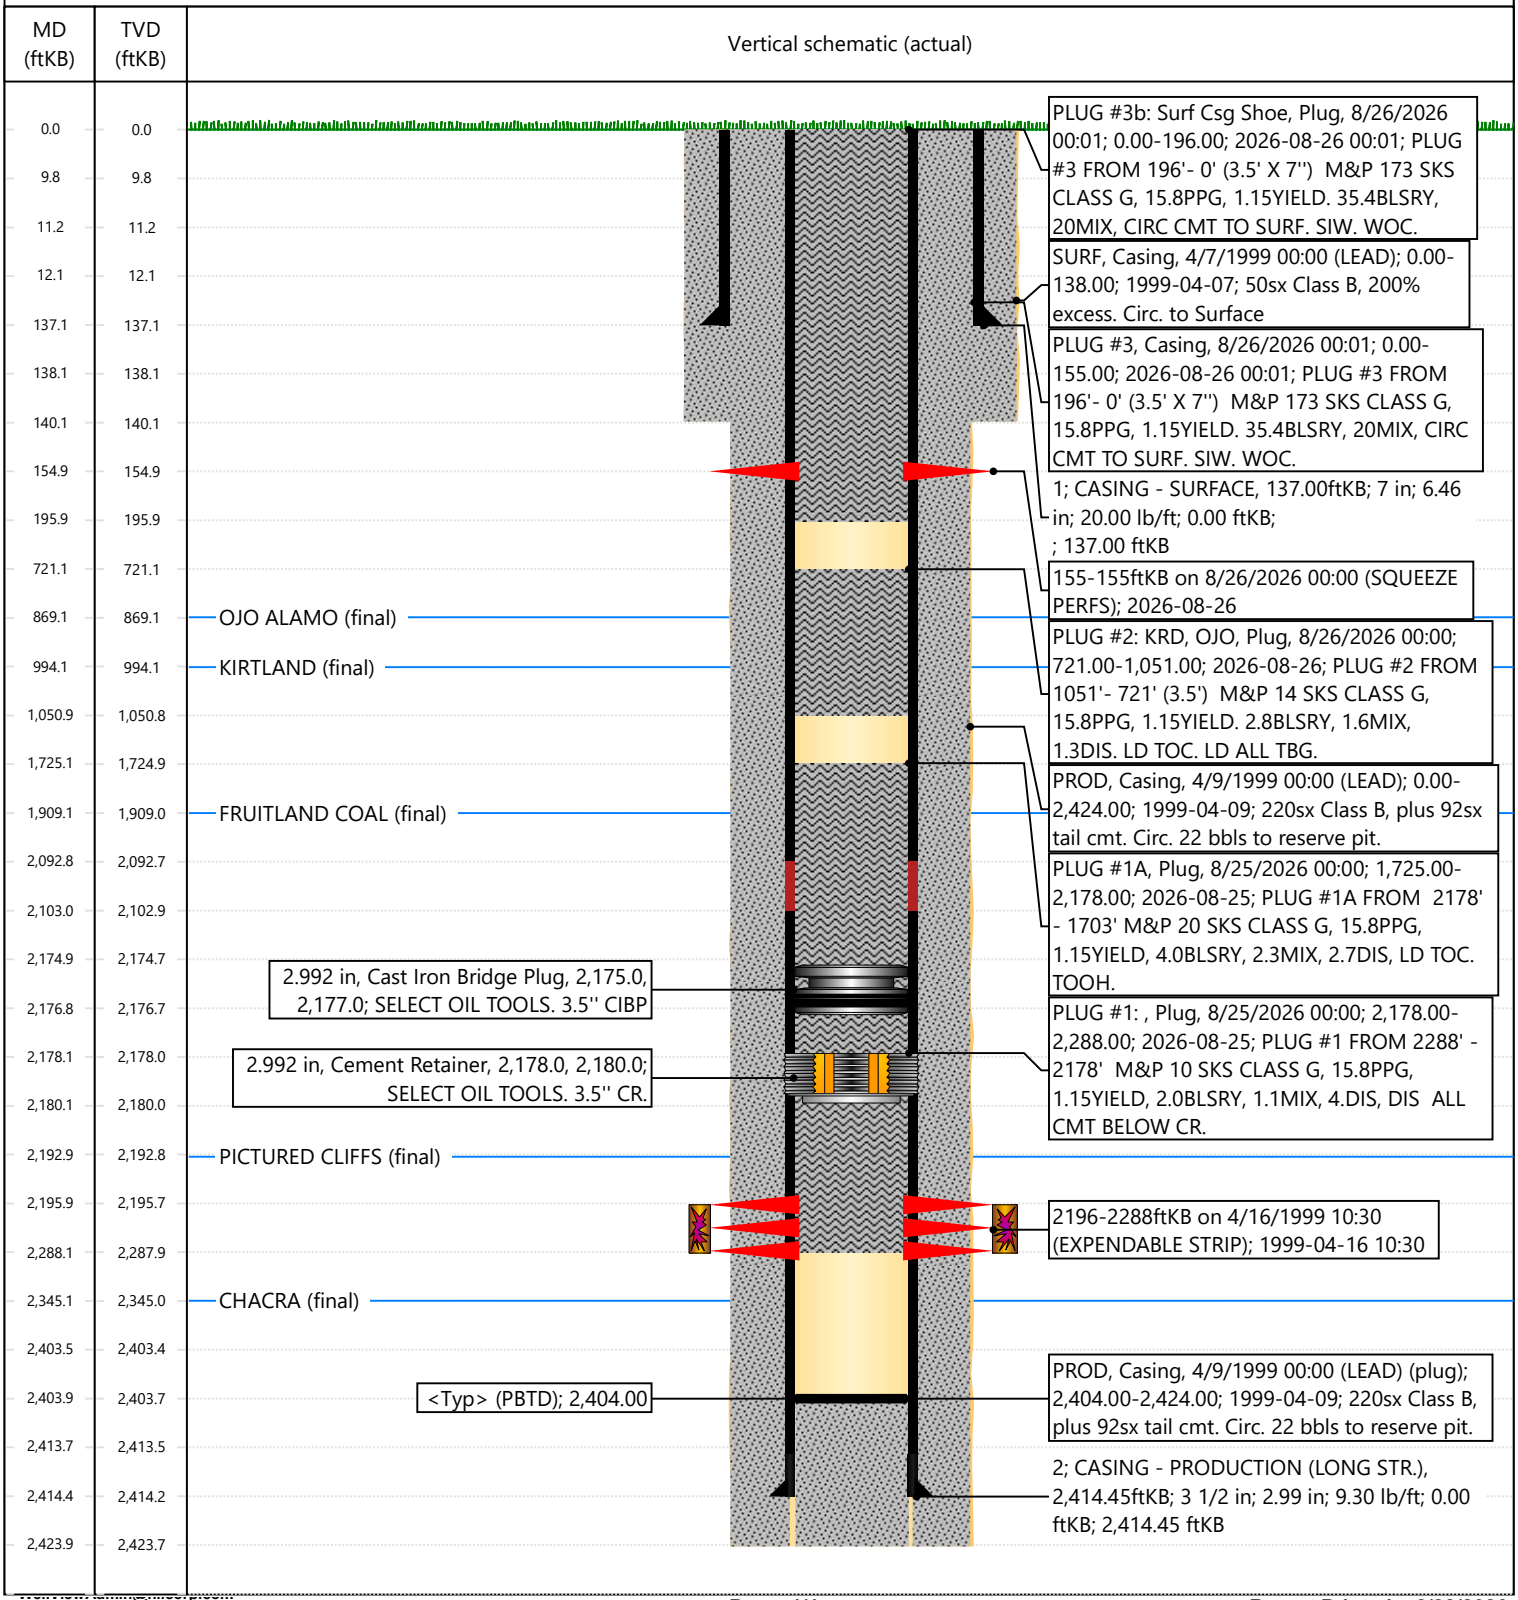

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 618760

CONDITIONS

Operator: HILCORP ENERGY COMPANY 1111 Travis Street Houston, TX 77002	OGRID: 372171
	Action Number: 618760
	Action Type: [C-103P] Sub. Plugging (C-103P)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	None	9/1/2026
