Submit 1 Copy To Appropriate District Office
District I – (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II – (575) 748-1283
811 S. First St., Artesia, NM 88210
District III – (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV – (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-103
Revised July 18, 2013

WELL API NO.
30-005-00054

5. Indicate Type of Lease
STATE ☒ FEE ☐

6. State Oil & Gas Lease No.

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)

7. Lease Name or Unit Agreement Name
Pre Ongard (Elks)

1. Type of Well: Oil Well ☒ Gas Well ☐ Other

8. Well Number: 001

2. Name of Operator
Pre-Ongard

9. OGRID Number:

3. Address of Operator

10. Pool name or Wildcat

4. Well Location
Unit Letter: K : 1670 feet from the S line and 2231 feet from the W line
Section 22 Township 10S Range 25E NMPM County: Chaves

11. Elevation *(Show whether DR, RKB, RT, GR, etc.)*

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:				SUBSEQUENT REPORT OF:			
PERFORM REMEDIAL WORK	☐	PLUG AND ABANDON	☐	REMEDIAL WORK	☐	ALTERING CASING	☐
TEMPORARILY ABANDON	☐	CHANGE PLANS	☐	COMMENCE DRILLING OPNS.	☐	P AND A	☒
PULL OR ALTER CASING	☐	MULTIPLE COMPL	☐	CASING/CEMENT JOB	☐		
DOWNHOLE COMMINGLE	☐						
CLOSED-LOOP SYSTEM	☐						
OTHER:	☐			OTHER:			☐

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

See Plugging Procedure/Events Below

Spud Date: Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Ethan Wakefield TITLE: Authorized Representative DATE: 9-29-26

Type or print name: Ethan Wakefield E-mail address: e.wakefield@dwsrigs.com PHONE: (405)343-7736

For State Use Only

APPROVED BY:_____TITLE_____DATE_____
Conditions of Approval (if any):

Plug And Abandonment End Of Well Report

Elks #001 (Pre-Ongard Well #001)

1670' FSL & 2231' FWL, Section 22, 10S, 25E

Chaves County, NM / API 30-005-00054

Work Summary:

10/2/23 Made BLM and NMOCD P&A operations notifications at 9:00 AM MST.

10/3/23 Arrived on location and held safety meeting. Rig crew and backhoe worked on location.

10/4/23 Arrived on location and held safety meeting. Continued to move dirt to make a location for the rig. Waited for parts and equipment.

10/5/23 Arrived on location and held safety meeting. Continued building location.

10/6/23 Arrived on location and held safety meeting. Set up beams and boards for the rig. Spotted rig and equipment. Waited on more boards. Unable to R/U base beam due to soft location. Waiting for more boards.

10/7/23 Arrived on location and held safety meeting. Finished setting boards for the rig. R/U packer and BHA. Cutoff frac valve. Ran packer in hole. Felt drag at 560', L/D one joint and set packer at 530'. R/U clinch set seating valve. R/U cementing services. Used cement pump to set packer. TOOH. Secured and shut down well.

10/8/23 Arrived on location and held safety meeting. R/U wireline services. RIH and logged well. POOH. R/D wireline services. Waited on further instruction.

10/9/23 Arrived on location and held safety meeting. Waited on welder. Cut off casing and welded on a T with a 6" butterfly valve and a 7" swedge.

10/10/23 Arrived on location and held safety meeting. Checked wellbore pressures. Bled down well. R/U camera for PVACD. RIH to top of packer at 530'. R/D camera. Shut down secure well shut down for the day. Wait on orders.

10/11/23 Arrived on location and held safety meeting. Recorded wellbore pressures. Bled down well. TIH to top of inflatable packer at 530'. R/U cementing services and pumped plug from 530' to surface to cover the inflatable packer and surface casing shoe. L/D tubing. R/D floor, tongs, slips. Welder cut off wellhead. R/U cementers and topped off the cellar. Took picture of Coordinates. RDMOL.

Plug Summary:

Plug #1: (Packer and Surface Casing Shoe, 120 Sacks Type I/II Cement)

R/U packer and BHA. Cutoff frac valve. Ran packer in hole. Felt drag at 560', L/D one joint and set packer at 530'. R/U clinch set seating valve. R/U cementing services. Used cement pump to set packer. TOOH. TIH to top of inflatable packer at 530'. R/U cementing services and pumped plug from 530' to surface to cover the inflatable packer and surface casing shoe. L/D tubing. R/D floor, tongs, slips. Welder cut off wellhead. R/U cementers and topped off the cellar. RDMOL.

Completed Wellbore Diagram

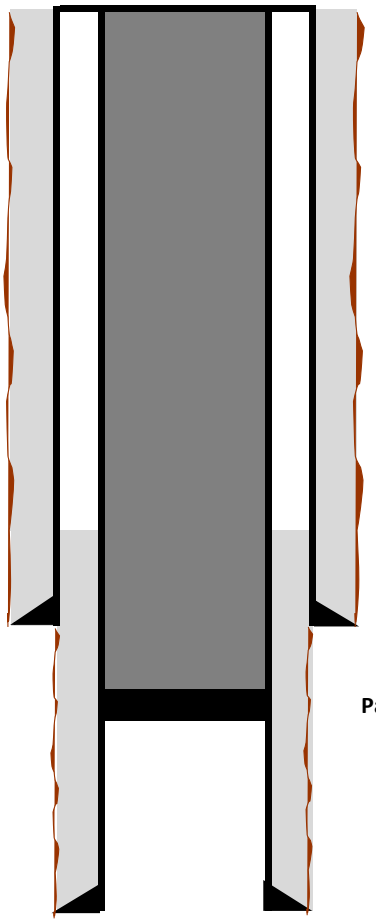
Pre-Ongard
Elks #001
API: 30-005-00054
Chaves County, New Mexico

Surface Casing

8.625" 24# @ 420 ft
OH: 10-1/4"

Plug 1
530 feet - surface
530 foot plug
120 Sacks of Type I/II Cement

Formation



Intermediate Casing
7" 19# @ 630 feet

Packer @ 530'



Figure 1: Cut Off

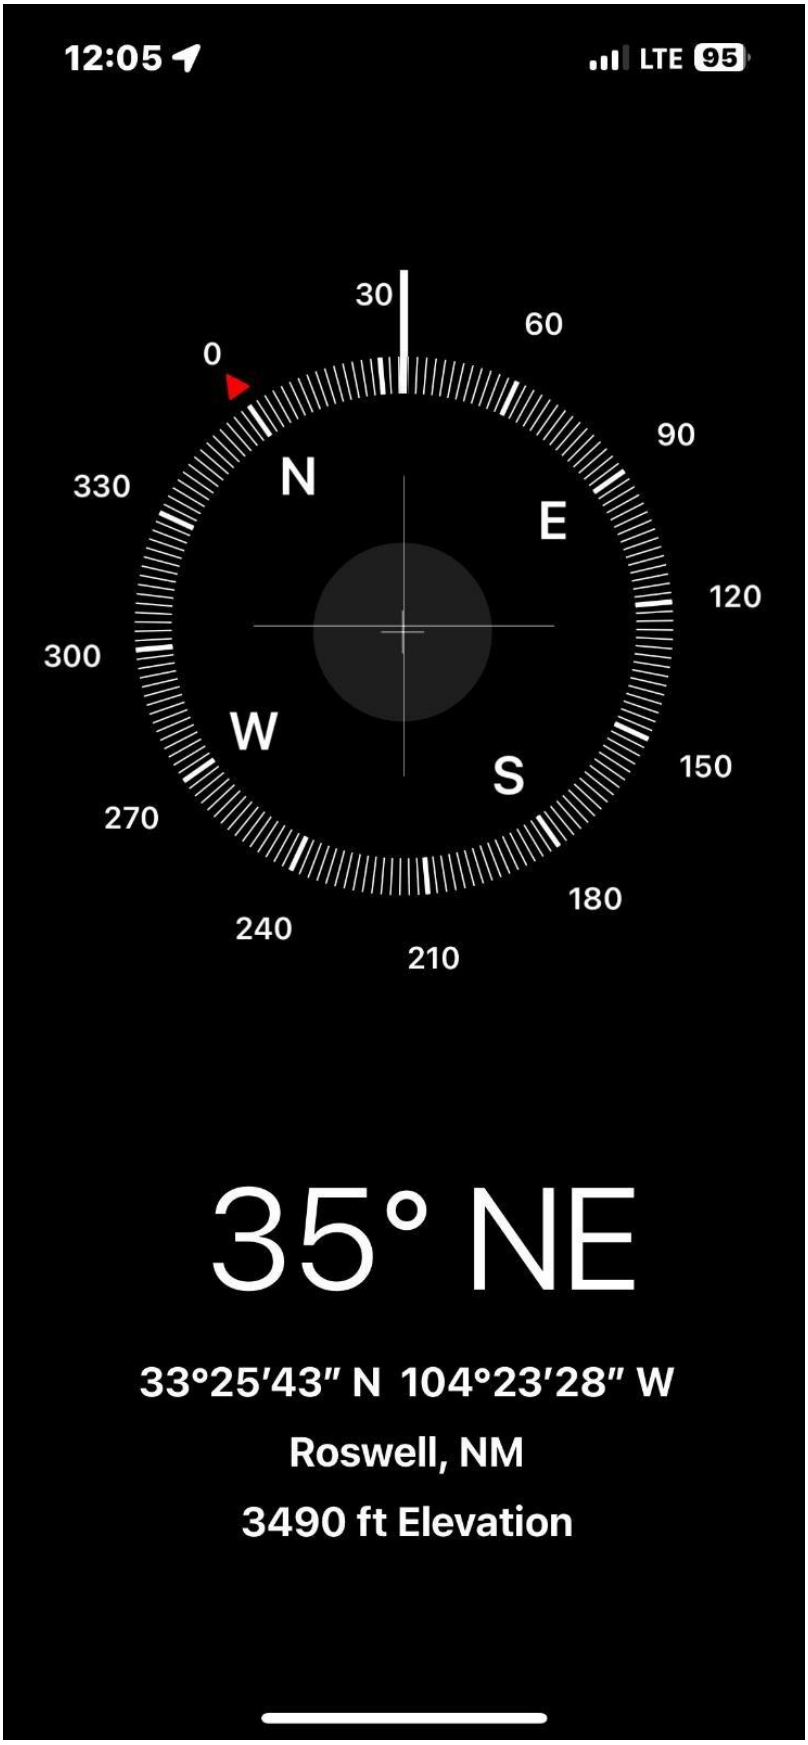

12:05
LTE 95
30
60
0
90
330
N
E
120
300
W
S
150
270
180
240
210
35° NE
33°25′43″ N 104°23′28″ W
Roswell, NM
3490 ft Elevation

Figure 2: GPS



Figure 3: Top Off

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

DEFINITIONS

Operator: J.A. Drake Well Service Inc. (OPG Vendor) 607 W. Pinon St Farmington, NM 87401	OGRID: 333581
	Action Number: 628950
	Action Type: [UF-OMA] Sub. Plugging (UF-OMA-C-103P)

DEFINITIONS

The OCD Mitigation Activity (OMA) forms are a subset of the OCD's forms exclusively designed for activities related to State of New Mexico's contracted evaluation, plugging, decommissioning, remediation, salvage and reclamation activities. Specifically, these forms are typically used where the OCD has acquired a hearing order allowing the OCD to perform mitigation activities on wells and associated facilities that no longer have an authorized or viable operator to perform the necessary work. These forms are not to be utilized for any other purpose.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

QUESTIONS

Operator: J.A. Drake Well Service Inc. (OPG Vendor) 607 W. Pinon St Farmington, NM 87401	OGRID: 333581
	Action Number: 628950
	Action Type: [UF-OMA] Sub. Plugging (UF-OMA-C-103P)

QUESTIONS

Prerequisites	
[OGRID] Well Operator	**[214263] PRE-ONGARD WELL OPERATOR**
[API] Well Name and Number	**[30-005-00054] PRE-ONGARD WELL #001**
Well Status	**Plugged (site released)**

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 628950

CONDITIONS

Operator: J.A. Drake Well Service Inc. (OPG Vendor) 607 W. Pinon St Farmington, NM 87401	OGRID: 333581
	Action Number: 628950
	Action Type: [UF-OMA] Sub. Plugging (UF-OMA-C-103P)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	This corrected C-103 replaces # 278697 dated 12-23-2023	9/30/2026
