Submit 1 Copy To Appropriate District Office
District I – (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II – (575) 748-1283
811 S. First St., Artesia, NM 88210
District III – (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV – (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-103
Revised July 18, 2013

WELL API NO. 30-015-23712

5. Indicate Type of Lease STATE ☑ FEE ☐

6. State Oil & Gas Lease No.

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)

7. Lease Name or Unit Agreement Name: AURORA

1. Type of Well: Oil Well ☑ Gas Well ☐ Other

8. Well Number #001

2. Name of Operator: OXY USA INC.

9. OGRID Number: 16696

3. Address of Operator: 5 GREENWAY PLAZA, SUTIE 110, HOUSTON, TX 77046

10. Pool name or Wildcat: TURKEY TRACK; 7 RVRS-QU-GB-SA

4. Well Location
Unit Letter A : 990 feet from the NORTH line and 330 feet from the EAST line
Section 3 Township 19S Range 29E NMPM EDDY County

11. Elevation *(Show whether DR, RKB, RT, GR, etc.)*

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:				SUBSEQUENT REPORT OF:			
PERFORM REMEDIAL WORK	☐	PLUG AND ABANDON	☐	REMEDIAL WORK	☐	ALTERING CASING	☐
TEMPORARILY ABANDON	☐	CHANGE PLANS	☐	COMMENCE DRILLING OPNS.	☐	P AND A	☑
PULL OR ALTER CASING	☐	MULTIPLE COMPL	☐	CASING/CEMENT JOB	☐		
DOWNHOLE COMMINGLE	☐						
CLOSED-LOOP SYSTEM	☐						
OTHER:	☐			OTHER:			☐

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

This well is plugged. Job start: 09/16/26. Job complete: 09/22/26. Well cut and capped 10/28/26. See the attached daily plugging job summary, plugged wellbore diagram and marker pictures for reference.

Spud Date: | Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Leslie Reeves TITLE REGULATORY MANAGER DATE 11/04/26

Type or print name LESLIE REEVES E-mail address: LESLIE_REEVES@OXY.COM PHONE: 713-497-2492

For State Use Only

APPROVED BY: TITLE DATE

Conditions of Approval (if any):

AURORA # 001
30-015-23712 PA SR JOB SUMMARY

09/16/26 MIRU. POOH WITH PUMP AND RODS.

09/17/26 NDWH, NUBOP. POOH WITH 2-3/8" TUBING. RIH W/ GUAGE RING TO 2080'. POOH. RIH AND SET CIBP @ 2062'. TAGGED. PULLED UP TO 2050', CIRC AND ATTEMPTED TO PSI TEST. DIDN'T TEST. RAN CBL F/ 2062' TO SURFACE.

09/18/26 RIH AND SET PKR @ 2059'. EOT @ 2056', PUMPED 25SX CL C CMT ON TOP OF CIBP. WOC.

09/19/26 RIH AND TAGGED TOC @ 1629'. CONFIRMED WITH NMOCD. PULLED UP, EOT @ 1610'. PUMPED 25SX CL C CMT. WOC. RIH AND TAGGED TOC @ 1294'. CONFIRMED WITH NMOCD. RIH AND SET PKR @ 395'. PSI TESTED TO 500PSI F/ 30 MIN, TEST HELD. RIH AND PERF'D @ 1075'. ESTABLISHED AN INJ RATE. SQUEEZED 160SX CL C CMT. WOC.

09/21/26 RIH AND TAGGED TOC @ 687'. RIH AND PERF'D @ 370'. ESTABLISHED INJ RATE BUT DID NOT CIRC TO SURFACE. CONFIRMED PLAN WITH NMOCD. SQUEEZED 25SX CLASS C CEMENT. WOC. RIH AND TAGGED TOC @ 370'. RIH AND SQUEEZED ANOTHER 25 SX CLASS C CMT. WOC.

09/22/26 RIH AND TAGGED TOC @ 240'. RIH AND PERF'D @ 200'. SQUEEZED 75SX CL C CMT TO SURFACE. WOC. VERIFIED CEMENT TO SURFACE. RDMO.

10/28/26 WELL CUT AND CAPPED.

API#:	30-015-23712
Lease Name:	Aurora
Well No:	1
County:	Eddy
Location:	Section 3, T19S, R29E, Unit A
Section Lines:	990' FNL & 330' FEL
RKB Elevation:	-
DF Elevation:	-
Ground Elevation:	3,421
Date Drilled:	May-81

Plugged Wellbore

PERF'D @ 200'. SQZD 75SX CL C CMT TO SUFRACE. VERIFIED.

PERF'D @ 370'. SQZD 25SX CL C CMT. WOC. TAGGED TOC @370'. SQZD ANOTHER 25 SX CL C CMT. TAGGED TOC @ 240'.


PERF'D @ 1075'. SQZD 160SX CL C CMT. WOC. TAGGED TOC @ 687'.

EOT @ 1610'. PUMPED 25SX CL C CMT. WOC. TAGGED TOC @ 1294'.

SET CIBP @ 2062'. TAGGED. PUMPED 25SX CMT F/ 2056'. WOC. TAGGED TOC @ 1629'.

Perforations (ft)

Queen	2,120	to	2,140
Grayburg	2,210	to	2,878



8-5/8" Grouted to Surface w/ 8 yds Redimix

Surface Casing

8 5/8 "	24#	-	-	@	320	
12 1/4 "	Hole		TOC	@	Surface	Calculated
			cmt'd	w/	300	sks

10 PPG Plug Mud Between Plugs

RBP between Queen & Grayburg (18 Apr 2016)
Actual Setting Depth unknown - assume ~ 2,150'

Production Casing

4 1/2 "	10.5#	-	-	@	3,008	
7 7/8 "	Hole		TOC	@	265	Calculated
			cmt'd	w/	450	sks

TD @	**3,008**	**TVD**
TD @	**3,008**	**TMD**
PBTD @	**2,959**	**TVD**
PBTD @	**2,959**	**TMD**

Aurora #001 30-015-23712

32.69418, -104.05496



Photo 1 of 7

Aurora #001 30-015-23712

32.69418, -104.05496



Photo 2 of 7

Aurora #001 30-015-23712

32.69418, -104.05496



Photo 3 of 7

Aurora #001 30-015-23712


32.69418, -104.05496



Photo 4 of 7

Aurora #001 30-015-23712

32.69418, -104.05496

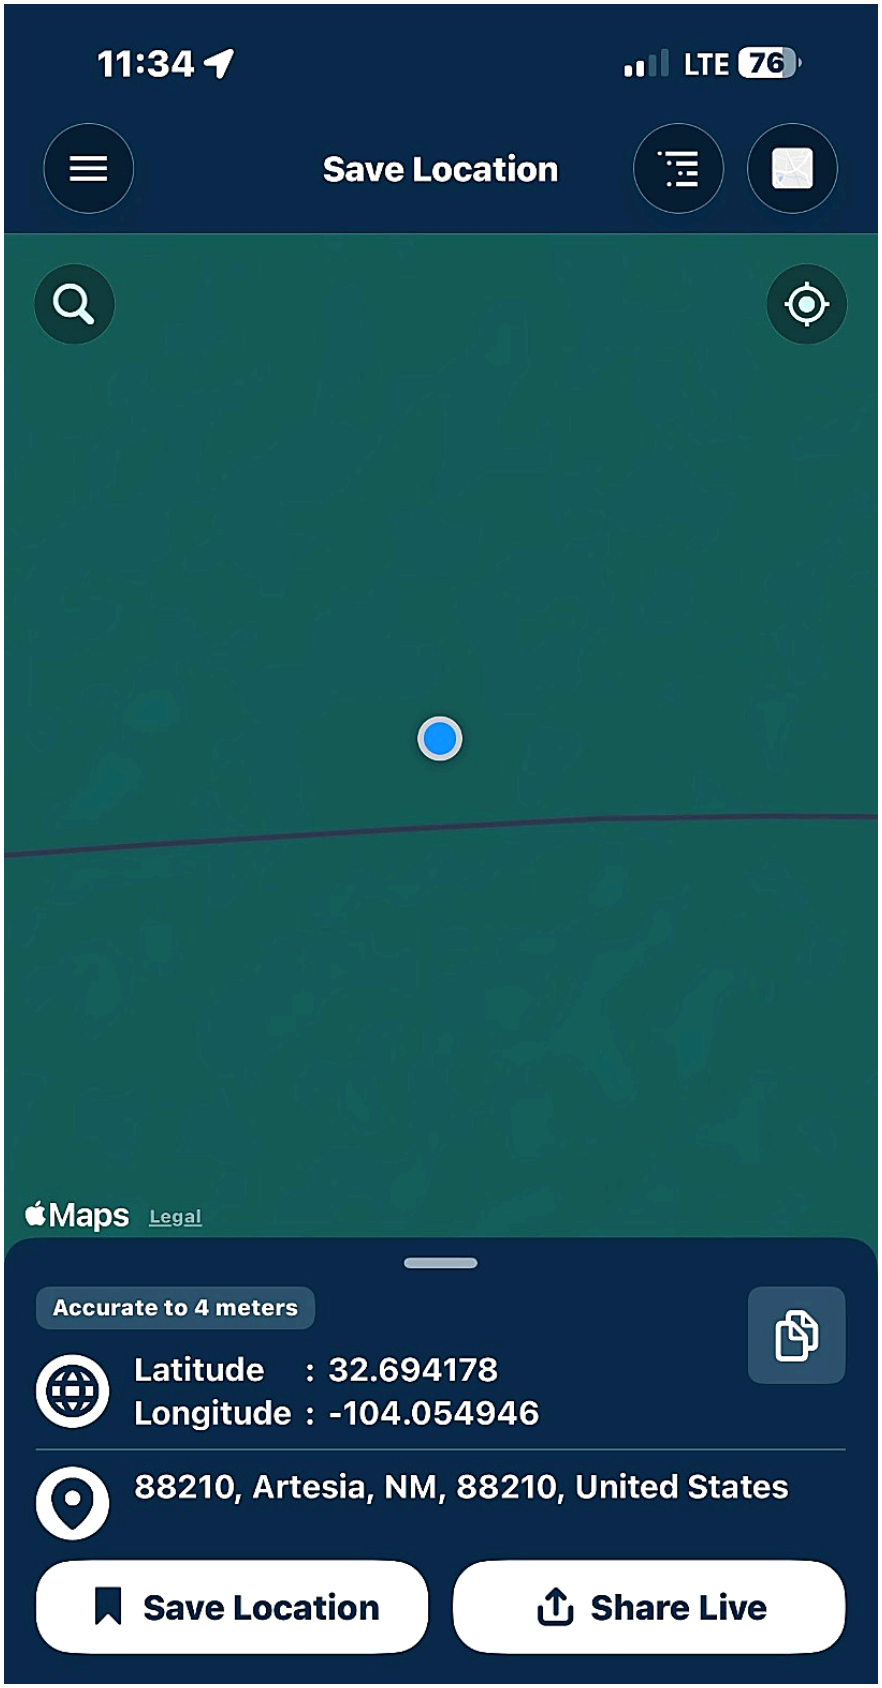

Aurora #001 30-015-23712

32.69418, -104.05496



Photo 6 of 7

Aurora #001 30-015-23712

32.69418, -104.05496



Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
https://www.emnrd.nm.gov/ocd/contact-us

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Operator: OXY USA INC P.O. Box 4294 Houston, TX 772104294	OGRID: 16696
	Action Number: 639403
	Action Type: [C-103P] Sub. Plugging (C-103P)

CONDITIONS

Created By	Condition	Condition Date
loren.diede	None	11/6/2026
