MACK

Energy Corporation

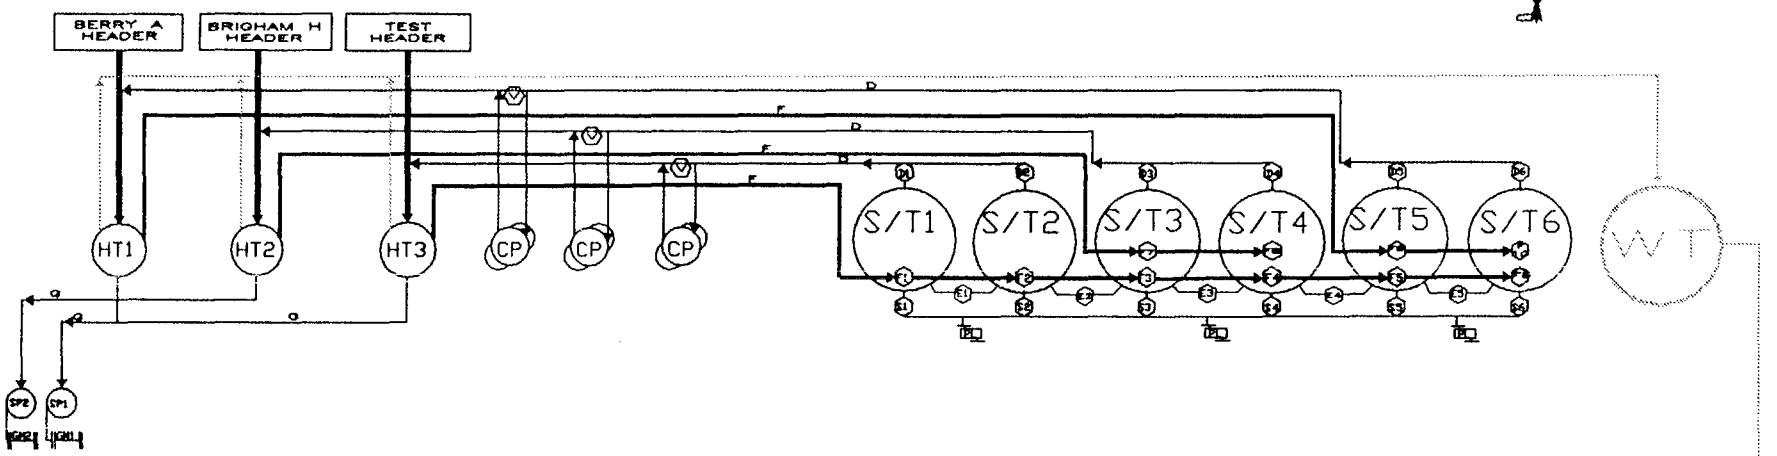

Fill Valves F3,F4,F5,F6, will be closed at all Times

Equilizer Valves E2,E4 will be Closed at all Times

Production Phase

Berry A Federal Battery		Brigham H Battery		Test Battery	
S/T 5	S/T 6	S/T 3	S/T 4	S/T 1	S/T 2
F9 Open	F9 Closed	F3 Open	F3 Closed	F1 Open	F1 Closed
D9 Open	D9 Closed	D3 Open	D3 Closed	D1 Open	D1 Closed
E5 Open	E6 Open	E3 Open	E3 Open	E1 Open	E1 Open
S5 Closed	S6 Closed	S3 Closed	S3 Closed	S1 Closed	S1 Closed
F10 Closed	F10 Open	F4 Closed	F4 Open	F2 Closed	F2 Open
D6 Closed	D6 Open	D4 Closed	D4 Open	D2 Closed	D2 Open
S6 Closed	S6 Closed	S4 Closed	S4 Closed	S2 Closed	S2 Closed

Sales Phase

Berry A Federal Battery		Brigham H Federal Battery		Test Battery	
S/T 5	S/T 6	S/T 3	S/T 4	S/T 1	S/T 2
F9 Closed	F9 Open	F3 Closed	F3 Open	F1 Closed	F1 Open
D9 Closed	D9 Open	D3 Closed	D3 Open	D1 Closed	D1 Open
E5 Closed	E6 Closed	E3 Closed	E3 Closed	E1 Closed	E1 Closed
S5 Open	S6 Closed	S3 Open	S3 Closed	S1 Open	S1 Closed
F10 Open	F10 Closed	F4 Open	F4 Closed	F2 Open	F2 Closed
D6 Open	D6 Closed	D4 Open	D4 Closed	D2 Open	D2 Closed
S6 Closed	S6 Open	S4 Closed	S4 Open	S2 Closed	S2 Open

This Lease is subject to the site Security plan for southeast New Mexico operations.

The Plan is Located at :

Mack Energy Corporation
P.O. Box 960
Artesia NM 88211-0960

Mack Energy Corporation
Berry A Federal Tank Battery
Brigham H Off Lease Storage
NE/4 NW/4
Sec. 21, T17S-R30E

Berry A Federal Lease
Brigham H Lease
Test Facility
