ConocoPhillips

Schematic Regulatory

SAN JUAN 32-9 UNIT #34B

District	Field Name	County	State/Province	API / UWI
NORTH	MV/DK COM	SAN JUAN	NEW MEXICO	3004535183

Original Spud Date	Surface Legal Location	East/West Distance (ft)	East/West Reference	North/South Distance (ft)	North/South Reference
8/3/2011	035-032N-010W-K	1,329 00	FWL	2,012 00	FSL

Well Config: DEVIATED - Original Hole, 11/29/2011 8:42:01 AM

ftKB (MD)	Schematic - Actual
15	
16	3-1, Casing Hanger, 4 1/2, 4 000, 15, 1 0
16	2-1, Casing Hanger, 7, 6 366, 15, 1.5
18	1-1, Casing Hanger, 9 5/8, 9.001, 15, 3 1
18	2-2, Casing Pup Joint, 7, 6.366, 17, 2.0
25	3-2, Mandrel Casing Pup Joint, 4 1/2, 4.000, 16, 9 3
108	3-3, Casing Joints, 4 1/2, 4.000, 25, 83.1
118	3-4, Casing Pup Joint, 4 1/2, 4.000, 108, 9.7
123	3-5, Casing Pup Joint, 4 1/2, 4 000, 118, 4 5
198	1-2, Casing Joints, 9 5/8, 9 001, 18, 180.3
200	1-3, Float Collar, 9 5/8, 9.001, 198, 1.5
230	1-4, Casing Joints, 9 5/8, 9.001, 200, 30.2
231	1-5, Sawtooth Collar, 9 5/8, 9.001, 230, 0.9
236	
754	3-6, Casing Joints, 4 1/2, 4.000, 123, 631.4
797	3-7, XO (CHANGE OVER), 4 1/2, 4.000, 754, 43.4
1,413	
2,548	2-3, Casing Joints, 7, 6.366, 19, 2,529 2
2,550	2-4, Stage Tool, 7, 6 366, 2,548, 2.5
2,710	
2,770	
3,100	
3,290	
3,368	2-5, Casing Joints, 7, 6.366, 2,550, 817.7
3,369	2-6, Float Collar, 7, 6.366, 3,368, 0 9
3,412	2-7, Casing Joints, 7, 6.366, 3,369, 43.3
3,414	2-8, Float Shoe, 7, 6.366, 3,412, 1 9
3,449	
3,799	3-8, Casing Joints, 4 1/2, 4.000, 797, 3,001.2
3,808	3-9, Marker Joint, 4 1/2, 4.000, 3,799, 10.0
3,817	1-1, Tubing, 2 3/8, 1.995, 15, 7,603 3
4,004	
4,662	PERF - CLIFF HOUSE / MENEFEE UPPER, 4,662-5,040, 11/11/2011
4,970	
5,040	
5,047	
5,092	
5,386	PERF - POINT LOOKOUT, 5,092-5,679, 11/11/2011
5,679	
5,774	
6,750	
7,316	3-10, Casing Joints, 4 1/2, 4 000, 3,809, 3,507.1
7,326	3-11, Marker Joint, 4 1/2, 4.000, 7,316, 10 6
7,426	
7,480	
7,553	
7,614	
7,618	1-2, Pup Jt/ Marker, 2 3/8, 1 995, 7,618, 2.1
7,620	1-3, Tubing, 2 3/8, 1.995, 7,620, 30.5
7,637	PERF - DAKOTA, 7,553-7,731, 11/9/2011
7,651	1-4, F Nipple, 2 3/8, 1.780, 7,651, 0 8
7,652	1-5, Pump Off Bit Sub, 2 3/8, 1.995, 7,652, 0.8
7,653	
7,653	
7,731	
7,753	
7,754	3-12, Casing Joints, 4 1/2, 4 000, 7,326, 427 8
7,755	3-13, Float Collar, 4 1/2, 4.000, 7,754, 0.6
7,755	3-14, Float Shoe, 4 1/2, 4.000, 7,755, 0 8
7,775	

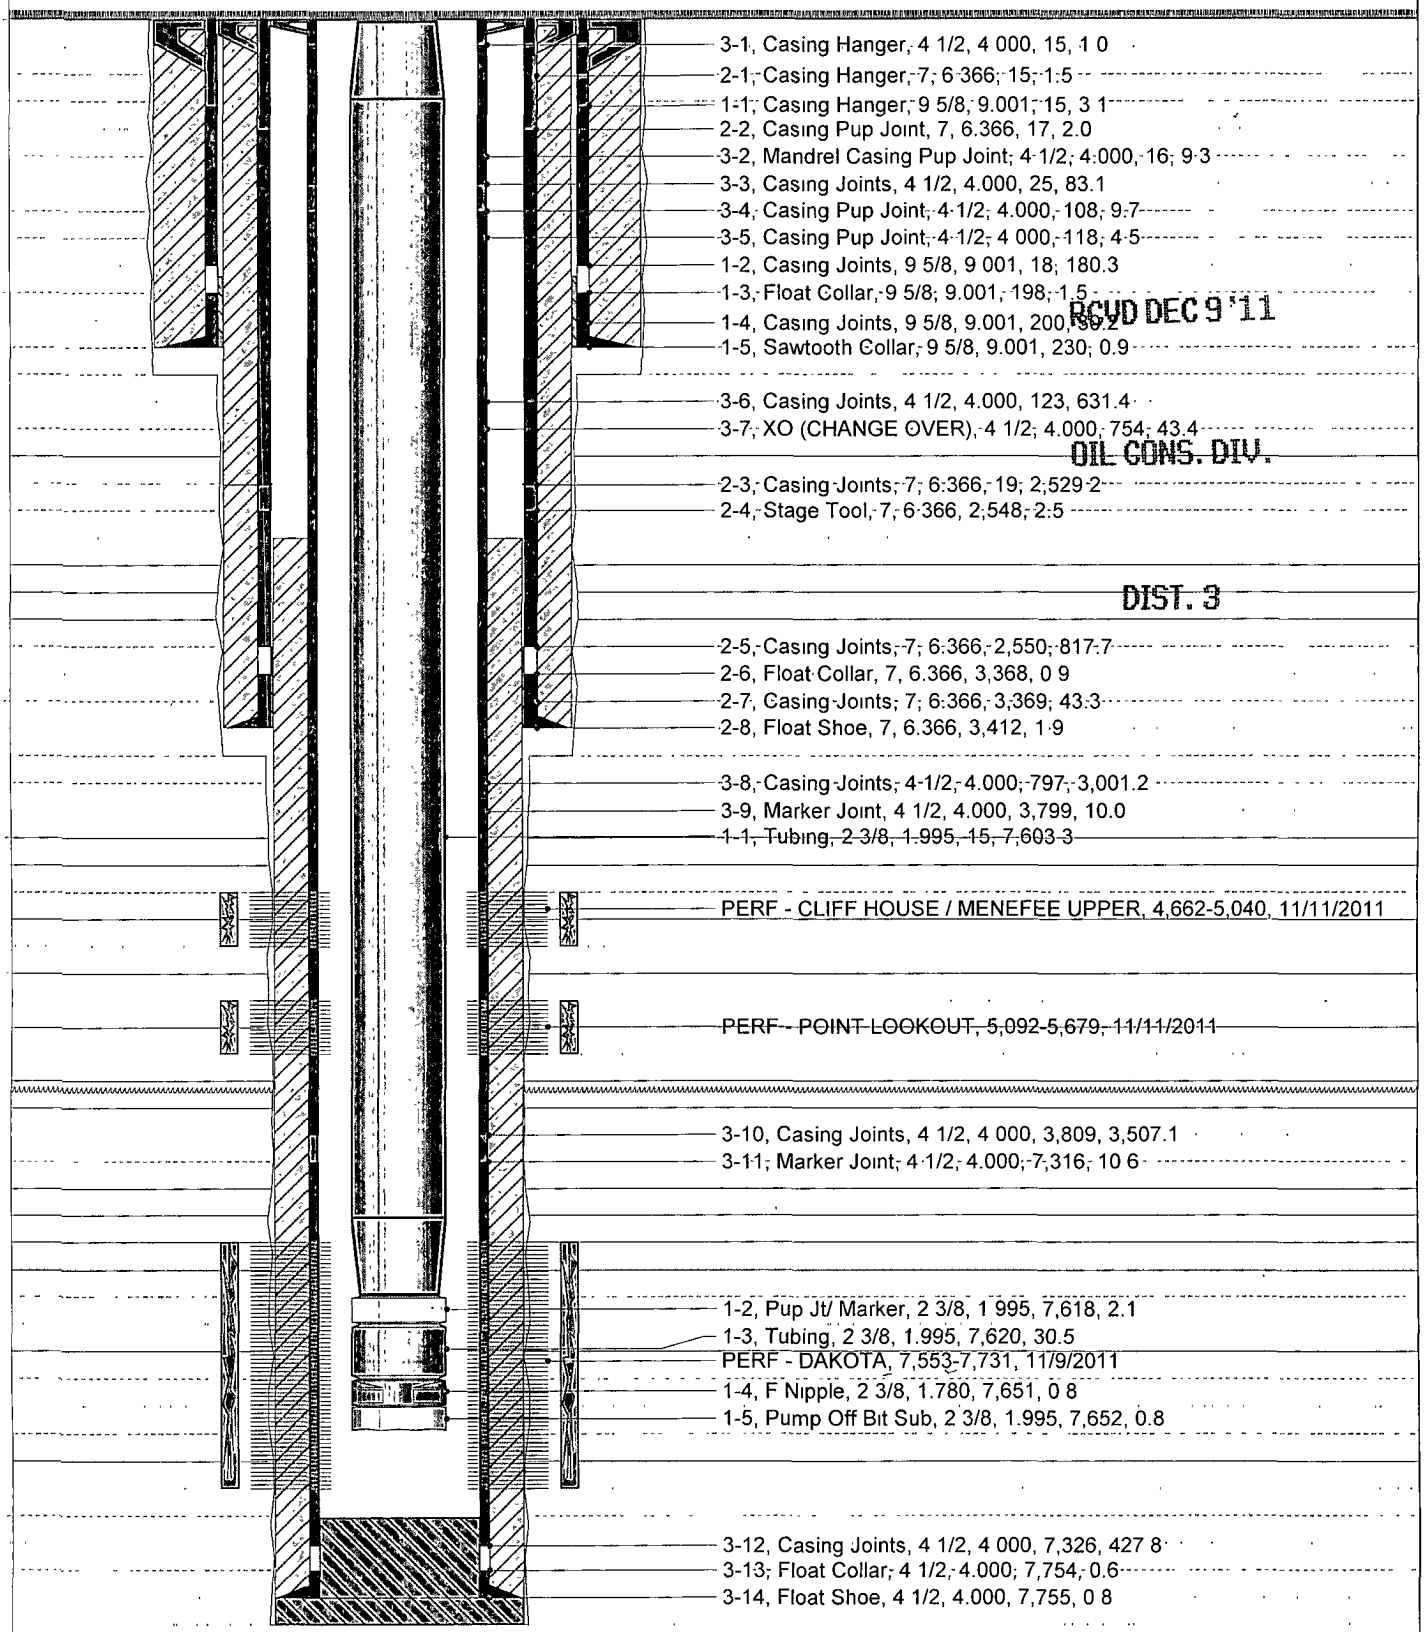

RCVD DEC 9 '11

OIL CONS. DIV.

DIST. 3

Report Printed: 11/29/2011
