PRAXAIR
Making our planet more productive

VISION ENERGY GROUP, LLC.

USG Section 18-54
J-Sec 7, T29N, R16W
San Juan County, New Mexico
API 30-045-279430
License I-89-IND-58

Not to scale **Prepared By: Mark Gehrke**
Date: 3/31/2015

OIL CONS. DIV DIST. 3
MAY 18 2015

ELEVATION
R.B.
G.L. **5,033**
KB
BHT °

Lat:
Long:
FNL ' FWL

Spud date:
Completion date: 7/21/90

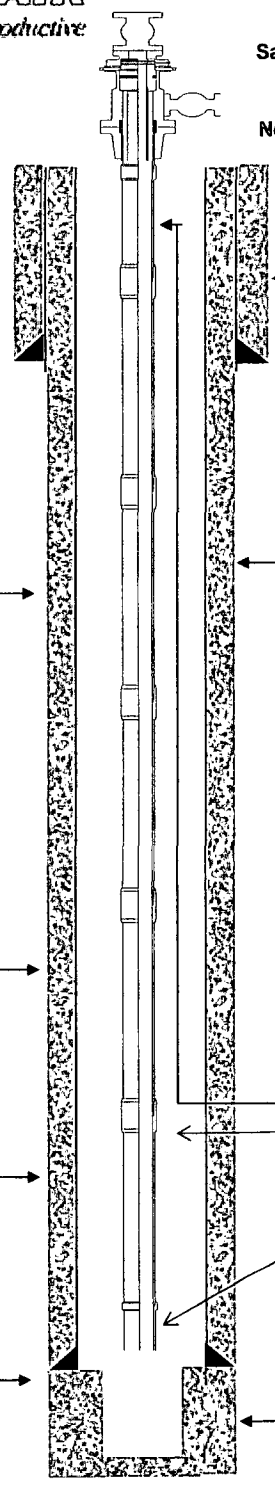

Juana Lope 208'

GREENHORN 601'

GRANEROS 665'

DAKOTA SS. 710'

Geological tops:	
Mancos	surface
Juana Lope	208'
Greenhorn	601'
Granderds	665'
Dakota	710

10 1/4" hole
SURFACE CSG: 7" 23# @ 47'
Cmt w/ 35 sks circulated
Cmt to surface
Top of surface casing 16" below surface

6 1/4" hole
PRODUCTION CSG: 4 1/2" 10.5# @ 706"
Cmt w/ 90 sks circulated
Cmt to surface

3 3/4"
PRODUCTION HOLE: 3 3/4" to 716.5'
Open hole completion

Casing	**4 1/2" 9.5# J55**		**Tubing**	**2 3/8" 4.7# J55**	
	I.D.	4.09		**I.D.**	1.995
	Drift	3.965		**Drift**	1.901
	Burst	4,380		**Burst**	7,700
	BBL/linft	0.0163		**BBL/linft**	0.0039
Annular Vol. w/ tubing		0.0108 bbl/ft		**ft/bbl**	258.642

	Qty	Length	Depth in hole
KB			
Tubbing Pup	1	8.00	8.00
2 3/8" Tubing ~31'	27	685.00	693.00
Seat Nipple	1	1.10	694.10
			694.10
6/13/2014			694.10
			694.10
1 1/2" Rod Insert Pump			694.10
			694.10
			694.10
			694.10
Total	**29**	**694.10**	**694.10**

NOTE: Tagged at 702'
14.5' of fill
