API # 30-039-30665

ConocoPhillips

Schematic - Current

SAN JUAN 30-5 UNIT #111E

Most Recent Job

Jobs

Job Category	Primary Job Type	Secondary Job Type	Actual Start Date	End Date
COMPLETIONS	INITIAL COMPLETION	INITIAL COMPLETION	8/3/2010	

Well Config: VERTICAL - Original Hole, 10/11/2010 8:30:04 AM

Schematic - Actual

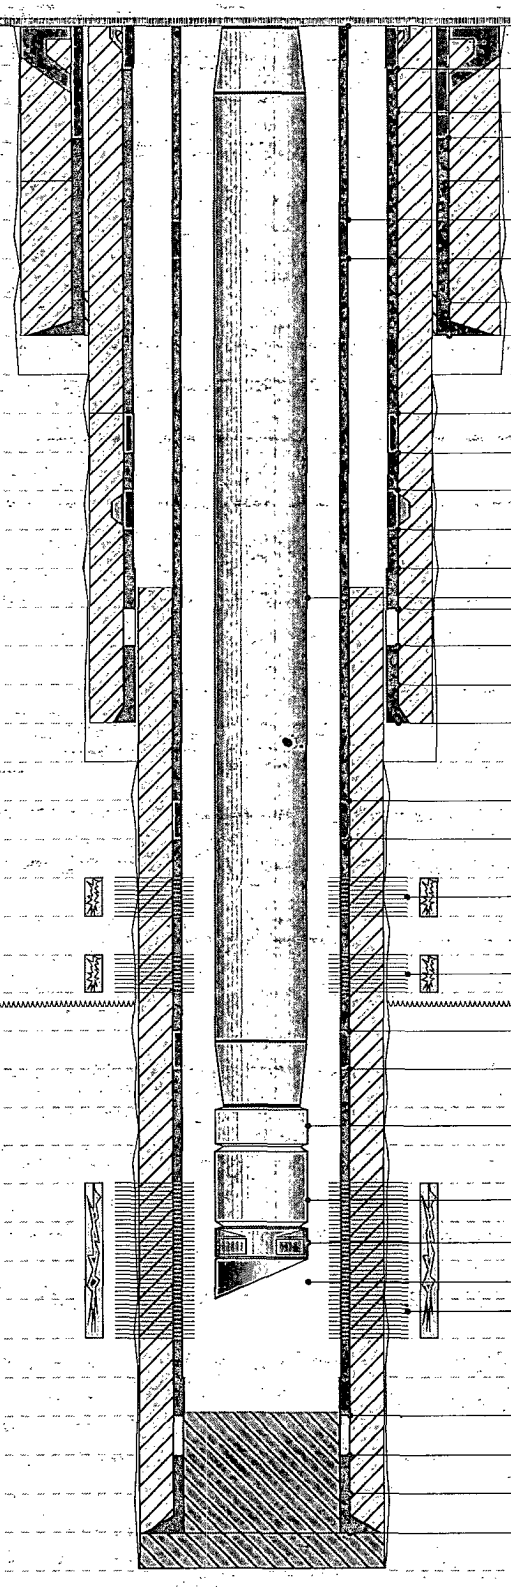

ftKB (MD)	
0	
15	3-2, Casing Pup Joint, 4 1/2, 4.000, 15
16	3-1, Casing Hanger, 4 1/2, 4.000, 15
18	2-1, Casing Hanger, 7, 6.366, 15, 1.5
18	2-2, Casing Pup Joint, 7, 6.456, 17, 1.3
37	1-1, Casing Hanger, 9 5/8, 9.001, 15, 3.3
39	3-3, Casing Joints, 4 1/2, 4.000, 15, 24.0
54	3-4, Casing Pup Joint, 4 1/2, 4.000, 39, 15.0
228	1-2, Casing Joints, 9 5/8, 9.001, 18, 209.9
229	1-3, Sawtooth Collar, 9 5/8, 9.001, 228, 0.8
235	
3,216	2-3, Casing Joints, 7, 6.456, 18, 3,198.3
3,219	2-4, Stage Tool, 7, 6.456, 3,216, 2.5
3,223	2-5, Casing Pup Joint, 7, 6.456, 3,219, 4.1
3,233	2-6, External Casing Packer, 7, 6.456, 3,223, 9.9
3,644	2-7, Casing Joints, 7, 6.456, 3,233, 411.0
4,285	1-1, Tubing, 2 3/8, 1.995, 15, 8,226.6
4,286	2-8, Casing Joints, 7, 6.366, 3,644, 641.9
4,328	2-9, Float Collar, 7, 6.366, 4,285, 0.6
4,329	2-10, Casing Joints, 7, 6.366, 4,286, 42.0
4,339	2-11, Float Shoe, 7, 6.366, 4,328, 1.0
4,726	3-5, Casing Joints, 4 1/2, 4.000, 54, 4,672
4,736	3-6, Marker Joint, 4 1/2, 4.000, 4,726, 10.1
5,542	Perforated, 5,542-5,884, 9/17/2010
5,884	
5,955	Perforated, 5,955-6,299, 9/17/2010
6,299	
7,941	3-7, Casing Joints, 4 1/2, 4.000, 4,736, 3,204.4
7,951	3-8, Marker Joint, 4 1/2, 4.000, 7,941, 10.0
8,242	1-2, Tubing Pup Joint/Marker, 2 3/8, 1.995, 8,242, 1.9
8,243	
8,247	1-3, Tubing, 2 3/8, 1.995, 8,244, 30.5
8,274	1-4, Profile Nipple/F-Nipple, 2 3/8, 1.995, 8,274, 0.8
8,275	1-5, Mule Shoe Guide, 2 3/8, 1.780, 8,275, 0.8
8,276	Perforated, 8,247-8,350, 9/15/2010
8,350	
8,358	
8,366	3-9, Casing Joints, 4 1/2, 4.000, 7,951, 415.3
8,367	3-10, Float Collar, 4 1/2, 4.000, 8,366, 0.8
8,387	3-11, Casing Joints, 4 1/2, 4.000, 8,367, 19.8
8,387	3-12, Float Shoe, 4 1/2, 4.000, 8,387, 0.8
8,389	

RCVD OCT 19 '10
OIL CONS. DIV.
DIST. 3

Report Printed: 10/11/2010
