ConocoPhillips

Schematic - Current

API # 300-39 30494

SAN JUAN 27-4 UNIT #57P

Burlington Resources Oil & Gas Co LP

RCVD AUG 4 '09
OIL CONS. DIV.
DIST. 3

Most Recent Job

Jobs

Job Category	Primary Job Type	Secondary Job Type	Actual Start Date	End Date
COMPLETIONS	INITIAL COMPLETION	INITIAL COMPLETION	5/5/2009	7/23/2009

Well Config: VERTICAL - Original Hole, 7/28/2009 12:13:00 PM

ftKB (MD)	Schematic - Actual
16	2-1, Casing Joints, 7, 6.456, 16
	1-1, Casing Joints, 9 5/8, 9.001, 16
17	3-1, Casing Joints, 4 1/2, 4.000, 16
18	3-2, Casing Hanger, 4 1/2, 4.000, 16, 1.0
	2-2, Casing Hanger, 7, 6.456, 16, 1.6
19	1-2, Well Head, 9 5/8, 9.001, 16, 2.7
25	2-3, Casing Pup Joint, 7, 6.456, 18, 7.6
27	1-3, Casing Pup Joint, 9 5/8, 9.001, 19, 8.0
47	3-3, Casing Pup Joint, 4 1/2, 4.000, 17, 29.4
	1-4, Casing Joints, 9 5/8, 9.001, 27, 171 5
198	1-5, Insert Float Shoe, 9 5/8, 9.001, 198, 0.0
240	1-6, Casing Joints, 9 5/8, 9.001, 198, 41.6
241	1-7, Guide Shoe, 9 5/8, 9 001, 240, 0.9
245	
971	3-4, Casing Joints, 4 1/2, 4.000, 46, 924.6
1,014	3-5, Casing Joints, 4 1/2, 4.052, 971, 42.7
2,420	
3,085	
3,086	2-4, Casing Joints, 7, 6.456, 25, 3,060.4
3,088	2-5, Stage Tool, 7, 6.456, 3,086, 2.5
3,929	2-6, Casing Joints, 7, 6.456, 3,088, 840.8
3,930	2-7, Float Collar, 7, 6.456, 3,929, 1.1
3,972	2-8, Casing Joints, 7, 6.456, 3,930, 42.2
3,973	2-9, Float Shoe, 7, 6.456, 3,972, 0.8
3,988	1-1, Tubing, 2 3/8, 1.995, 16, 8,055.2
4,244	3-6, Casing Joints, 4 1/2, 4.052, 1,014, 3,230.0
4,254	3-7, Marker Joint, 4 1/2, 4.052, 4,244, 9.7
5,335	PERFORATED, 5,335-5,761, 6/1/2009
5,761	
5,826	PERFORATED, 5,826-6,297, 6/1/2009
6,297	
7,778	3-8, Casing Joints, 4 1/2, 4.052, 4,253, 3,524.0
7,787	3-9, Marker Joint, 4 1/2, 4.000, 7,777, 9.9
7,958	PERFORATED, 7,958-8,064, 6/1/2009
8,064	
8,071	1-2, Tubing Pup Joint, 2 3/8, 1.995, 8,071, 1.9
8,073	
8,090	1-3, Tubing, 2 3/8, 1.995, 8,073, 30.7
8,104	1-4, Profile Nipple, 2 3/8, 1.780, 8,104, 0.9
8,105	1-5, Wireline Guide, 2 3/8, 1.995, 8,105, 0.8
8,106	PERFORATED, 8,090-8,171, 6/1/2009
8,171	
8,195	3-10, Casing Joints, 4 1/2, 4.000, 7,787, 407.8
8,195	3-11, Float Collar, 4 1/2, 4.000, 8,195, 0.6
8,196	3-12, Float Shoe, 4 1/2, 4.000, 8,196, 0.8
8,197	
8,200	

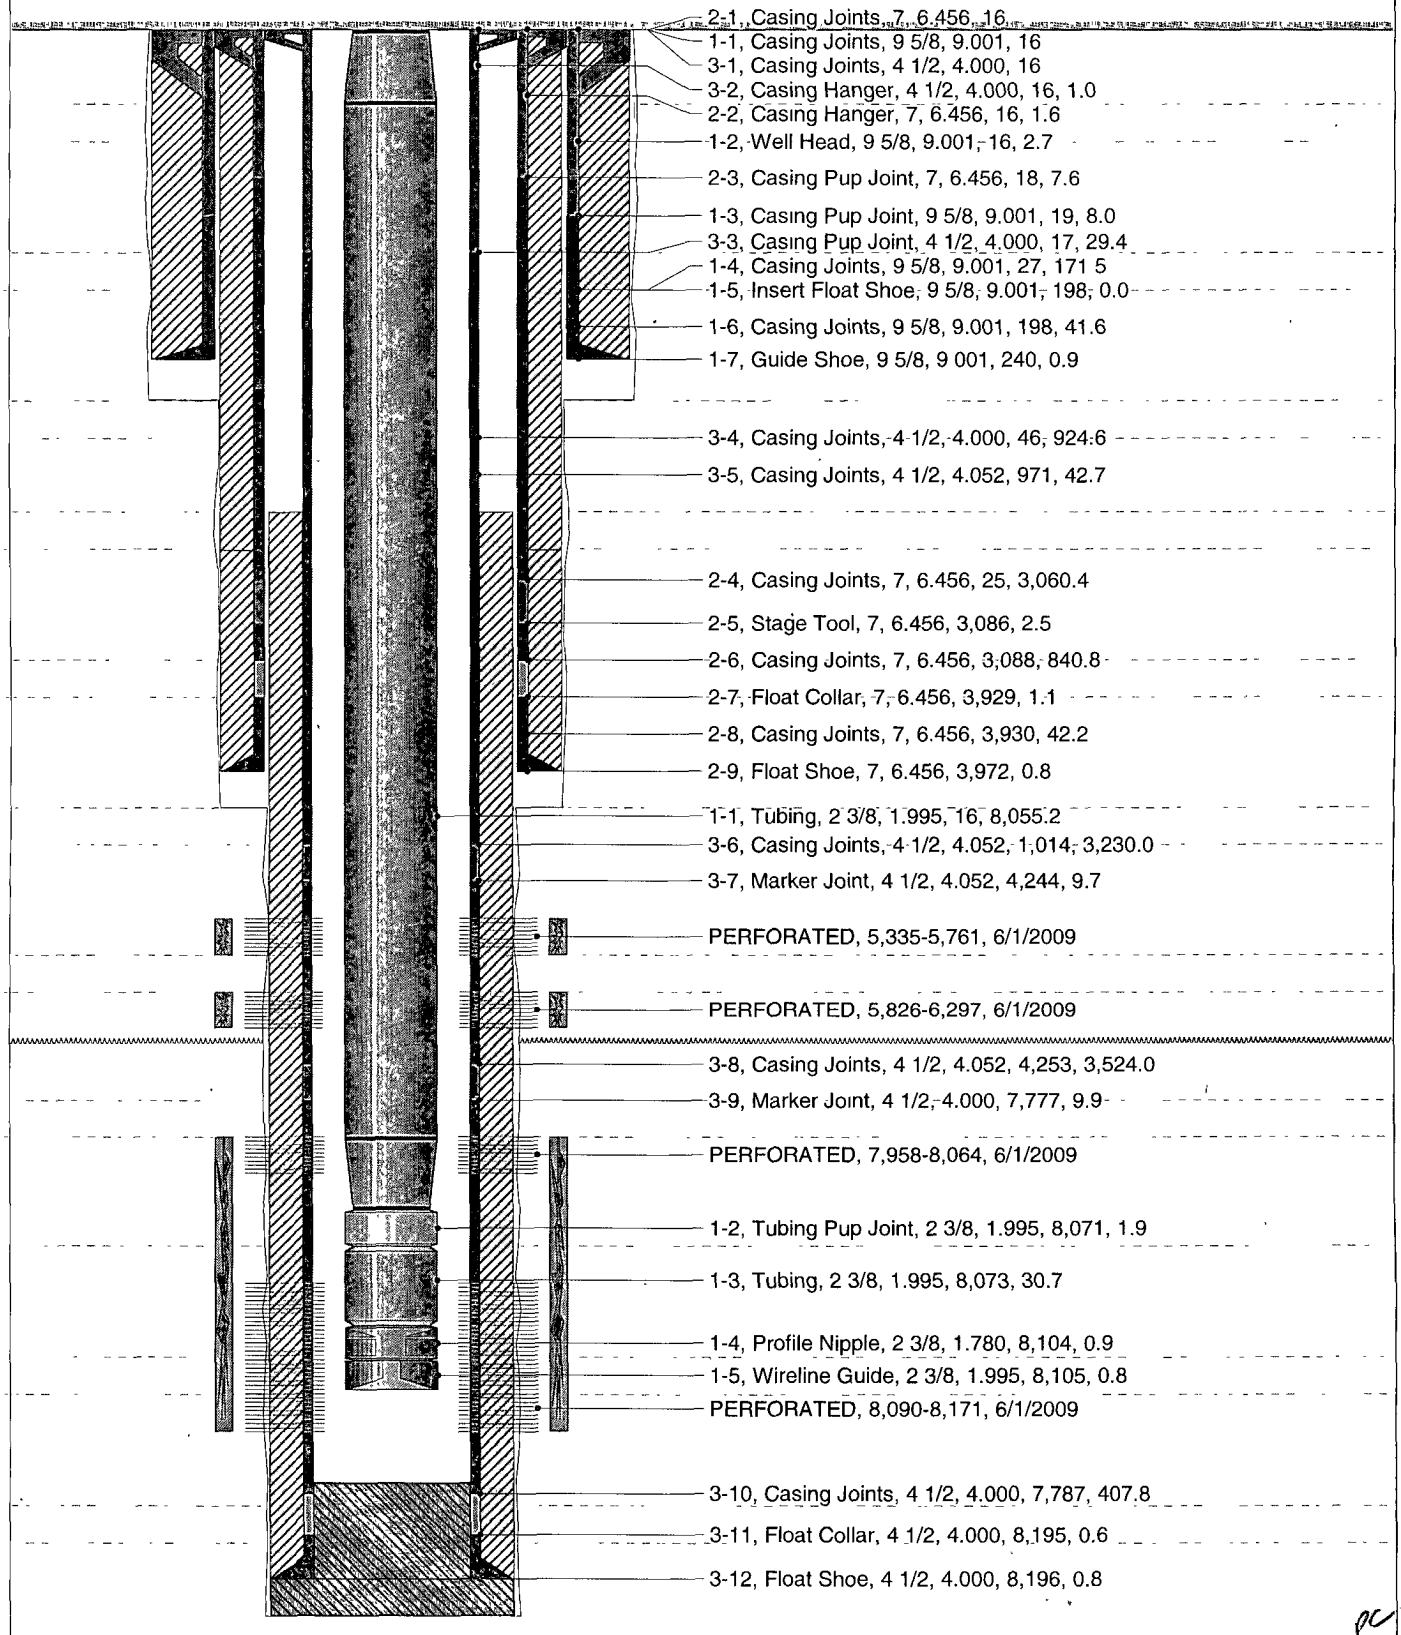

pc

Report Printed: 7/28/2009
