ConocoPhillips

Schematic - Current

Burlington Resources

SAN JUAN 30-6 UNIT #96N

API # 30-039-30836

District	Field Name	API / UWI	County	State/Province
NORTH	MV/DK COM	3003930836	RIO ARRIBA	NEW MEXICO

Original Spud Date	Surface Legal Location	East/West Distance (ft)	East/West Reference	North/South Distance (ft)	North/South Reference
3/3/2010	026-030N-007W-H	153.00	FEL	2,565.00	FNL

Well Config: DEVIATED - Original Hole, 12/10/2010 8:20:52 AM

ftKB (MD)	Schematic - Actual
15	3-2, Casing Pup Joint, 4 1/2, 4.000, 15
	3-1, Casing Pup Joint, 4 1/2, 4.000, 15
16	1-1, Casing Joints, 9 5/8, 9.001, 15
	2-1, Casing Joints, 7, 6.366, 15
16	2-2, Casing Hanger, 7, 6.366, 15, 1.0
	3-3, Casing Hanger, 4 1/2, 4.000, 15, 1.5
18	1-2, Casing Hanger, 9 5/8, 9.001, 15, 3.3
35	
38	3-4, Casing Pup Joint, 4 1/2, 4.000, 17, 21.4
227	1-3, Casing Joints, 9 5/8, 9.001, 18, 208.9
228	1-4, Sawtooth Collar, 9 5/8, 9.001, 227, 0.8
233	
2,904	2-3, Casing Joints, 7, 6.366, 16, 2,887.7
2,906	2-4, Stage Tool, 7, 6.366, 2,904, 2.5
	1-1, Tubing, 2 3/8, 1.995, 15, 7,893.9
4,191	3-5, Casing Joints, 4 1/2, 4.000, 38, 4,152.7
4,201	3-6, Marker Joint, 4 1/2, 4.000, 4,191, 10.1
4,506	Perforated, 4,506-4,822, 11/19/2010
4,718	2-5, Casing Joints, 7, 6.366, 2,906, 1,811.9
4,720	2-6, Float Collar, 7, 6.366, 4,718, 1.5
4,763	2-7, Casing Joints, 7, 6.366, 4,720, 43.3
4,764	2-8, Float Shoe, 7, 6.366, 4,763, 1.5
4,785	
4,822	
5,038	Perforated, 5,038-5,394, 11/19/2010
5,394	
5,452	Perforated, 5,452-5,976, 11/19/2010
5,976	
7,579	3-7, Casing Joints, 4 1/2, 4.000, 4,201, 3,378.6
7,589	3-8, Marker Joint, 4 1/2, 4.000, 7,579, 10.2
7,814	
7,909	Perforated, 7,814-7,990, 11/17/2010
7,911	1-2, Tubing Pup Joint/Marker, 2 3/8, 1.995, 7,909, 2.0
7,941	1-3, Tubing, 2 3/8, 1.995, 7,911, 30.3
7,942	1-4, Profile Nipple/F-Nipple, 2 3/8, 1.780, 7,941, 0.8
7,943	1-5, Mule Shoe Guide, 2 3/8, 1.780, 7,942, 0.9
7,980	
7,990	
8,005	3-9, Casing Joints, 4 1/2, 4.000, 7,589, 415.6
8,006	3-10, Float Collar, 4 1/2, 4.000, 8,005, 0.8
8,006	
8,006	3-11, Float Shoe, 4 1/2, 4.000, 8,006, 0.6
8,007	
8,055	
8,057	

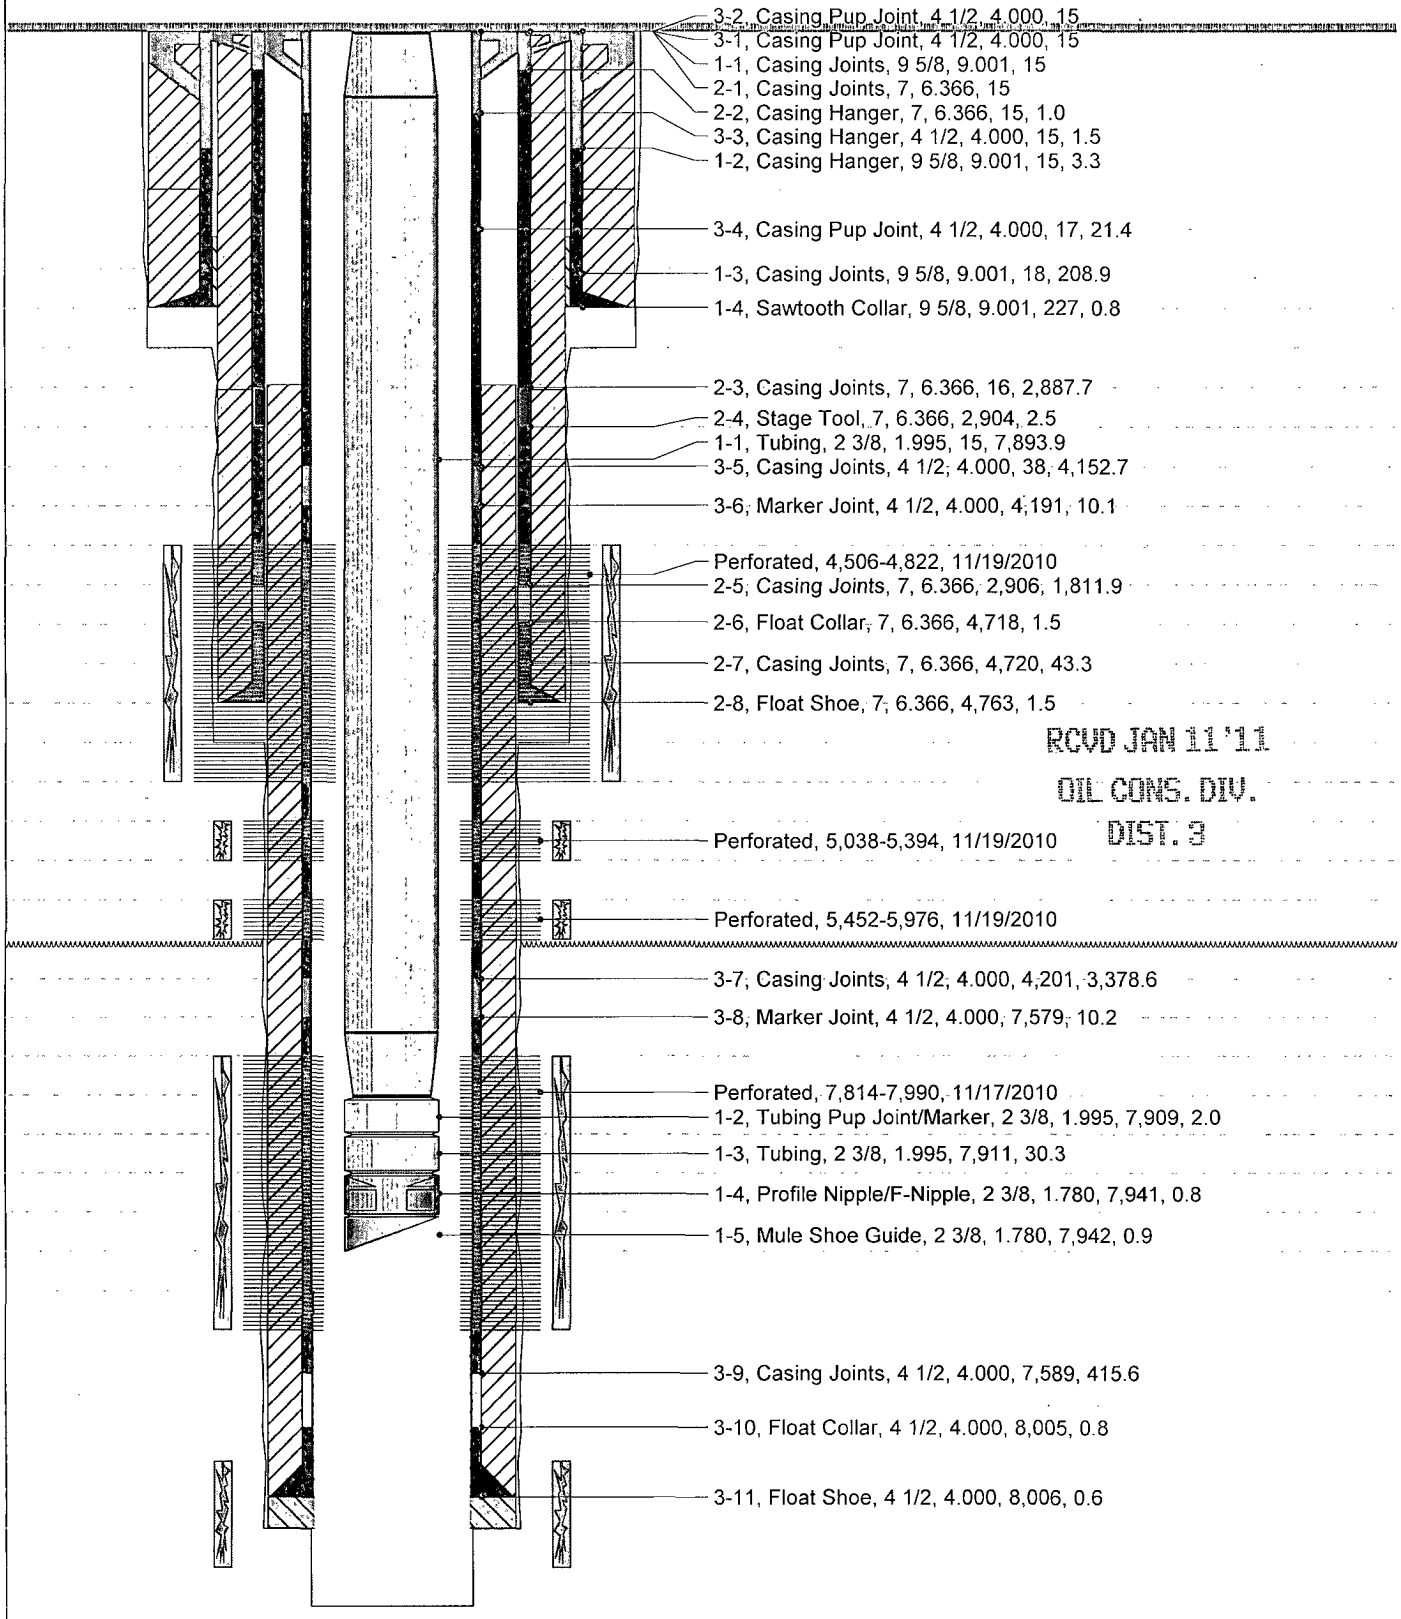

RCVD JAN 11 '11
OIL CONS. DIV.
DIST. 3

Report Printed: 12/10/2010
