CIMAREX

9/9/2009

Well:	**Park State 36 Com #2**	**Permit #:**	
Location:	Sec 36-T24S-R25E	**Field:**	White City/South Carlsbad
County, State	**Eddy, NM**	**Objective:**	Brushy Canyon
Surface Location:	660 FNL 500 FWL	**TVD/MD:**	5030'/8912'
Bottomhole Loc:	330 FSL 375 FWL	**Cementing:**	
E-Mail:		**Mud:**	
Wellhead:	SEC A 11" 3M x 8-5/8" SOW	**Motors:**	
	SEC B 11" 3M X 7-1/16" 5M	**OH Logs**	
		Rig:	880
Xmas Tree		**Offset Wells:**	
Tubing:	2 7/8"		
Superintendent:	**Jim Evans**		
Engineer:	Ryan Braxton		

30-015-37179

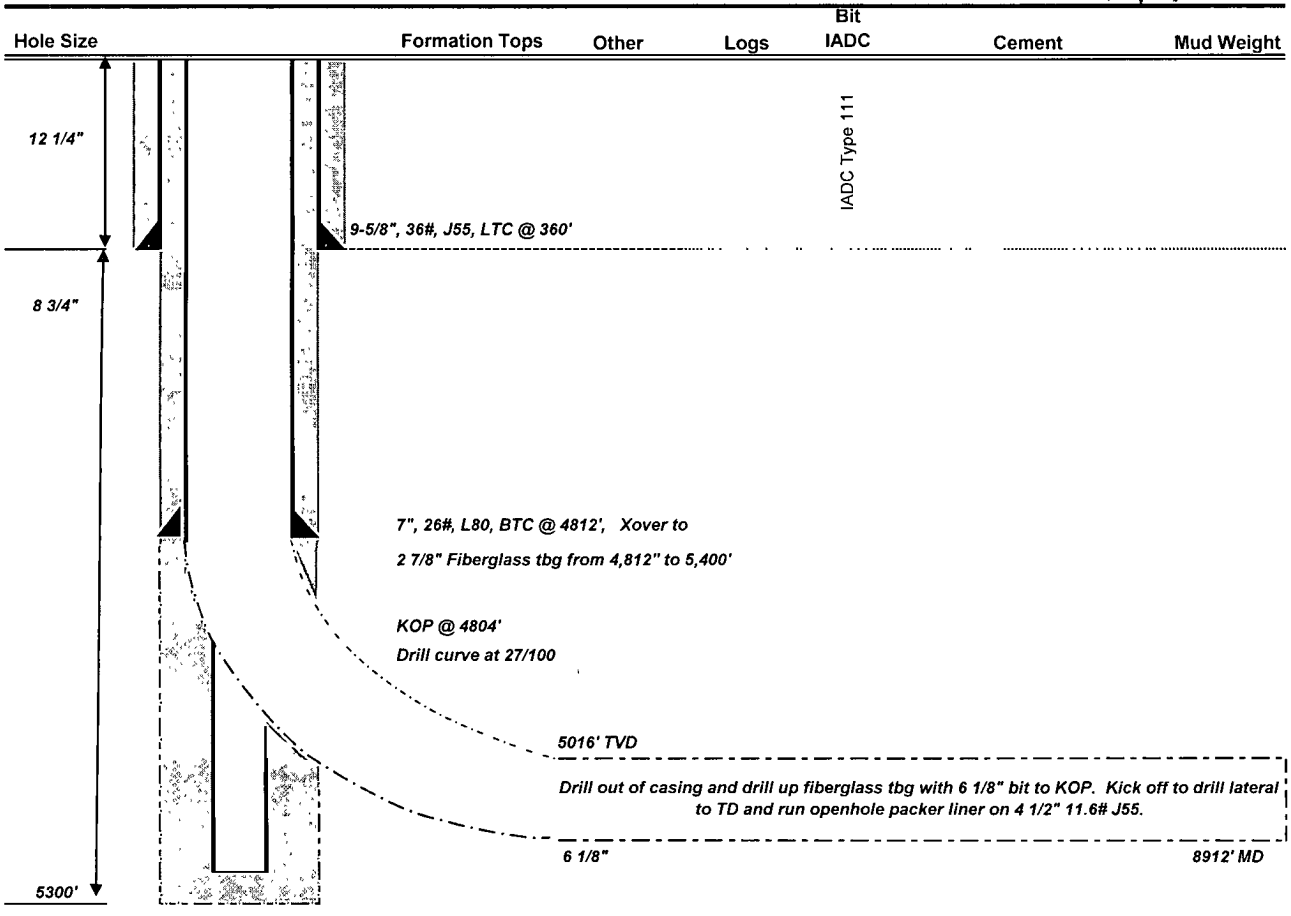

NOTES: Drill to 500'. Run 4812' 7" casing with 2 7/8" fiberglass tubing below to 5400'. Pump cement job to cement fiberglass and casing inplace. With 6 1/8" bit, drill out float collar and drill up fiberglass tubing to KOP. Kickoff and drill lateral to TD. Will run openhole paker liner system on 4 1/2" 11.6# J55 for a 12 stage frac.
