30-025-43074

Wellbore Diagram : NHSAU 668-24

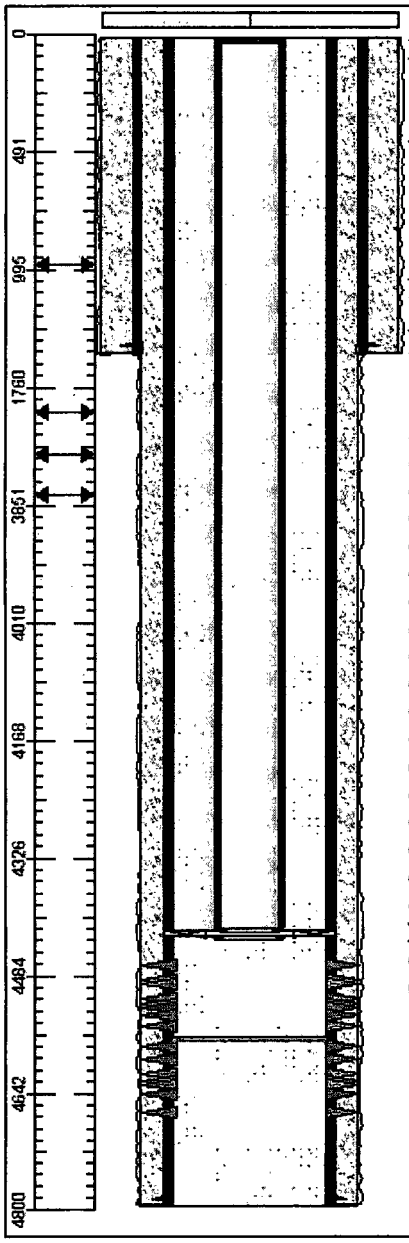

Tubing String Quantity (Top-Bottom Depth) Desc
1 @(4422-4429) Packer Mandrel 7.000" OD Threaded Connection 2.875" x 7" 17-26# Arrowset1-X Dbl Grip Pckr-
Surface Casing (Top-Bottom Depth) Desc
@(1539-1540) Float Shoe/Guide Shoe Nominal - 9.625" OD-10.630" Drillout ID-8.865"-
@(17-1540) Cement (behind Casing)-
@(17-1540) J-55 9.625 OD/ 36.00# Round Short 8.921 ID 8.764 Drift-
Production Casing (Top-Bottom Depth) Desc
@(4422-4429) Packer (Retrievable) (Unknown Type) - 7.000" 2.875" x 7" 17-26# Arrowset1-X Dbl Grip Pckr-
@(4462-4484) Perforations-Open
@(4487-4498) Perforations-Open
@(4507-4509) Perforations-Open
@(4514-4516) Perforations-Open
@(4518-4524) Perforations-Open
@(4528-4540) Perforations-Open
@(4545-4564) Perforations-Open
@(4566-4569) Plug - Cement on Top of Bridge Plug-
@(4569-4573) Bridge Plug Cast Iron 7.000"-
@(4571-4577) Perforations-Open
@(4589-4602) Perforations-Open
@(4607-4614) Perforations-Open
@(4617-4620) Perforations-Open
@(4623-4634) Perforations-Open
@(4636-4655) Perforations-Open
@(4462-4664) Producing Interval (Completion)-
@(4660-4664) Perforations-Open
@(4753-4754) Float Collar Nominal - 7.000" OD- 7.650" Drillout ID- 6.351"-
@(17-4796) Cement (behind Casing)-
@(17-4796) J-55 7.000 OD/ 26.00# Round Short 6.276 ID 6.151 Drift-
@(4795-4796) Casing Shoe (7.000 OD Casing)-
Wellbore Notes (Top-Bottom Depth) Desc
@(4796-4796) Total Depth-
@(4566-4796) Plug Back Total Depth-

HOBBS OCD
JUL 02 2018
RECEIVED
